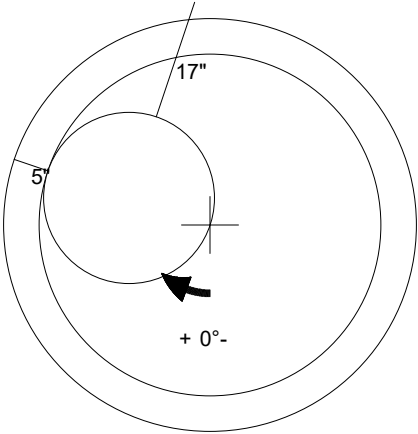



Job Name: 23-2309 - Richland Estates Subdivision		Plant: 100		Tech: J. Horsley		
Job Location: Portland, TN		6/30/2026 8:53:33 AM		PC: T. Lewis		
Contractor: Core & Main LP (BG)						
Structure ID: 03 SS-MH						
P2 MH048CN30X		ECC XYPEX CONE w/ 24" HOLE				
P4) 24" - CASTING HEIGHT - 6" P3) 24" - XYPEX GRADE RING - 3" P2) 48" - ECC XYPEX CONE w/ 24" HOLE - 30" P1) 48" - MH BASE w/XYPEX - 24" 1) JOINT WRAP - 0.065"x12"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) 48" - Conseal CS-231 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 2) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 1981 lb 2911 lb 0 lb 0 lb 1440 lb 0 lb 0 lb 16 lb 0 lb ----- 6551 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = XYPEX C-500 NF RED 4. CASTING BY OTHERS (JBS 1155 F/C SANITARY). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
						
 48" - ECC XYPEX CONE w/ 24" HOLE - 30" - (P2)						
Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 1981 lb Volume (Net): 0.51cu.yd	
