

Job Name: 23-2309 - Richland Estates Subdivision
Job Location: Portland, TN
Contractor: Core & Main LP (BG)

Plant: 100

6/30/2026 8:53:30 AM

Tech: J. Horsley

PC: T. Lewis



Structure ID: 27 ST-JB

P2 MH048LD12ECC

MH FLAT TOP w/ 24" ECC Hole

- P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING - 3"
P2) 48" - MH FLAT TOP w/ 24" ECC Hole - 12"
P1) 48" - MH BASE Custom Ht - 36"
1) 48" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00"
2) Hole - 30
3) MH Step ML-10-TDS-NCR - 10"


Structure Total: 4977 lb

Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING BY OTHERS (JBS 1150 F/C).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB = H20 LOADING.
- RISER (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

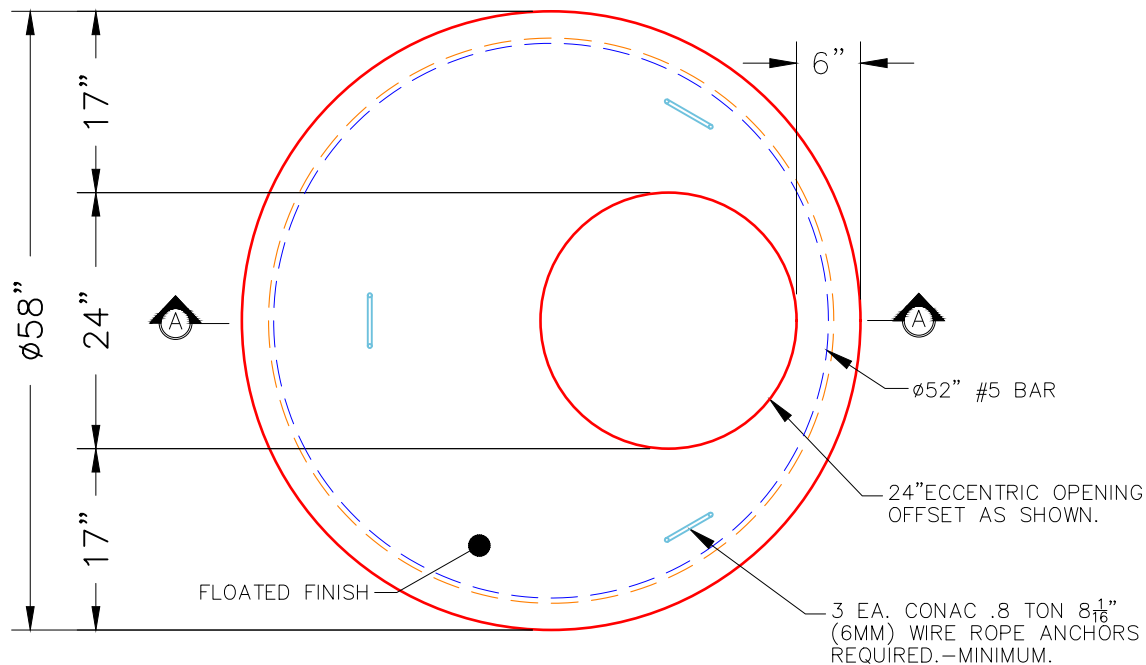

PLAN VIEW

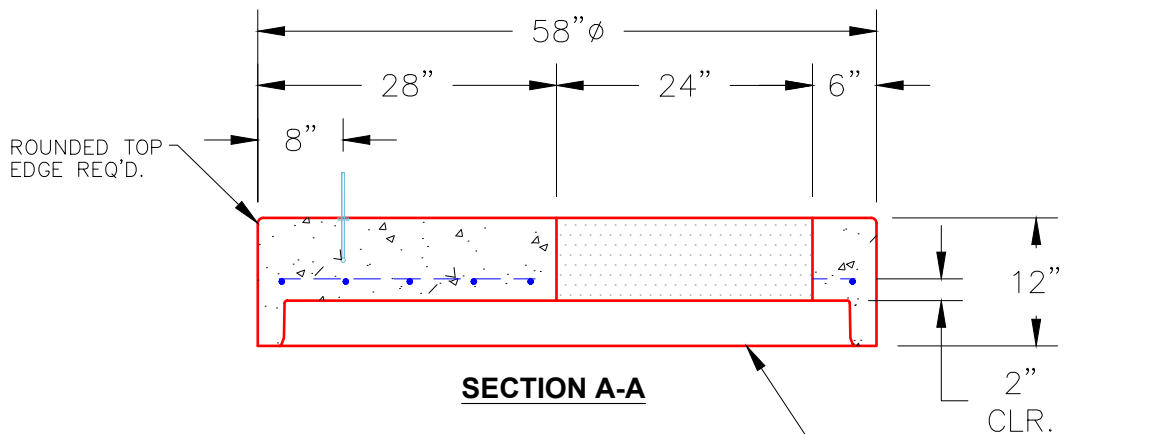

SECTION A-A

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1561 lb
Volume (Net): 0.42cu.yd
