

Job Name: 23-2404 Hampton Hills (Phase 1)
Job Location: Richmond, KY
Contractor: Seven Earthmovers LLC

Plant: 100

5/19/2026 1:02:18 PM

Tech: J. Horsley

PC: C. Golf



Structure ID: CBI-C3

P2 CBITA10-TS-MOD 36x120

CB INLET KY A 10' TOP SAG F/G

- P2) 36" x 120" - CB INLET KY A 10' TOP SAG F/G - 10"
P1) 36" x 120" - BOX BASE 8inW, 8inF, Variable Ht T/n - 50"
1) CASTING - HOE KY-206 F/C (KY CBI A)
1) Hole - 32
2) Hole - 22
1) Horiz Slot n/n - 120"x8"

Structure Total:


4866 lb
14610 lb
206 lb
0 lb
0 lb
0 lb
19682 lb

Structure Notes:


1. PER KYTC CBI A / ASTM C913 SPEC'S.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING (HOE KY-206) TO BE CAST INTO TOP PHASE.

REINFORCING PER ASTM AS615 (GRADE 60).
- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- BASE WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- BASE FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


REINFORCEMENT CUT LIST				
R#	QTY	MATERIAL	CUT LENGTH	SHAPE
A	8	#5 BAR	11'-0"	STR
B	20	#5 BAR	3'-8"	STR
E	2	#5 BAR	11'-0"	STR
H	8	#5 BAR	4'-4"	STR

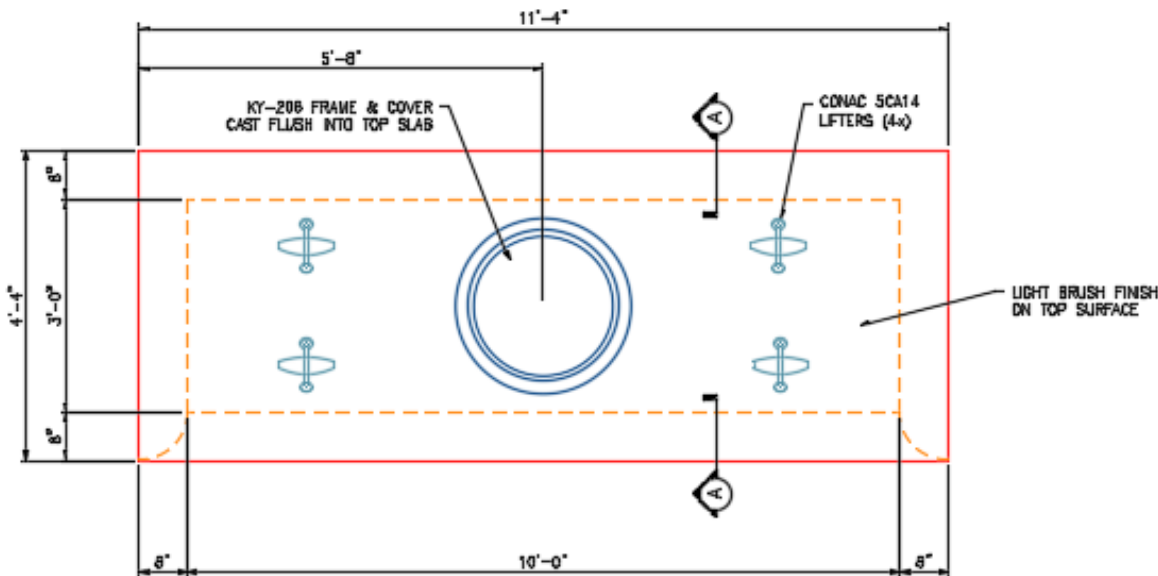

TOP VIEW

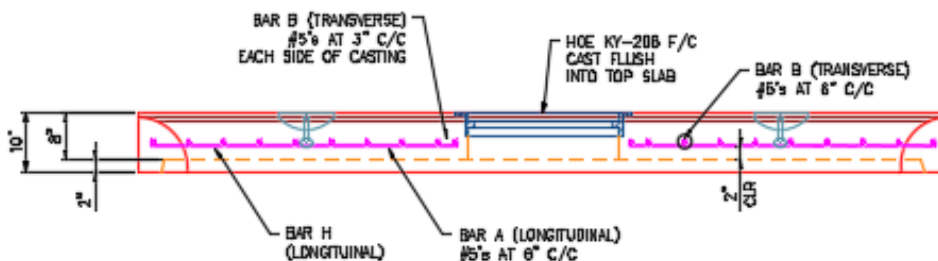

FRONT ELEVATION VIEW

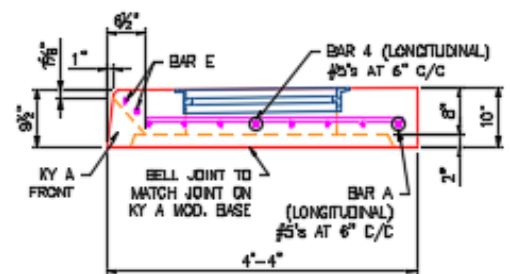

SECTION "A-A"

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 8"

Height (Ext): 10"

Weight (Net): 4866 lb
Volume (Net): 1.24cu.yd
