

Contractor: Seven Earthmovers LLC

TECH: J. Horsley

Plant: 100



Size: 24" x 24"

Rim to Invert: 4'

Floor Height: 8"


Slack: 1"

REINFORCING PER ASTM AS615 (GRADE 60).
 - BASE WALLS (As .31) #5 BARS AT 12" C.C.E.W.
 - BASE FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P2) 24" x 24" - CASTING HEIGHT - 11"
P1) 24" x 24" - BOX BASE 8inW, 8inF F/n - 36"
1) CASTING - HOE KY-206 F/C (KY CBI A)
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 20

0 lb
3924 lb
206 lb
0 lb
0 lb

Structure Total: 4130 lb

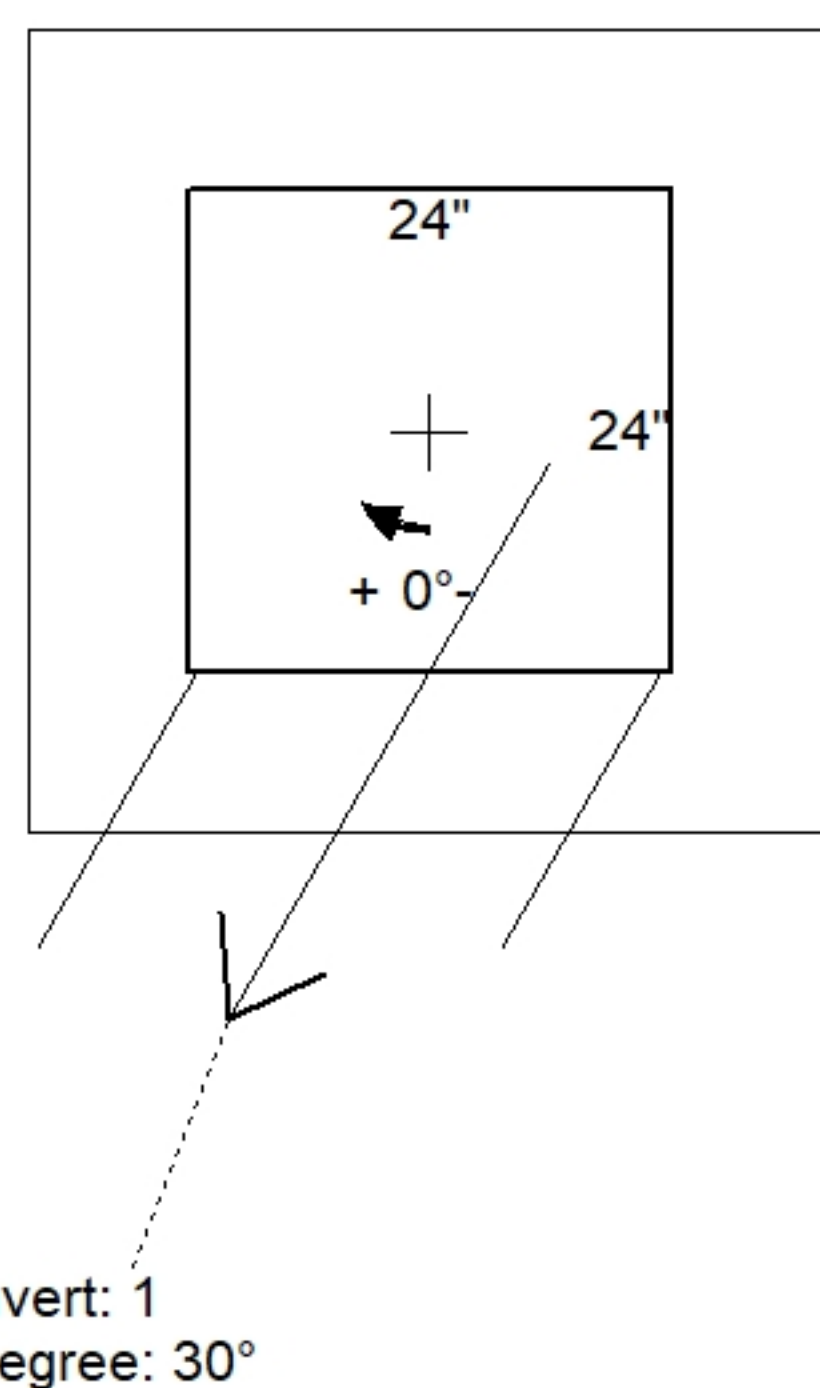


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	907.02'							
Reducer								
Invert 1	903.02'	30°	15" ADS N-12	18"	20"	Hole 20	-2.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 24" - CASTING HEIGHT - 11" - (P2)

24" x 24" - BOX BASE 8inW, 8inF F/n - 36" - (P1)

Cast (Int. Dim.) - Interior Dimensions

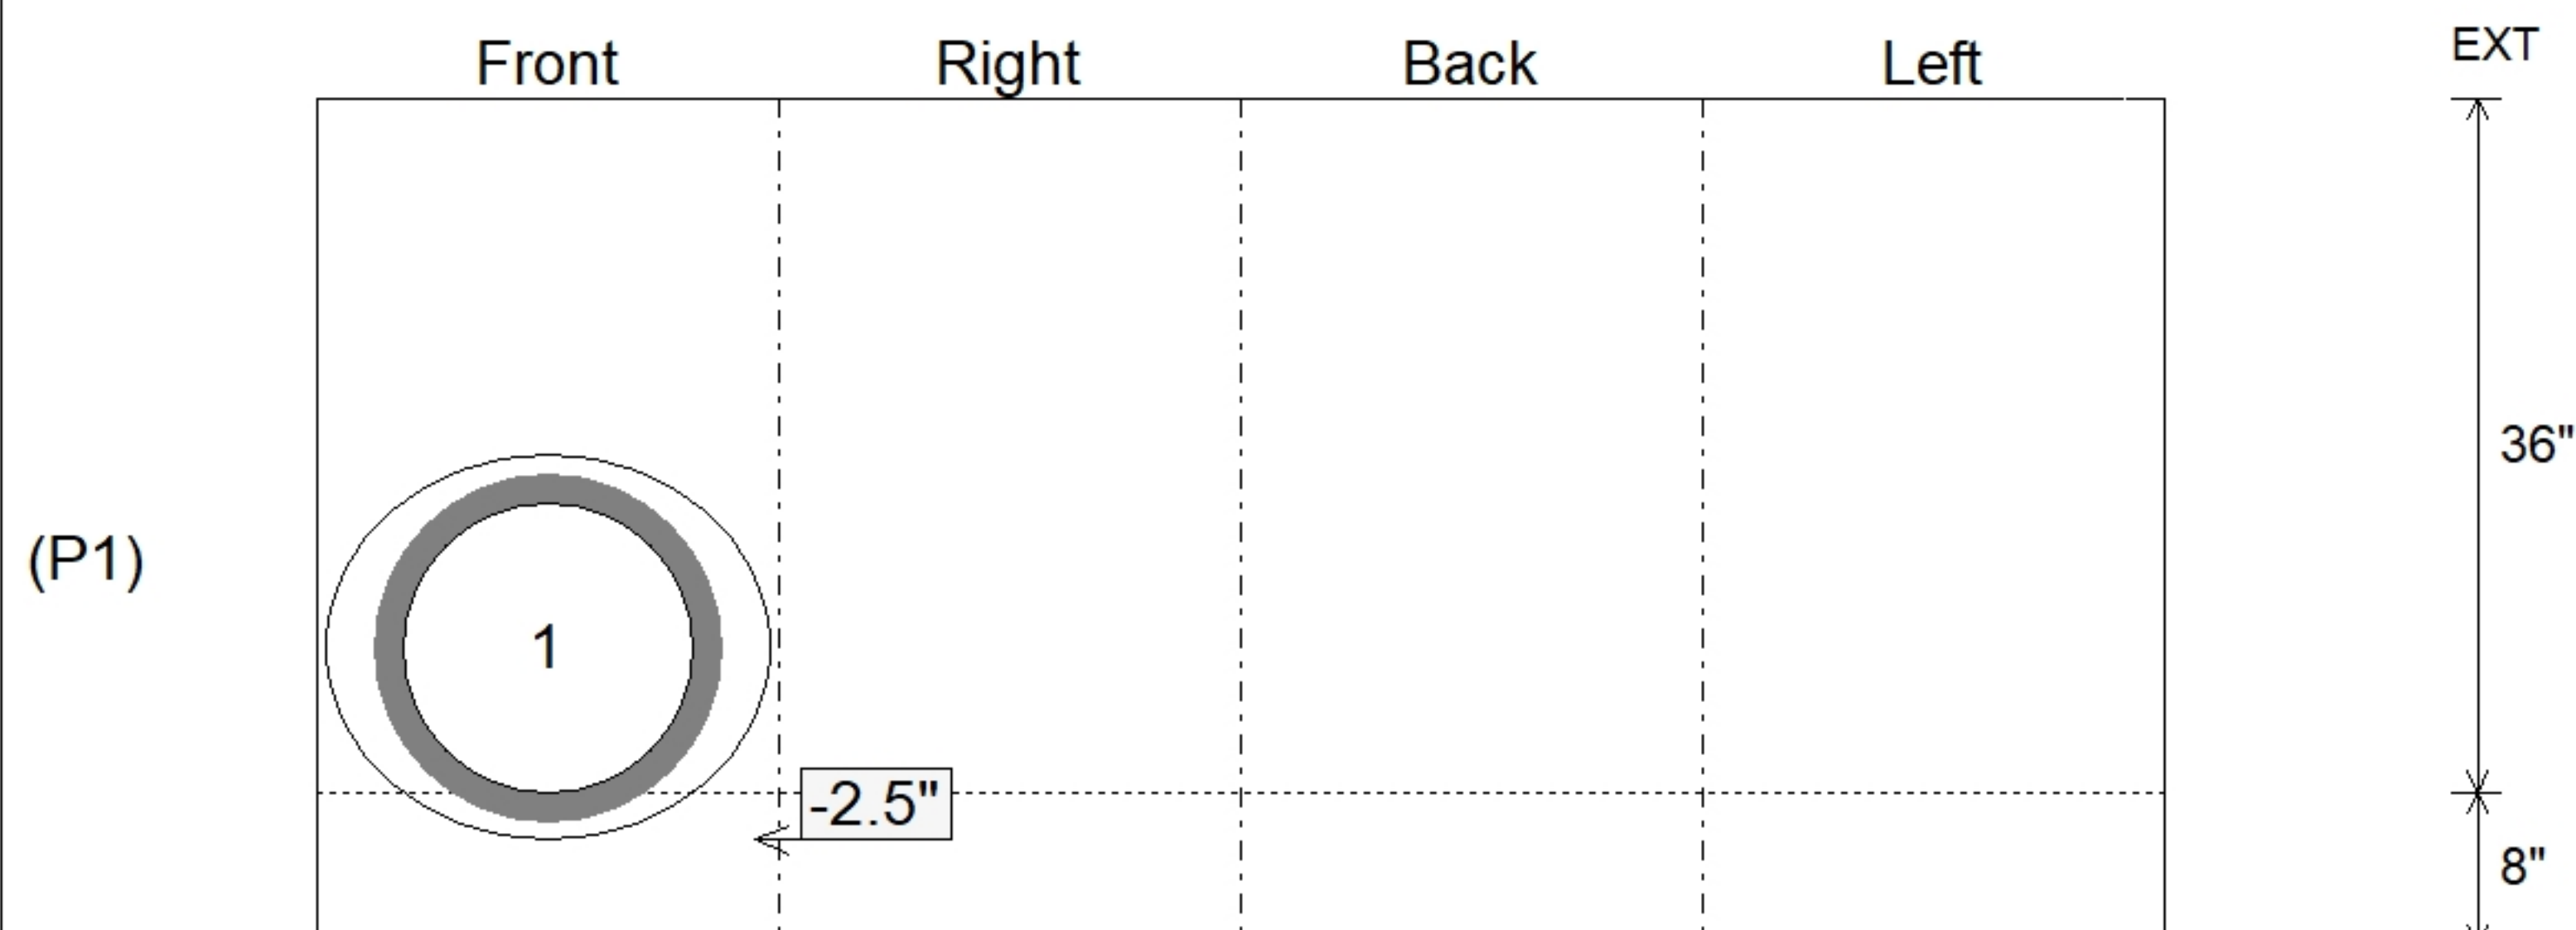

Submittal Drawing
5/19/2026 12:54:51 PM

SUBMITTAL
APPROVED BY:
