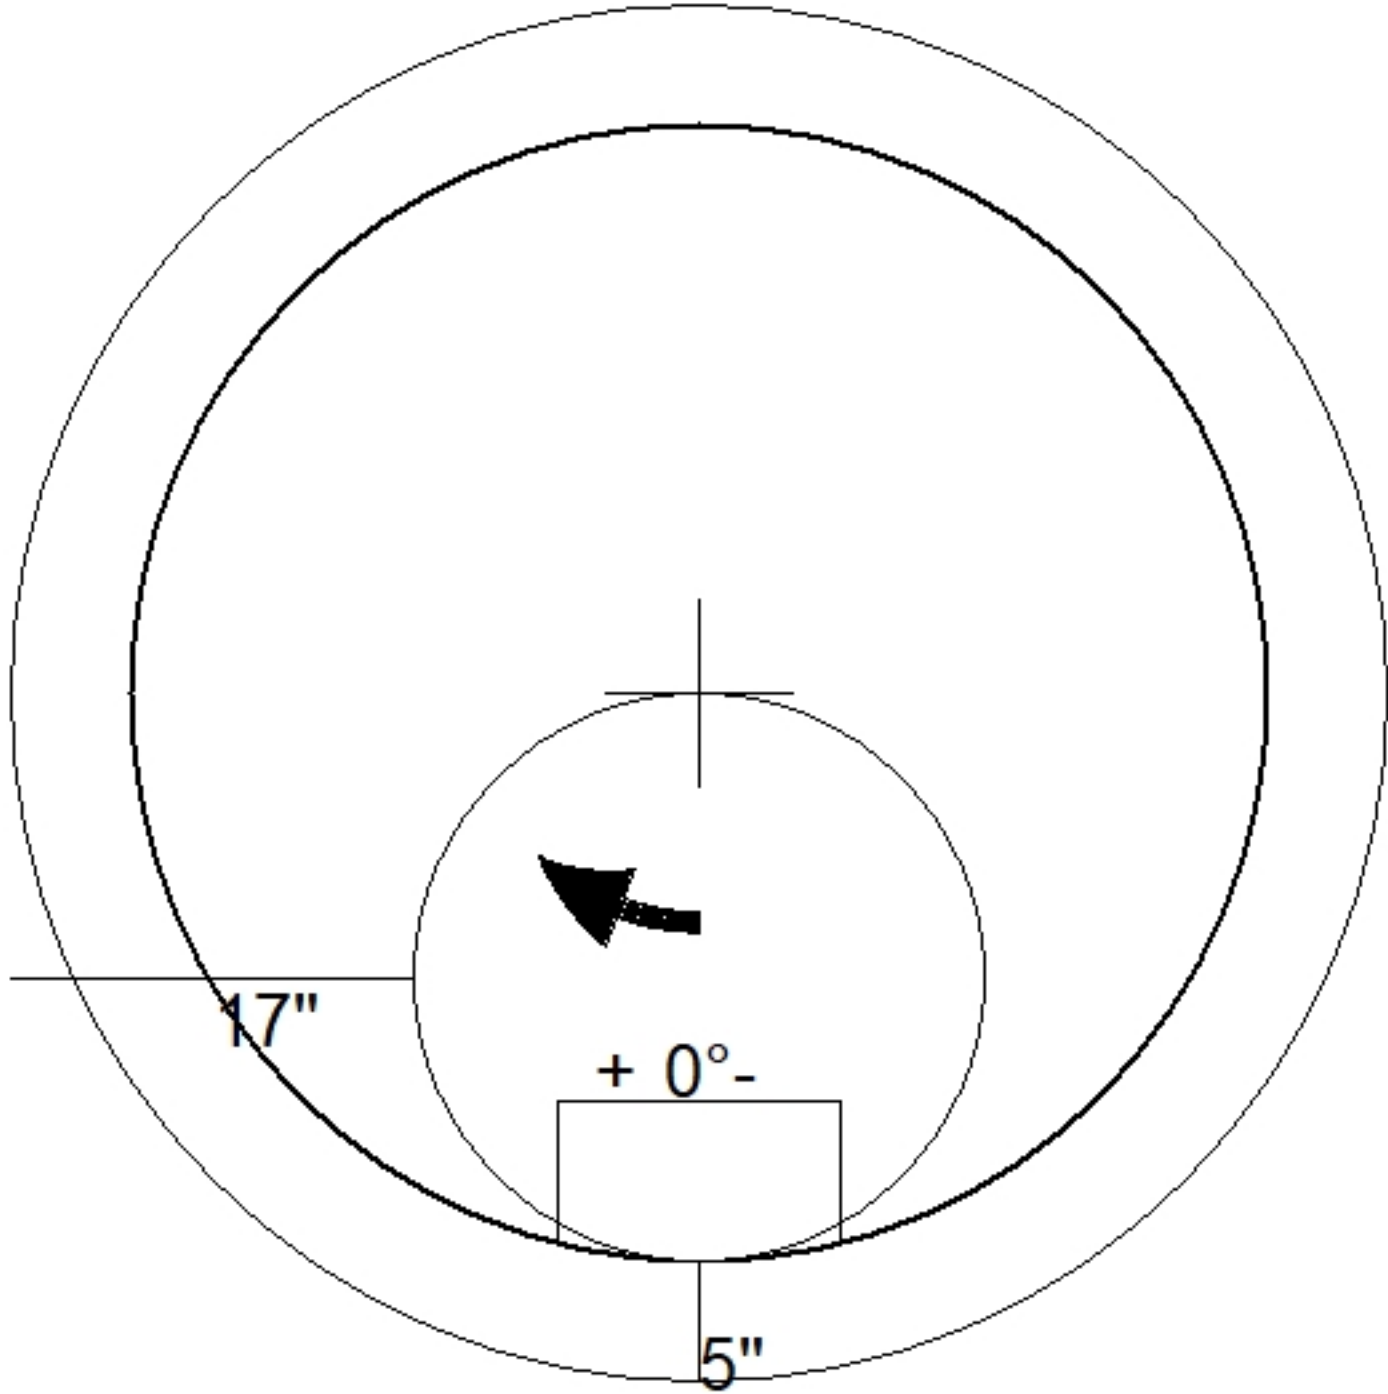
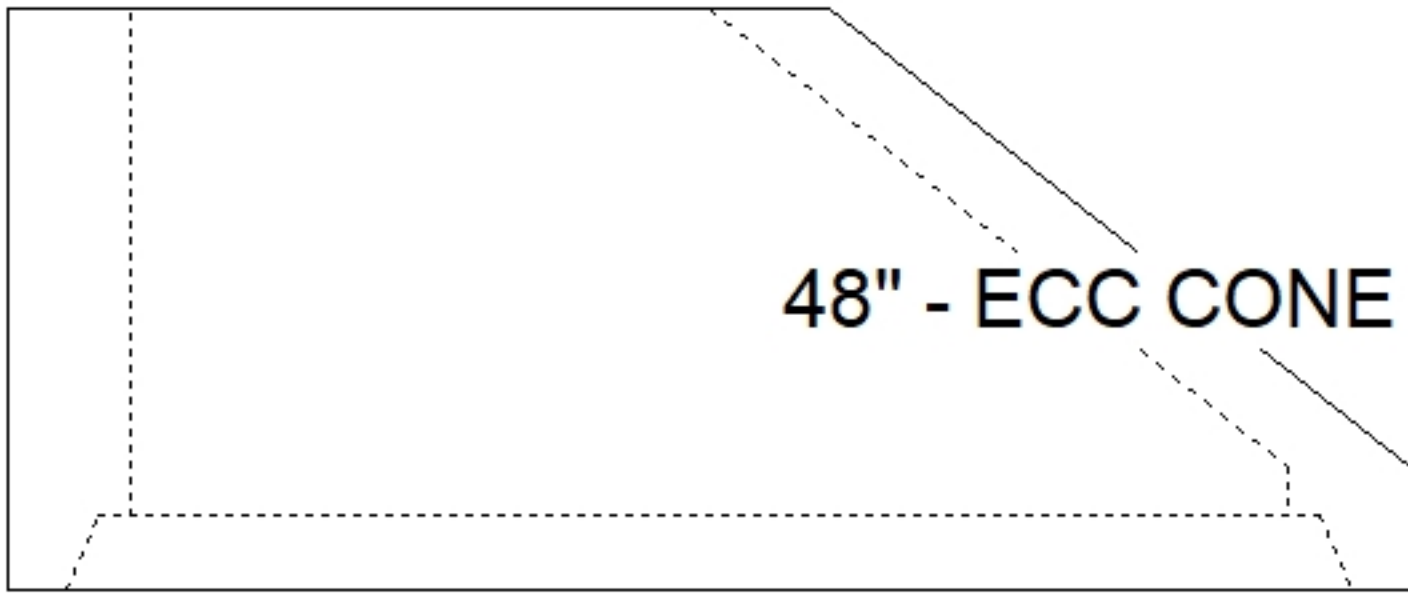


Job Name: 23-2404 Hampton Hills (Phase 1) Job Location: Richmond, KY Contractor: Seven Earthmovers LLC		Plant: 100 5/19/2026 1:02:20 PM	Tech: J. Horsley PC: C. Golf	
Structure ID: SSMH AA-7				
P2 MH048CN24		ECC CONE w/ 24" HOLE F/G		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 24" P1) 48" - MH BASE Custom Ht T/n - 25" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-350 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 3) MH Step ML-10-TDS-NCR - 10"		0 lb 1550 lb 2981 lb 1440 lb 0 lb 0 lb 305 lb 0 lb 16 lb 0 lb ----- 6292 lb Structure Total:	<u>Structure Notes:</u> 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-350 F/C) SHIPPED LOOSE. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
 48" - ECC CONE w/ 24" HOLE F/G - 24" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1550 lb Volume (Net): 0.33cu.yd
