

Contractor: Seven Earthmovers LLC

TECH: J. Horsley

Plant: 100



Size: 48"

Rim to Invert: 14.02'

Floor Height: 6"


Slack: 0.24"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


14) MH Step ML-10-TDS-NCR - 10"

0 lb

Structure Total: 15935 lb

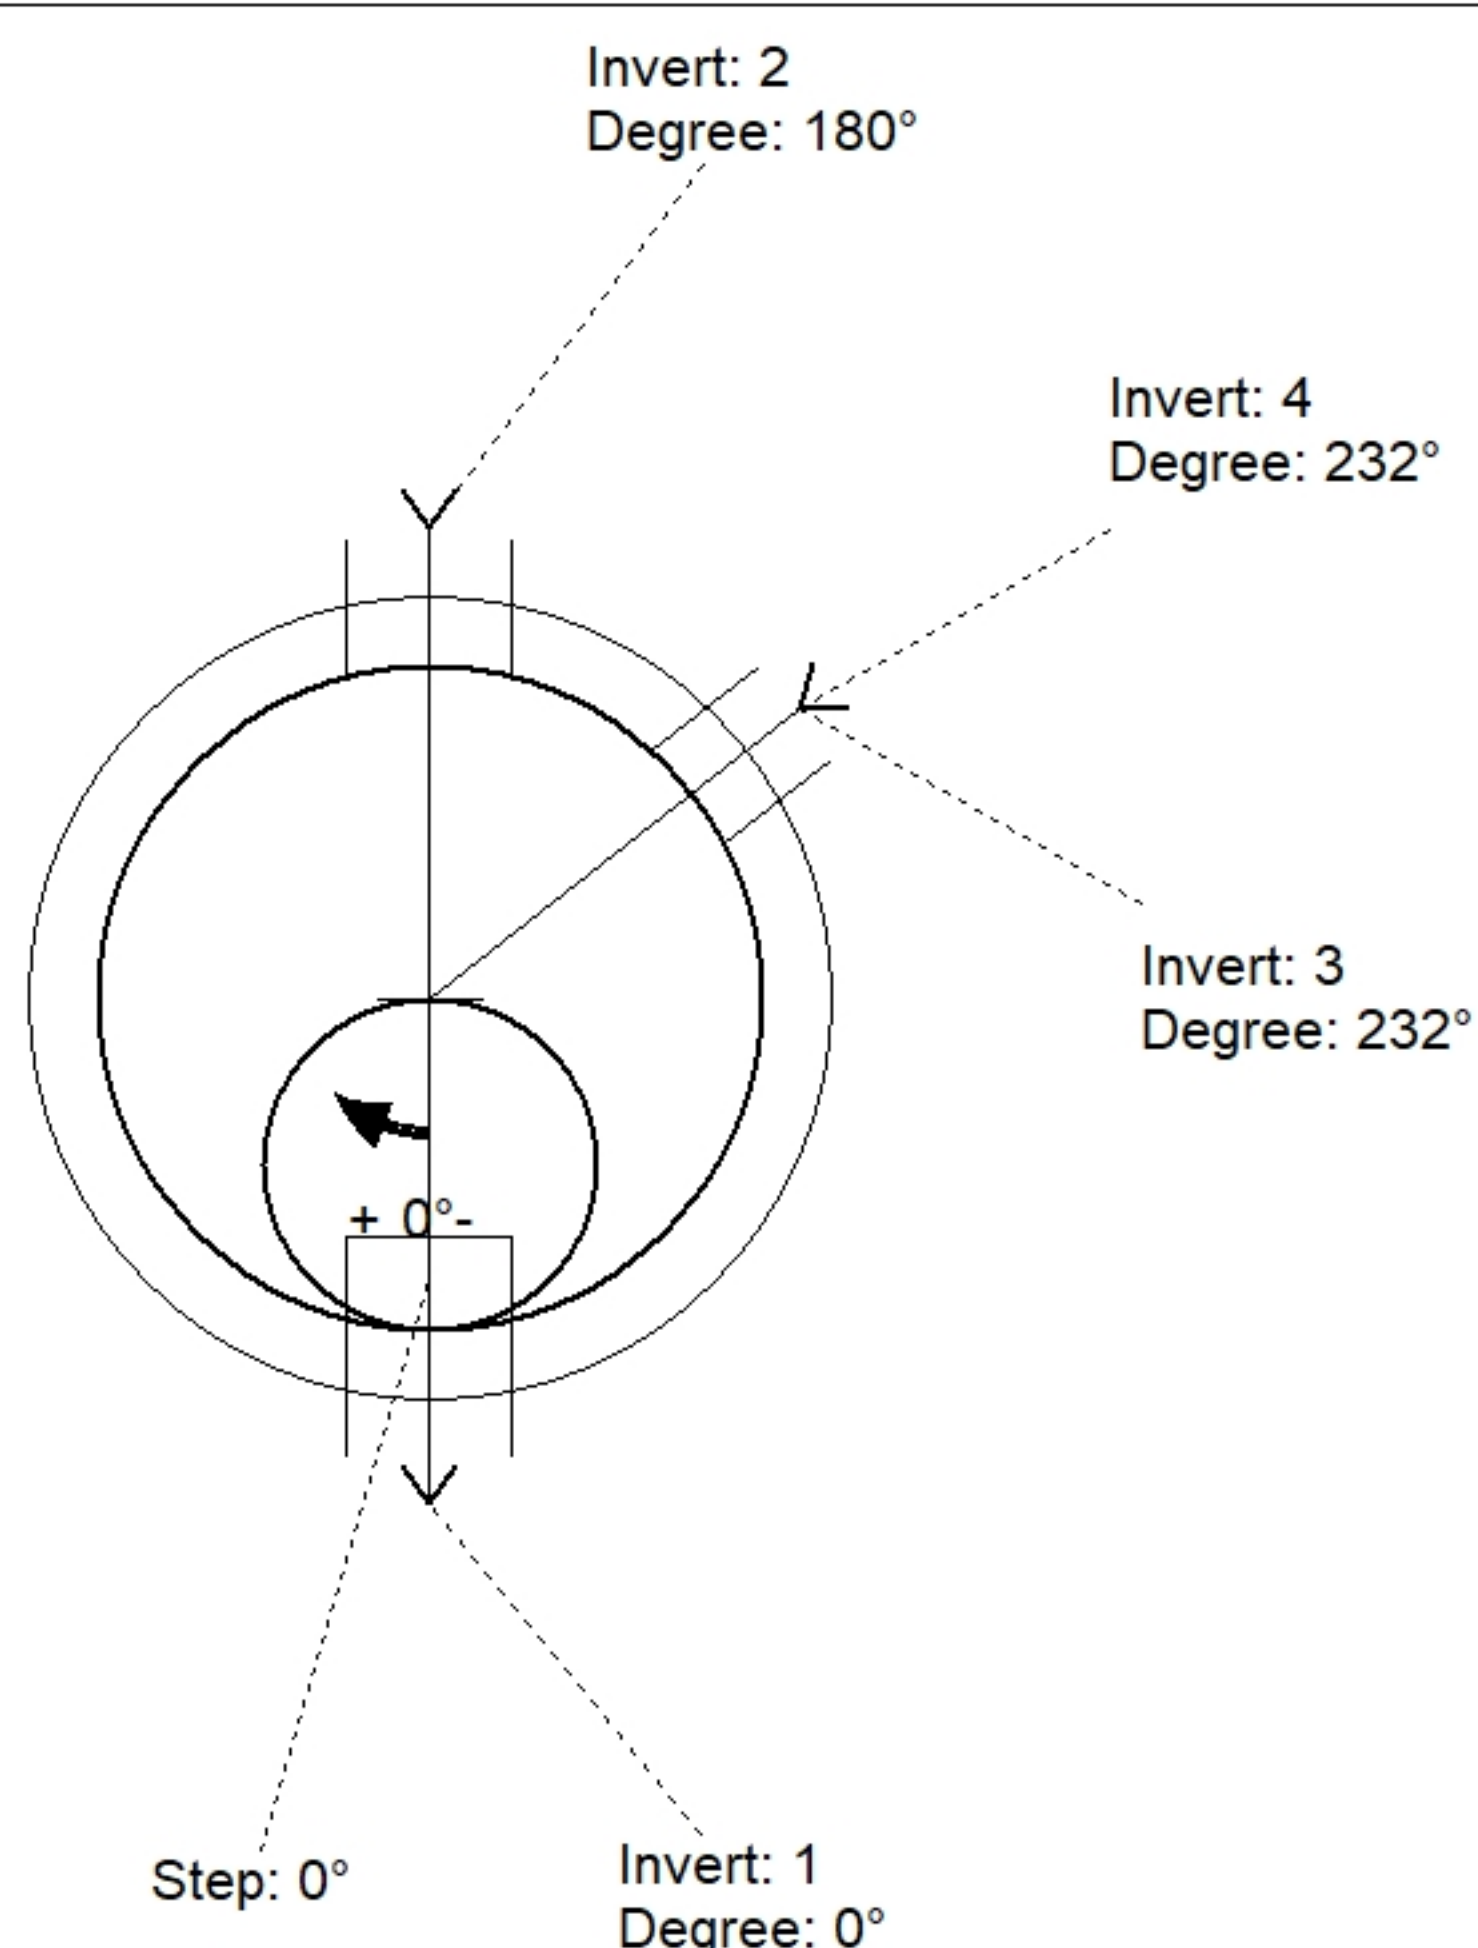

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	858'							
Reducer								
Invert 1	843.98'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	844.08'	180°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	1.25"	P1
Invert 3	852'	232°	8" PVC SDR35	8.5"	8.5"	Drop Tee 8" PVC	20.75"	P3
Invert 4	844.08'	232°	8" PVC SDR35	8.5"	8.5"	Drop Elbow 8" PVC	3"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

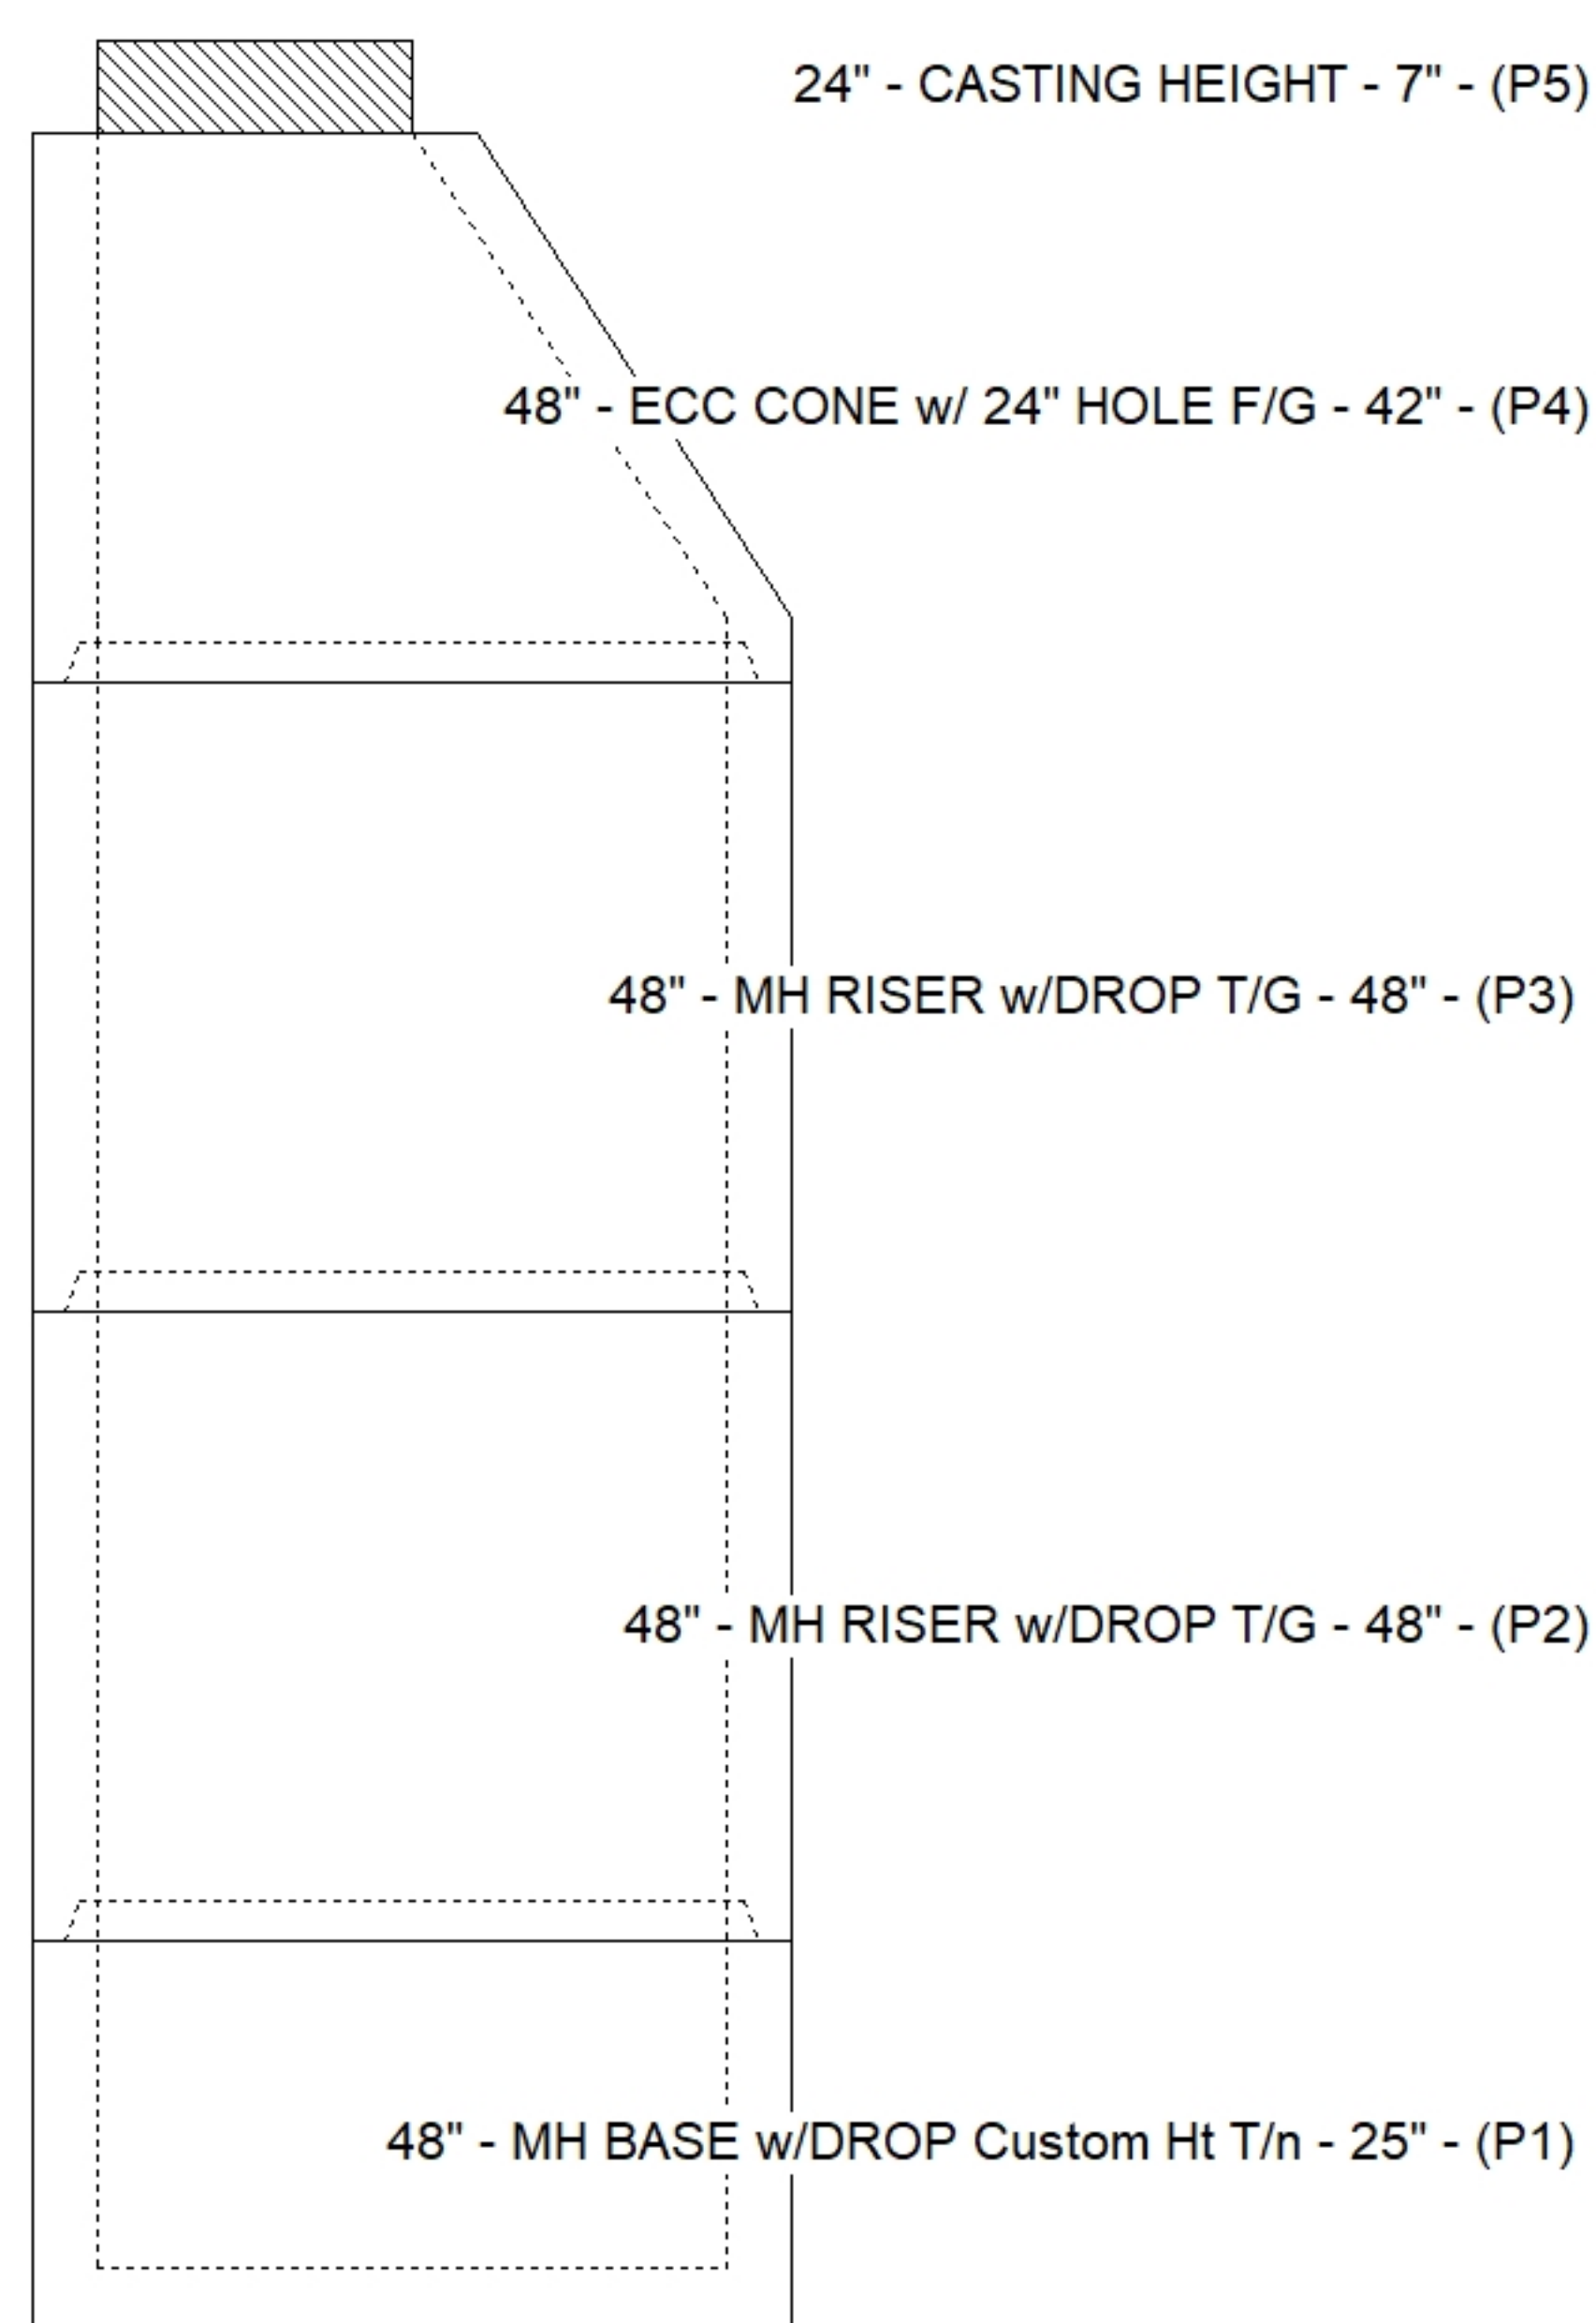

5/19/2026 12:54:57 PM

APPROVED BY:
