

Contractor: Seven Earthmovers LLC

TECH: J. Horsley

Plant: 100



Size: 48"

Rim to Invert: 4.5'

Floor Height: 6"


Slack: 0"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

4) MH Step ML-10-TDS-NCR - 10"



0 lb

Structure Total: 6335 lb

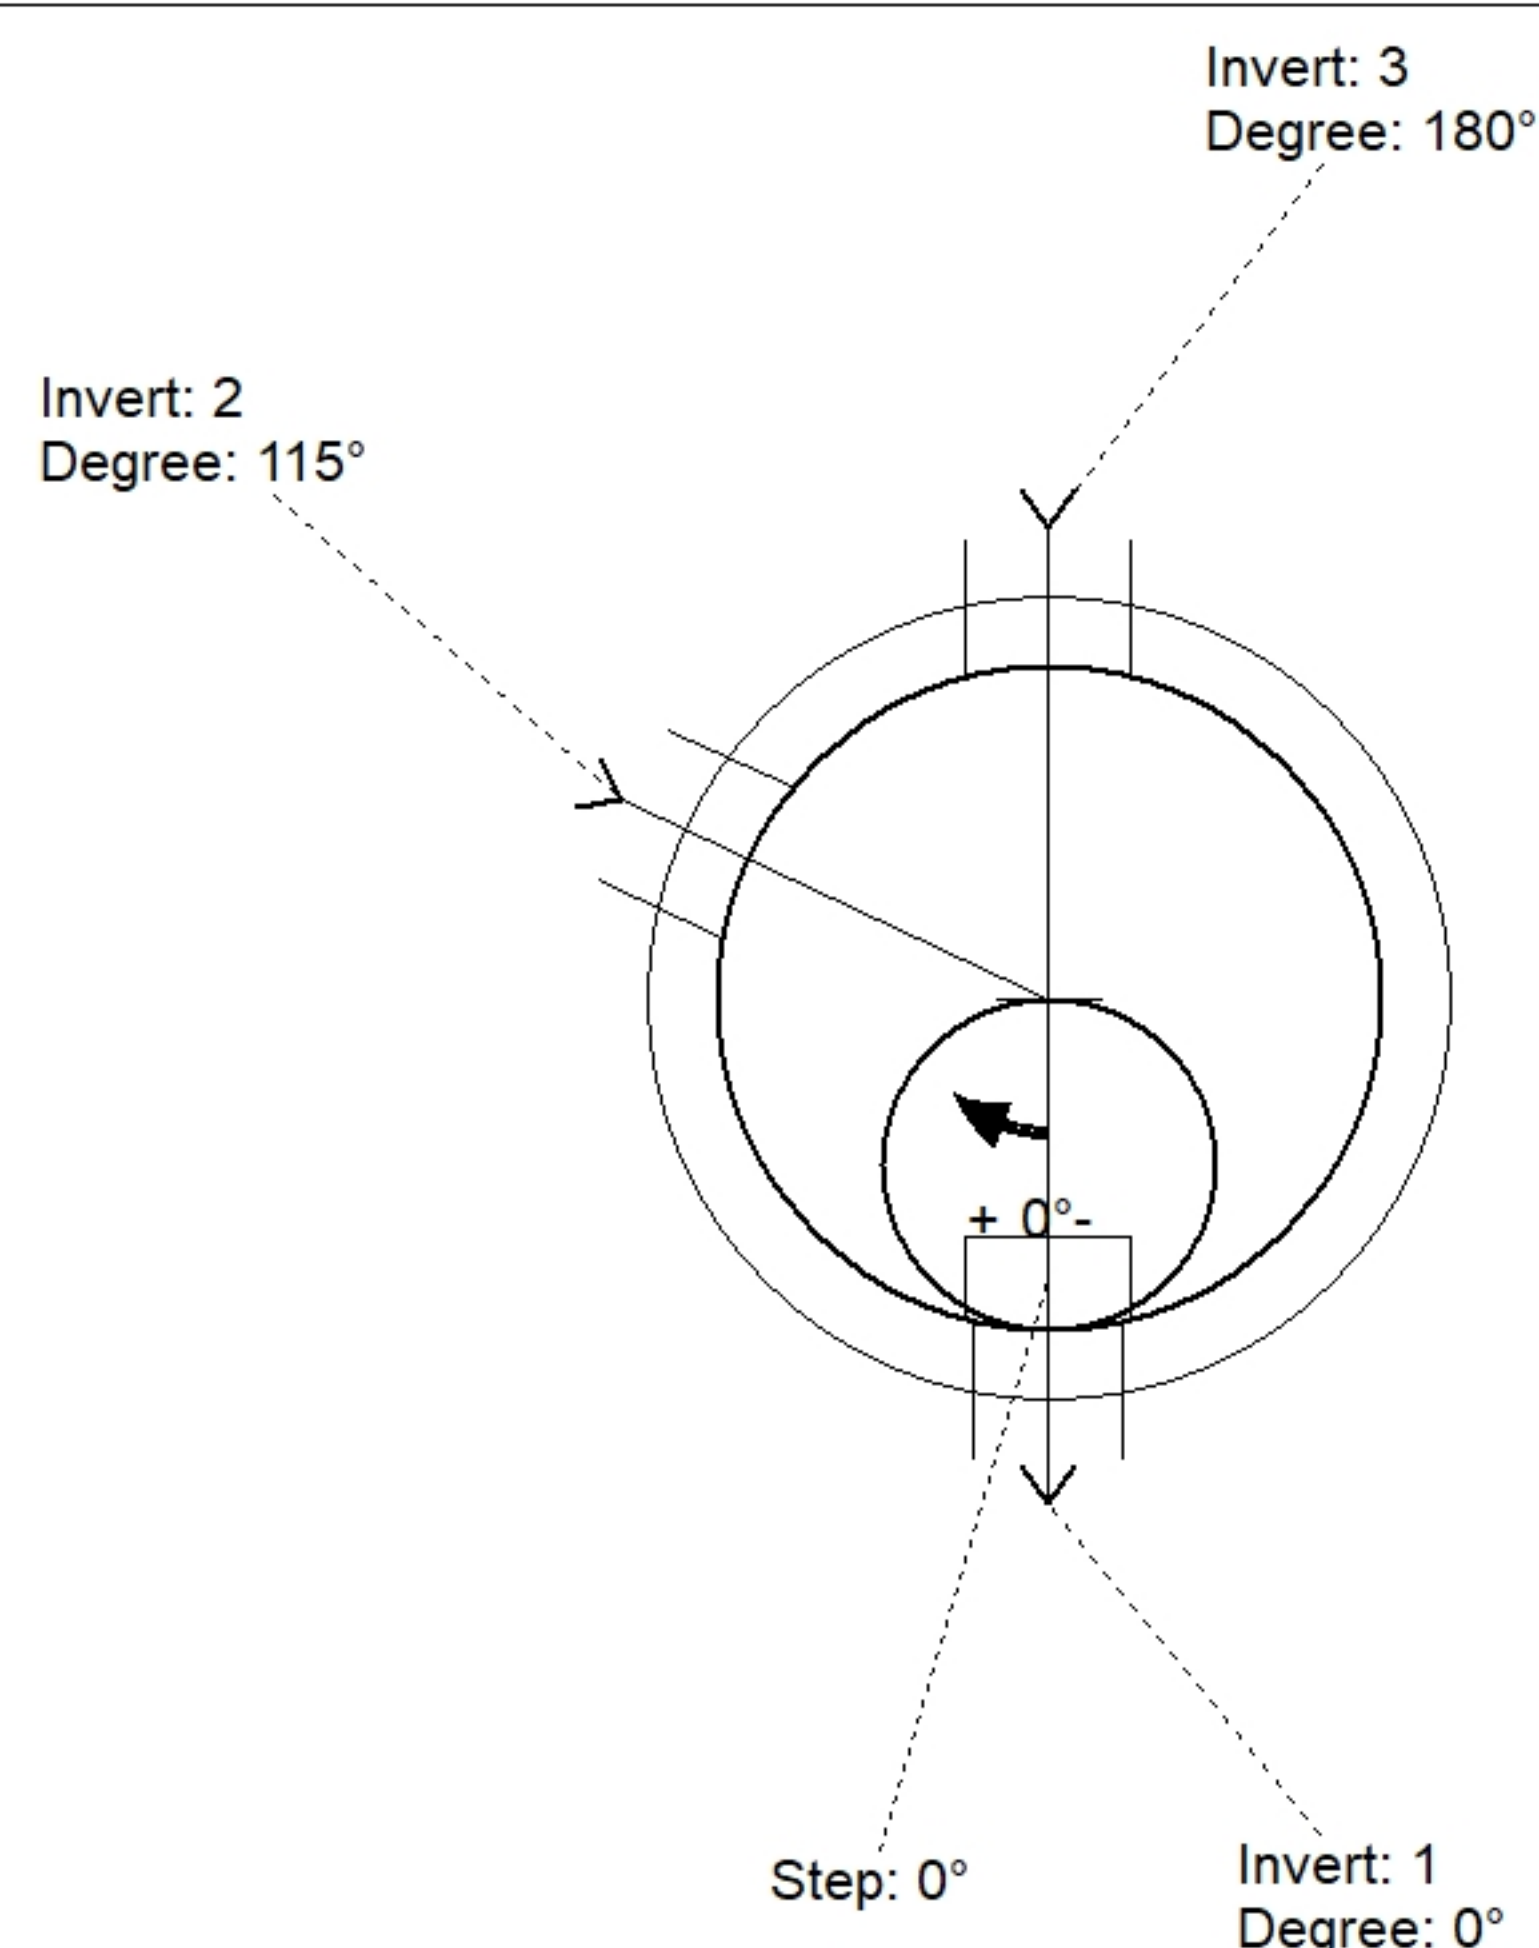

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	896'							
Reducer								
Invert 1	891.5'	0°	8" PVC SDR35	8.5"	10.75"	Quik-Lok QL-08-C	0.625"	P1
Invert 2	891.6'	115°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	0.25"	P1
Invert 3	891.6'	180°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	0.25"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Cast (Int. Dim.) - Interior Dimensions

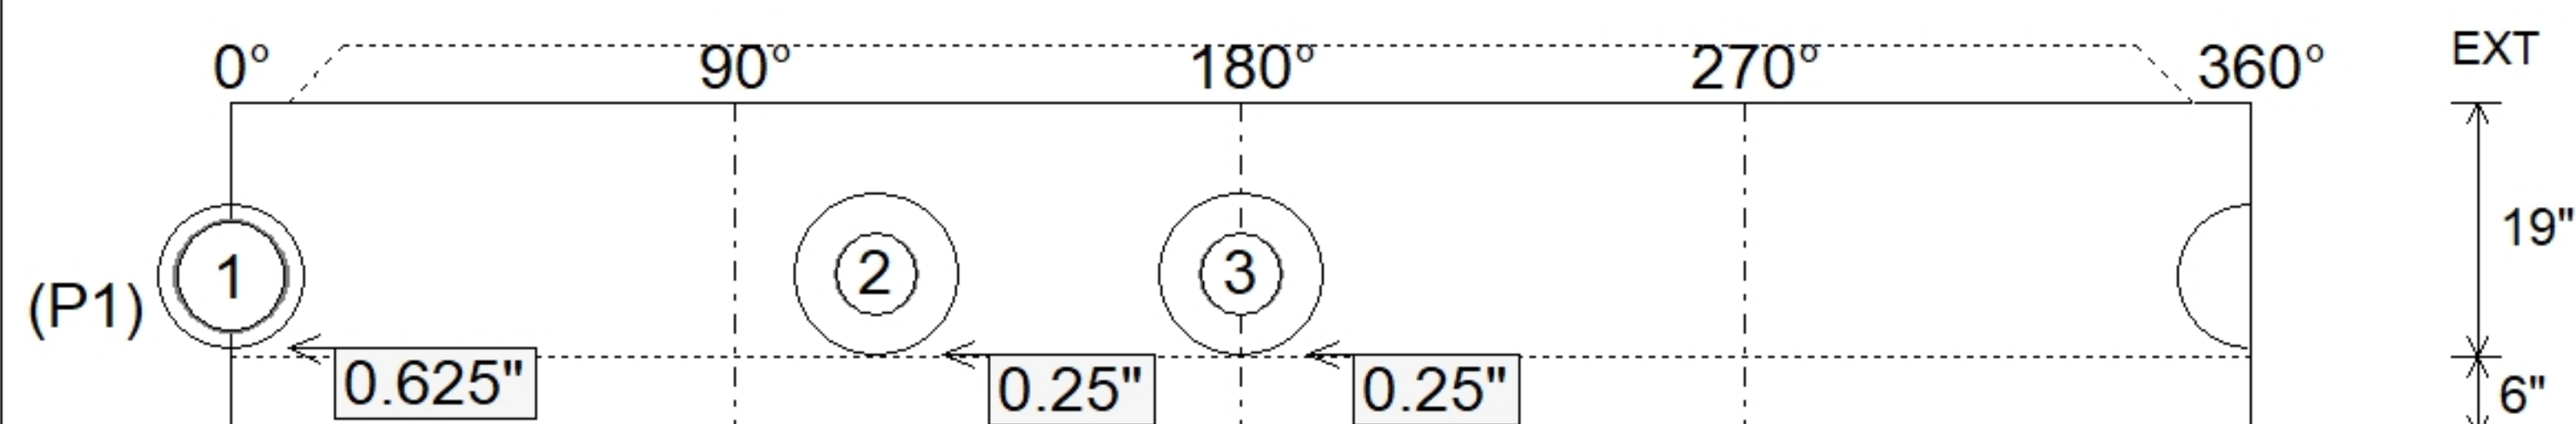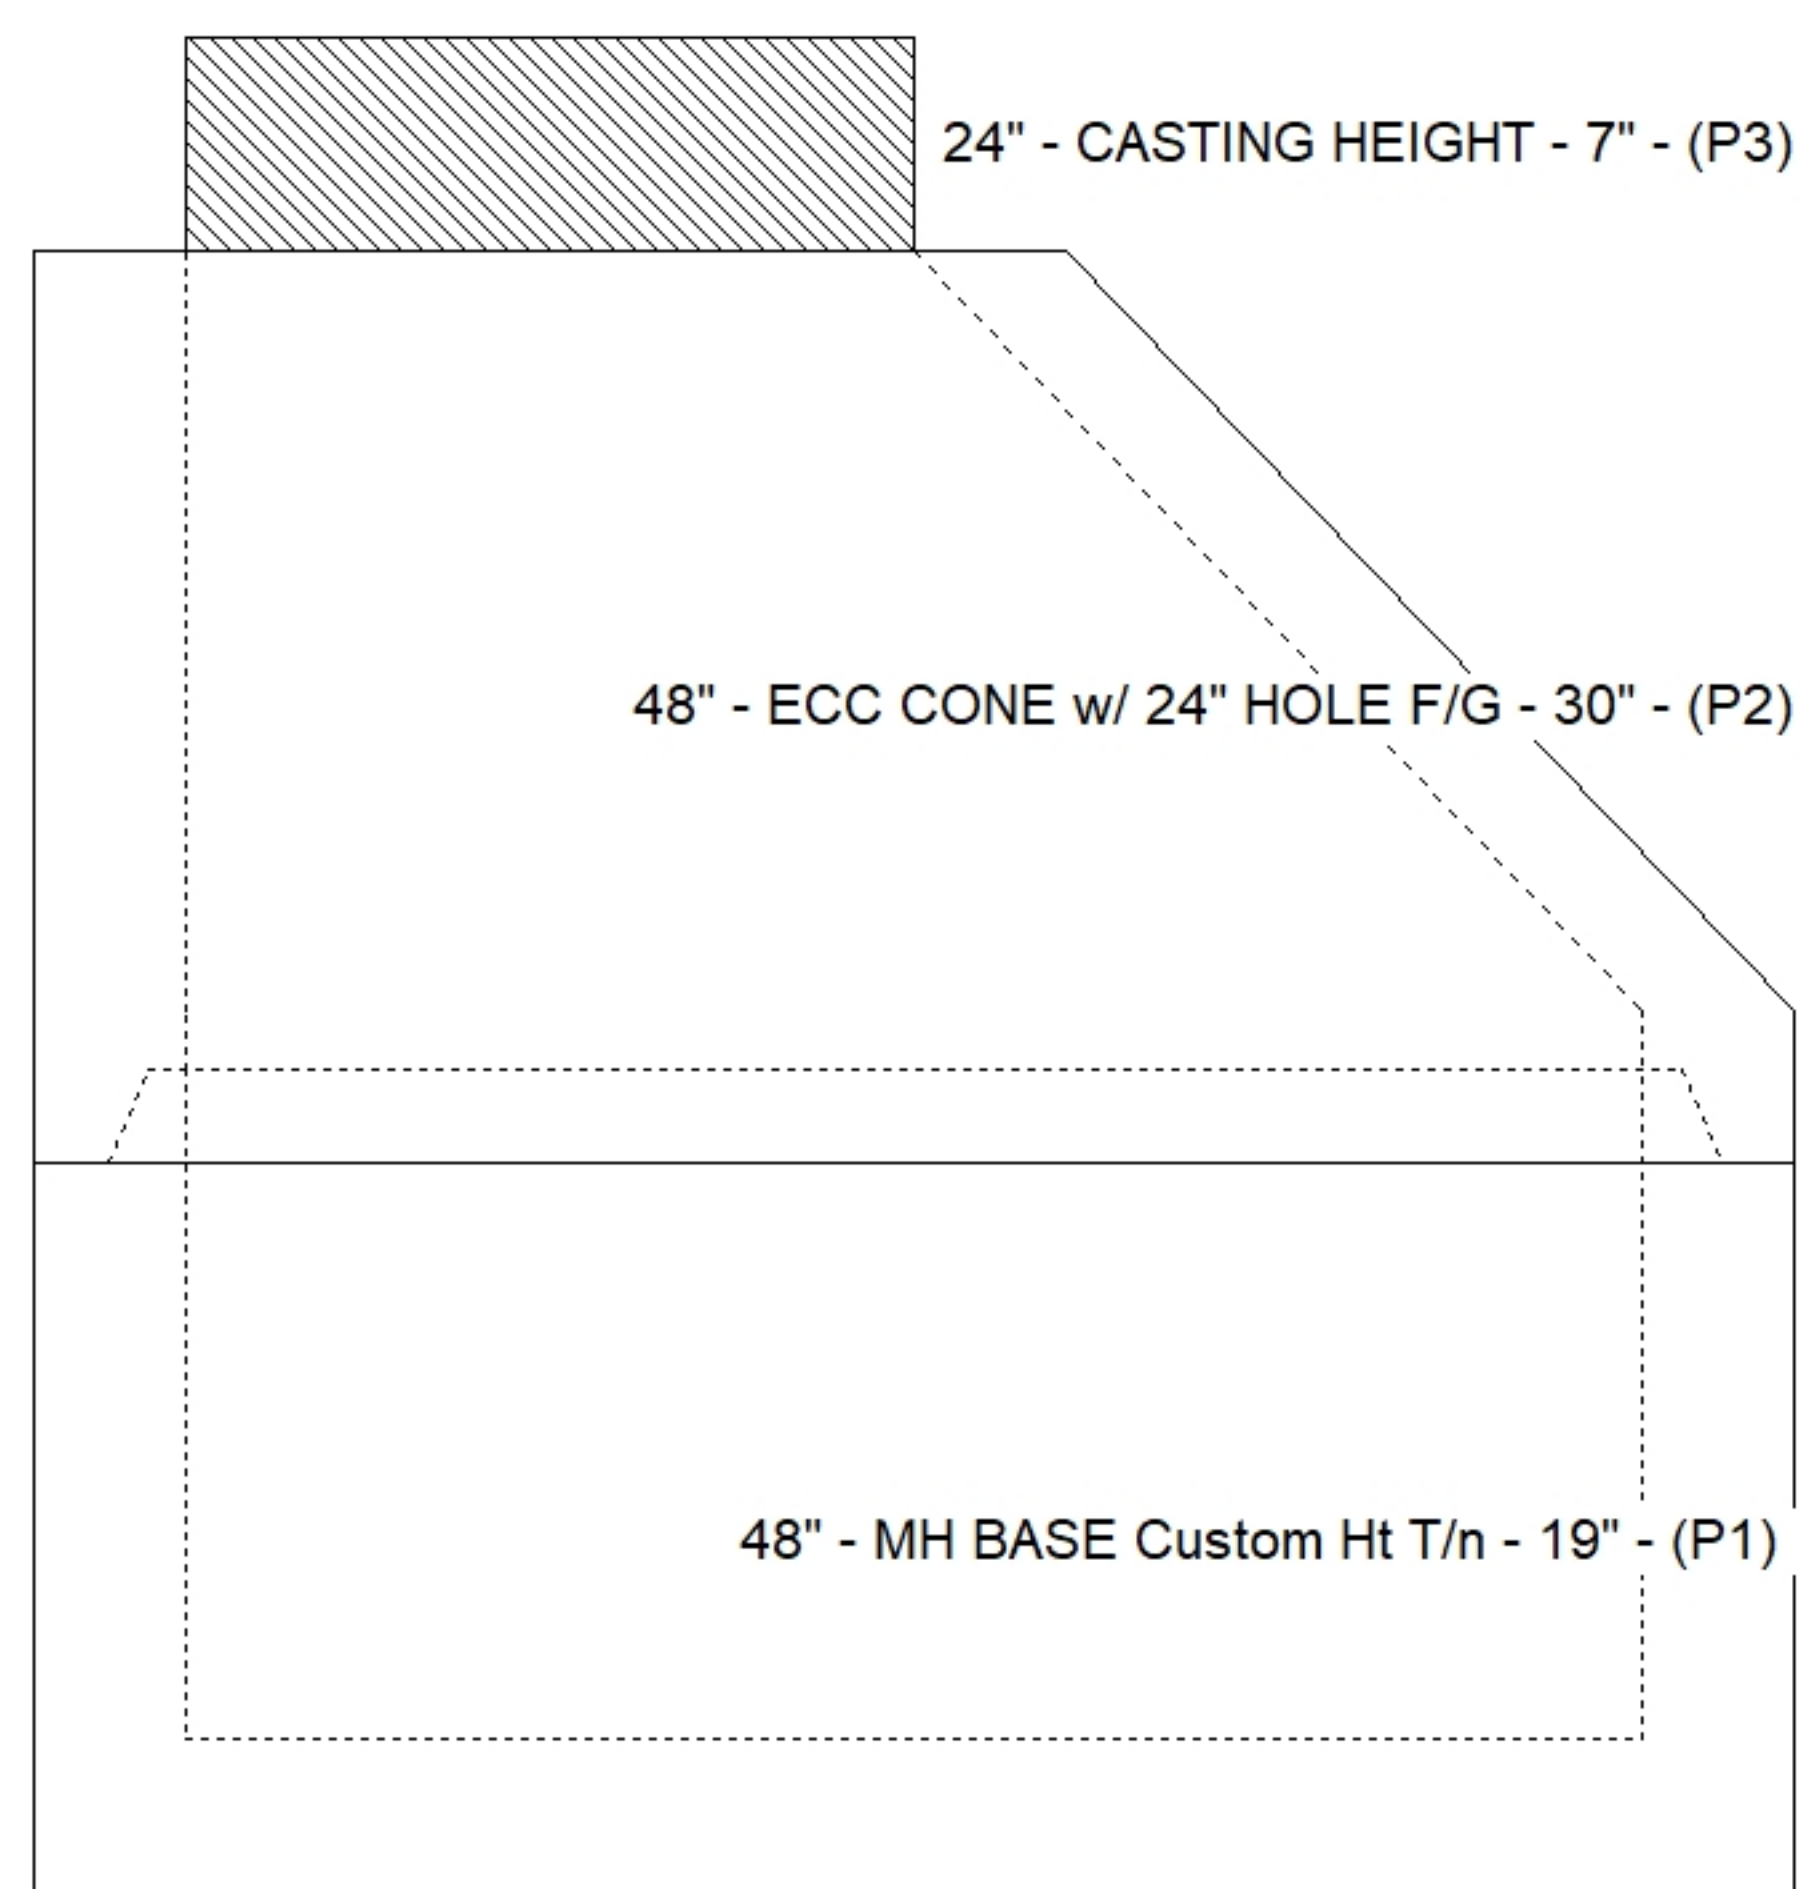

5/19/2026 12:54:59 PM

APPROVED BY:
