


Contractor: Seven Earthmovers LLC

Plant: 100



Slack: 0.8"

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	859.5'							
Reducer								
Invert 1	849.85'	0°	8" PVC SDR35	8.5"	12"	PSX 12-08 NYLO	0"	P1
Invert 2	854.85'	180°	8" PVC SDR35	8.5"	8.5"	Drop Tee 8" PVC	37.5"	P2
Invert 3	849.95'	180°	8" PVC SDR35	8.5"	8.5"	Drop Elbow 8" PVC	3"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

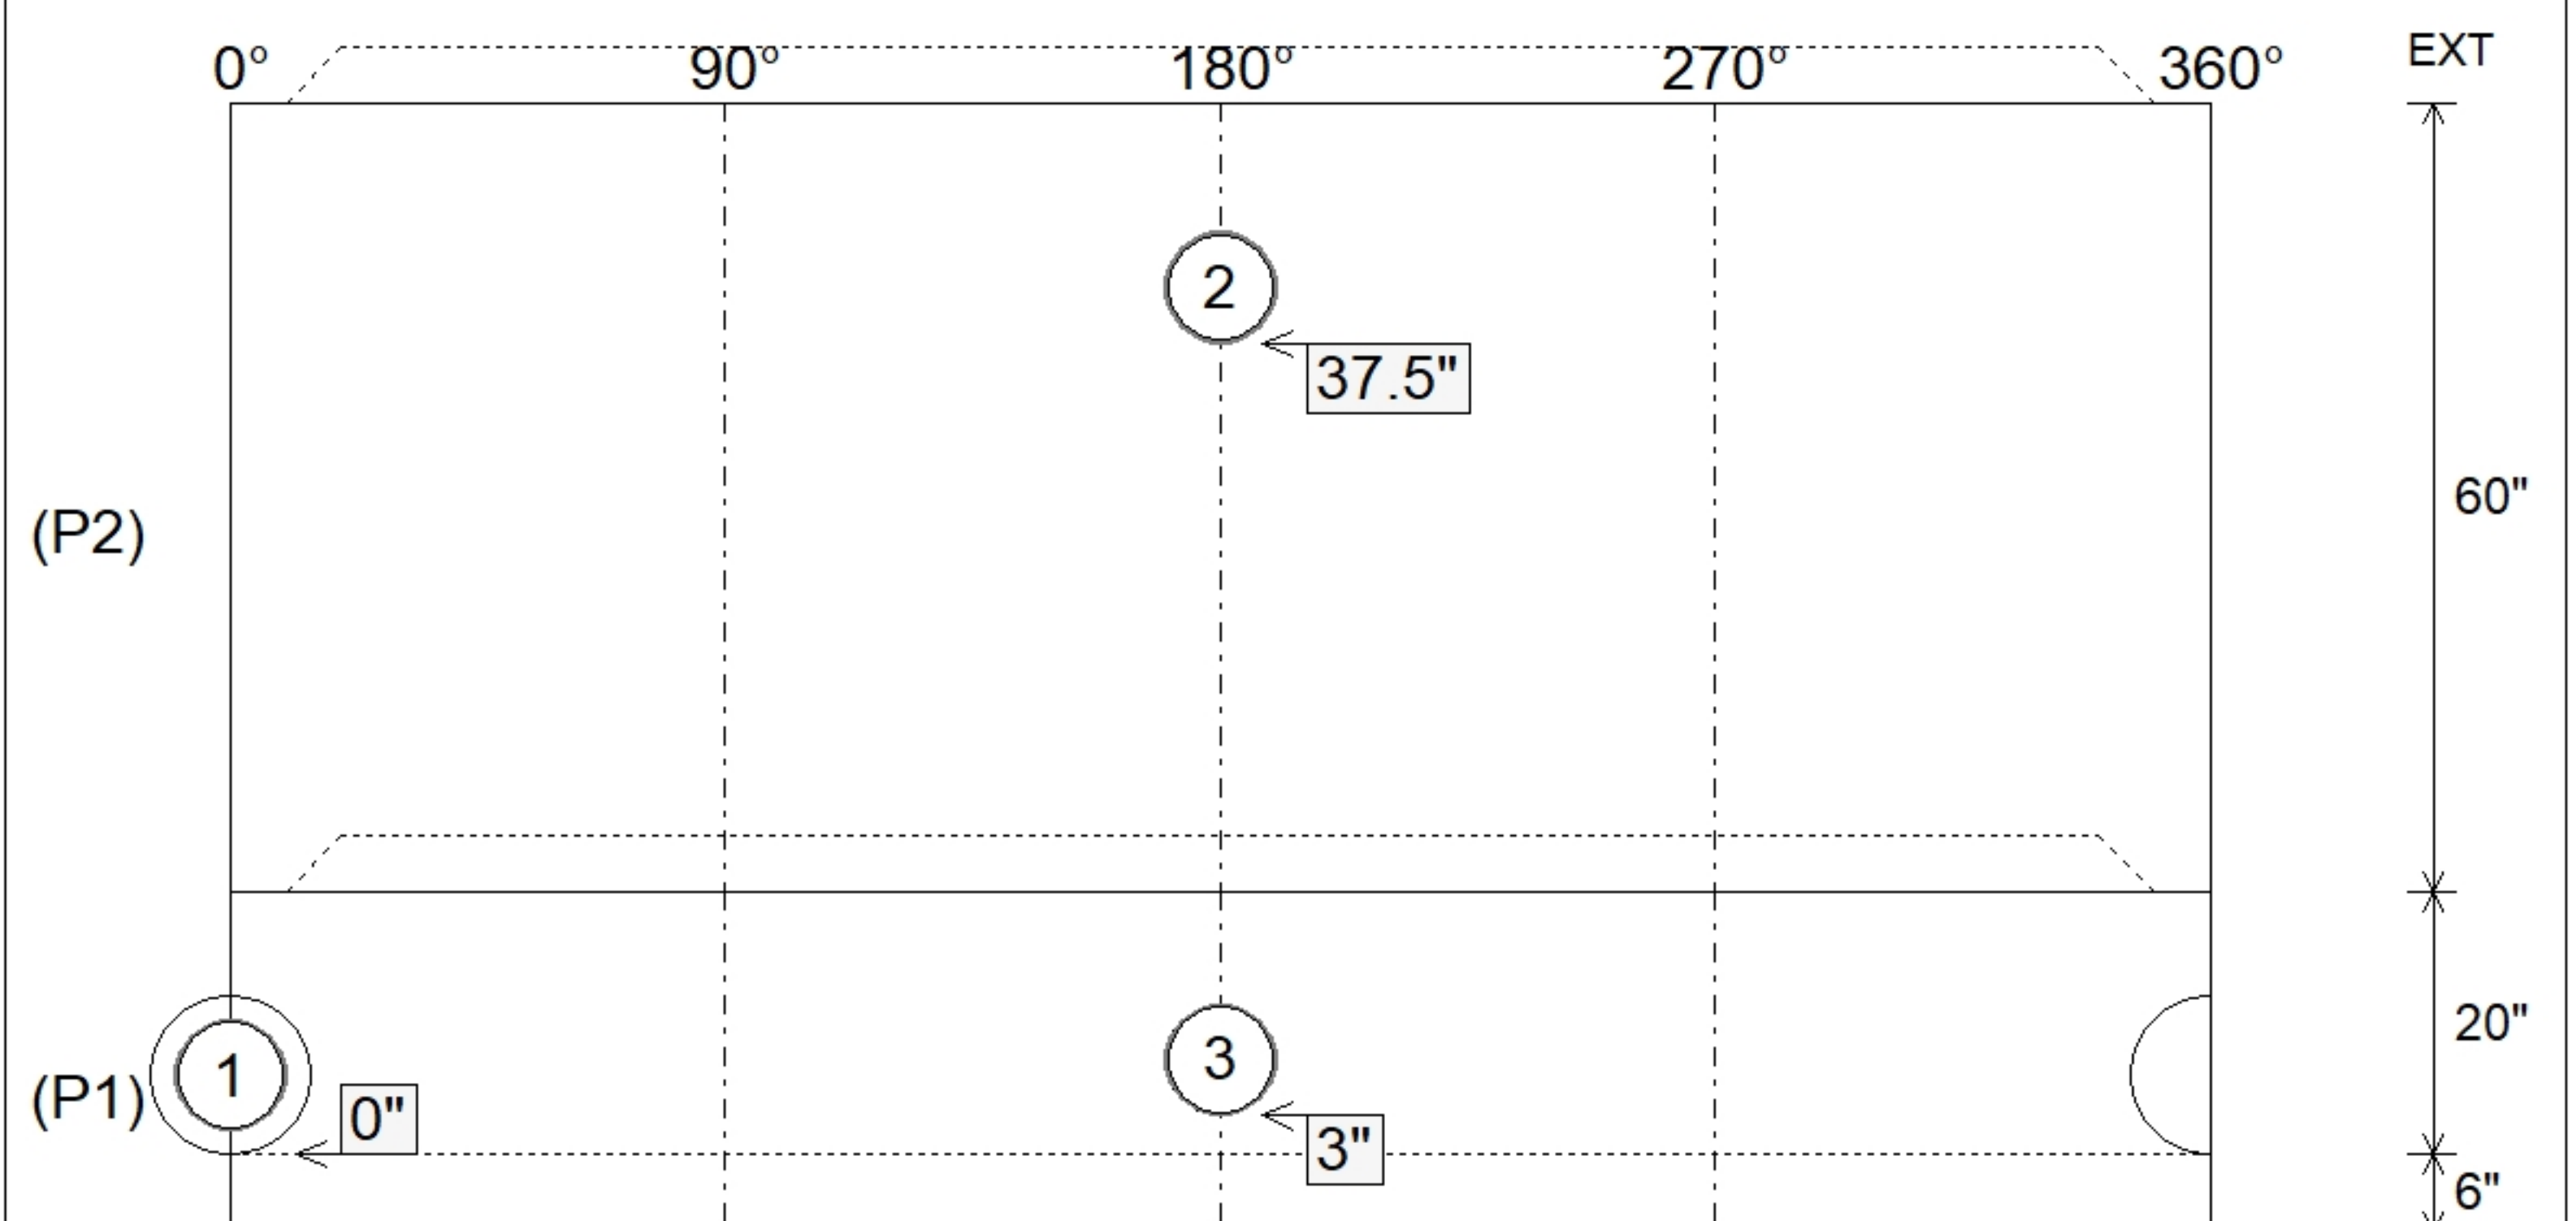

APPROVED BY:

