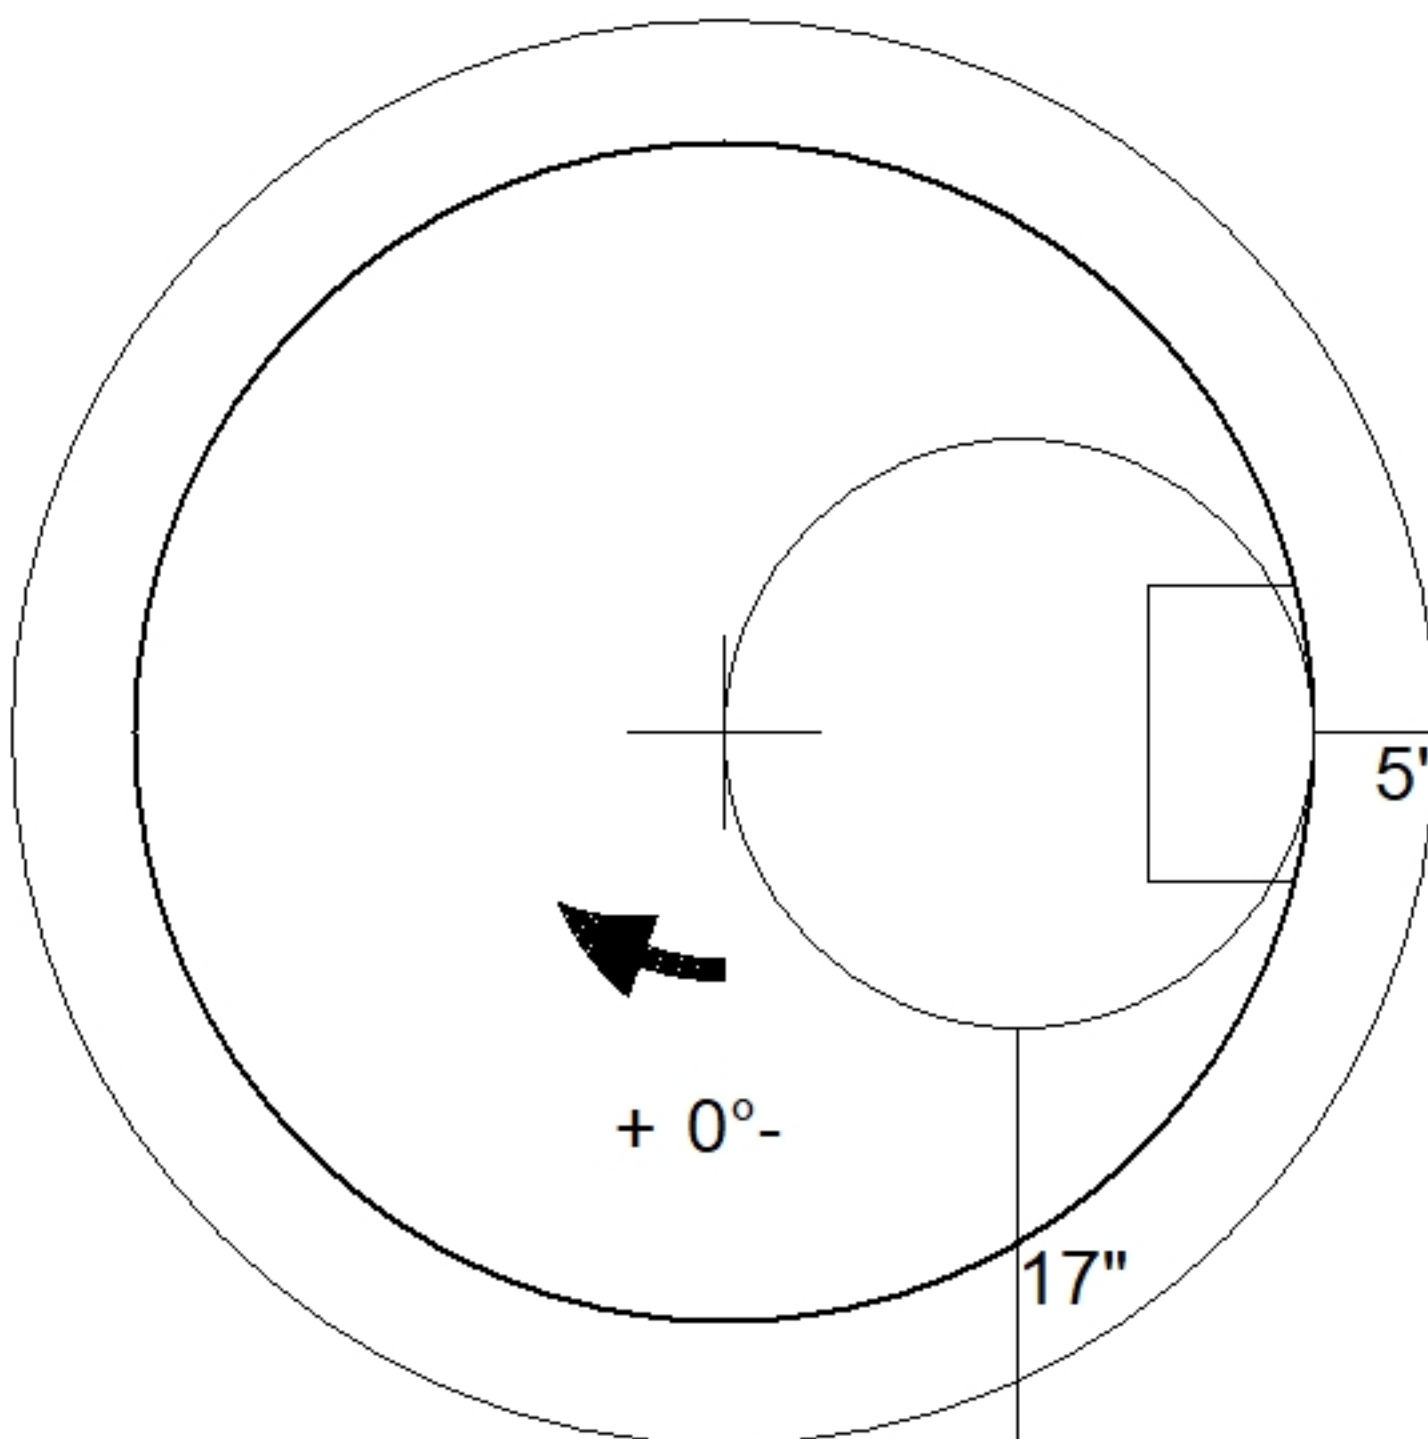
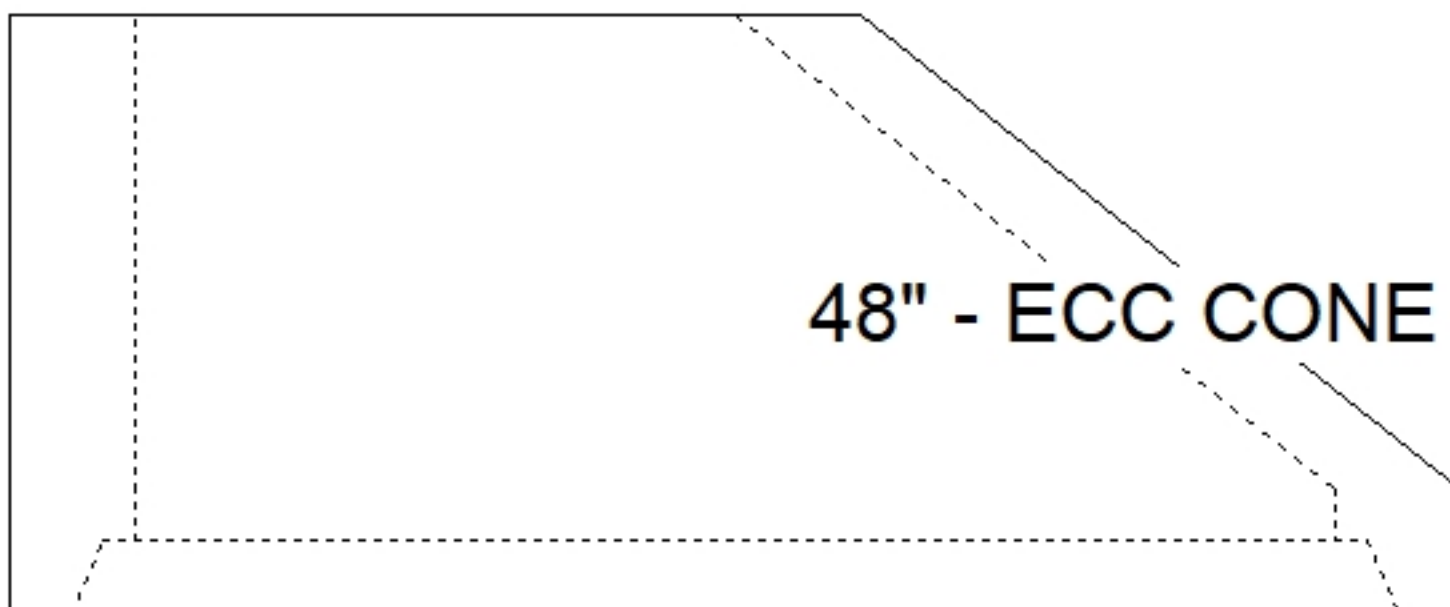


Job Name: 24-1164 Paddy's Run Flood PS		Plant: Beaver Dam, Ky.	Tech: S. Felletter	
Job Location: Louisville, Ky.		5/19/2026 8:37:15 AM	PC:	
Contractor: Core & Main LP (Lou)				
Structure ID: MH 4 (0+30)				
P2 MH048CN24		ECC CONE w/ 24" HOLE F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 4" P2) 48" - ECC CONE w/ 24" HOLE F/G - 24" P1) 48" - MH BASE T/n - 24" 1) 48" - STORM INVERT CHANNEL - 1/4 HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) Chimney Seal - Trelleborg FlexRib Chimney Seal 1) CASTING - HOE WT-420-MSD F/C Storm 1) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 18M DD 1) PSX - 12-06 NYLO 4) MH Step ML-10-TDS-NCR - 10"		0 lb 270 lb 1550 lb 2741 lb 1075 lb 0 lb 0 lb 10 lb 340 lb 0 lb 16 lb 8 lb 0 lb ----- Structure Total: 6010 lb	Structure Notes: 1. PER ASTM C478 & MSD SPECIFICATIONS. 2. CONCRETE = 5,000 PSI AT 28 DAYS. 3. CASTING BY ICST (HOE MC-420). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12). - RISER/WALLS (As .12). - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1550 lb Volume (Net): 0.33cu.yd
