

Job Name: 24-1643B - KYTC McCracken Co. Call 200 (ID 241301)
Job Location: Paducah, KY
Contractor: Jim Smith Contracting Co, LLC

PC: C. Goff
TECH: J. Horsley
Plant: 100








Structure ID: **St. 45+00 (PC 9)**

Spec: Box Culvert
Type: Box Culvert (08W/08F/08T)
Size: 48" x 48"

Rim: 5.75'
Invert: 5.75'
Rim to Invert: 0'

Sump: 0"
Floor (Top): 0'
Floor Height: 0'

Floor (Bot): 0'
Overall Height: 5.75'
Slack: 0'

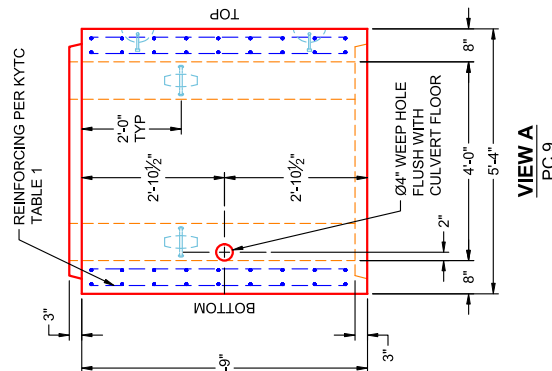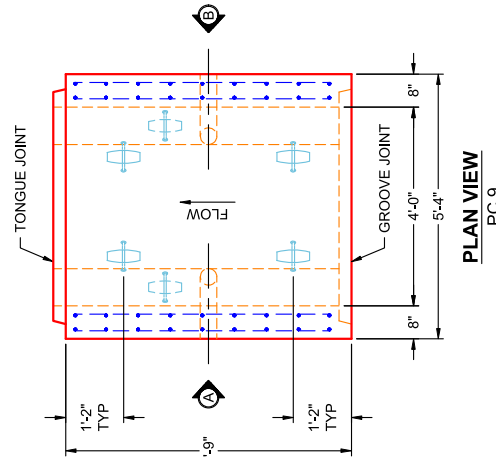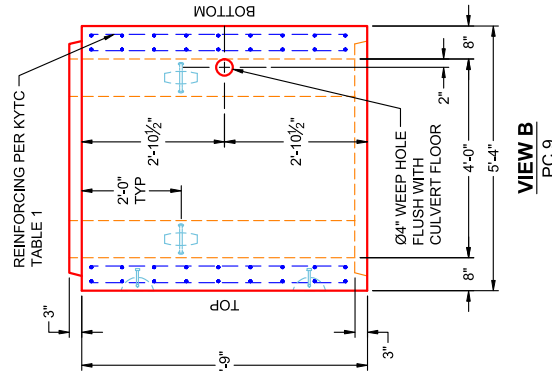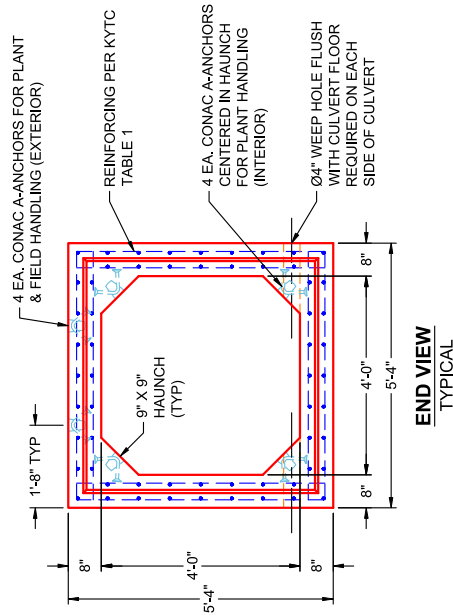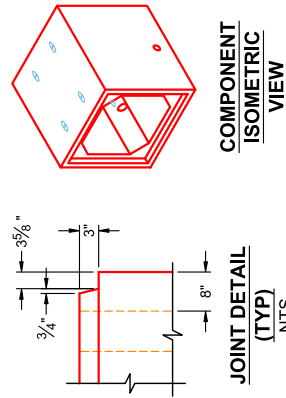

- GENERAL NOTES:**
- PER SECTION 605 OF KYTC STANDARD SPECS FOR ROAD & BRIDGE CONSTRUCTION
- KYTC STAMP REQUIRED
- WEEP HOLES REQUIRED
 - LOAD REQUIREMENTS: KY-HL93 (KY TABLE 1)
 - REINFORCEMENT PER KYTC TABLE 1
 - COVER DEPTH: 0' - 7"
 - CONCRETE: 5,000 PSI AT 28 DAYS
 - JOINT SEALANT: 1" BUTYL MASTIC (CS-102)
EXTERIOR JOINT WRAP: 12" WIDE (CS-212)
 - WEIGHT: 4' X 4' RCBC = 1,968 LBS / LF
(5'-9\"/>

SUBMITTAL DRAWING:
4'-0" X 4'-0" X 5'-9" BOX CULVERT (8" WALLS & 9" HAUNCH)

CUSTOMER: JIM SMITH CONTRACTING
PROJECT: KYTC MCCracken CO CALL 200 (ID 241301)
STRUCTURE: ST. 45+00 (PC 9)
QUOTE/SALES ORDER NO: 24-1643B
CHECKED BY: B. SMITH
DATE: 05/28/26

SCALE: NTS
PG. 1 OF 1




REVISION INFORMATION	
REV. DATE:	NO REVISIONS TO DATE

THIS DRAWING IS THE PROPERTY OF INFRASTRUCTURE PRECAST, INC. ANY USE OR DUPLICATION OF THIS DRAWING WITHOUT PRIOR AUTHORIZATION IS STRICTLY PROHIBITED.


GENERAL NOTES:

- PER SECTION 605 OF KYTC STANDARD SPECS FOR ROAD & BRIDGE CONSTRUCTION
 - KYTC STAMP REQUIRED
 - WEEP HOLES REQUIRED
- LOAD REQUIREMENTS: KY-HL93 (KY TABLE 1)
- REINFORCEMENT PER KYTC TABLE 1
- COVER DEPTH: 0' - 7"
- CONCRETE: 5,000 PSI AT 28 DAYS
- JOINT SEALANT: 1" BUTYL MASTIC (CS-102)
EXTERIOR JOINT WRAP: 12" WIDE (CS-212)
- WEIGHT: 4' X 4' ROBC = 1,968 LBS / LF
- 4'-11 1/2" LONG SECTION = 9,756 LBS
- 5'-9" LONG SECTION = 11,314 LBS

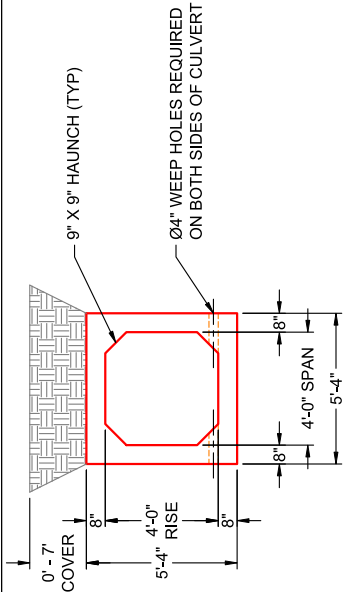


TYP. COVER DETAIL

NTS




JOINT DETAIL (TYP)

NTS

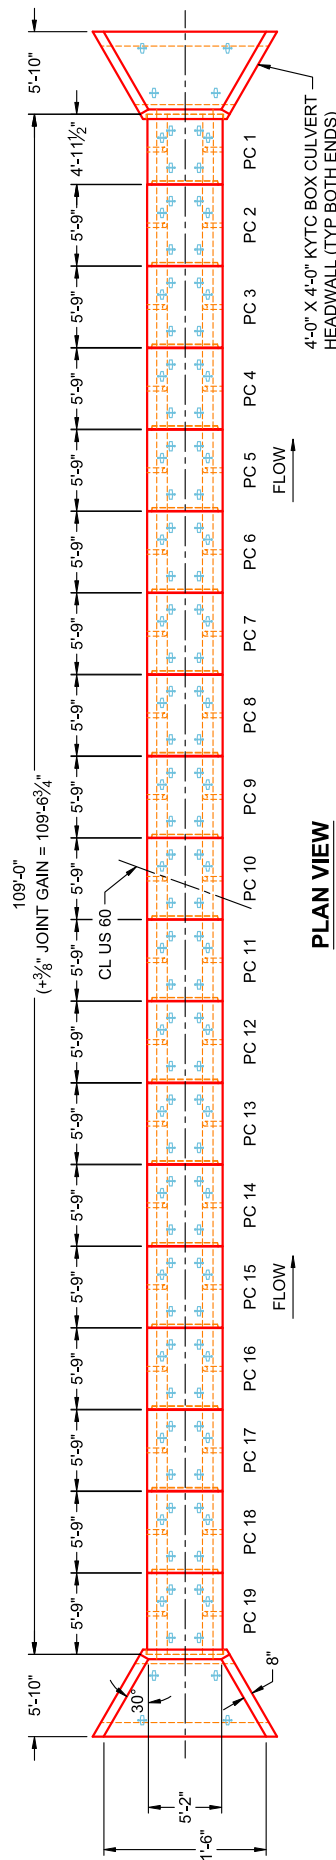

PLAN VIEW

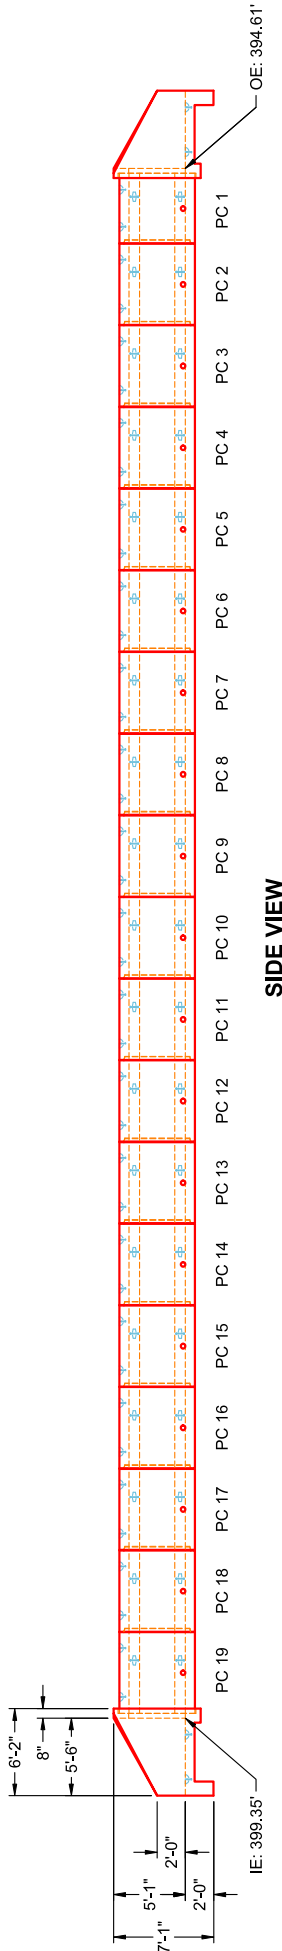

SIDE VIEW

REVISION INFORMATION

REV. / DATE: NO REVISIONS TO DATE



SUBMITTAL DRAWING:
4' X 4' BOX CULVERT LAYING PLAN

CUSTOMER: JIM SMITH CONTRACTING

PROJECT: KYTC MCCracken CO. CALL 200 (ID 241301)

STRUCTURE: ST. 45+00

QUOTE/Sales ORDER NO: 24-1643B

CHECKED BY: B. SMITH

DATE: 05/28/26

SCALE: NTS

PG. 1 OF 1
