


Job Name: 24-2527B - KYTC Nelson Co Call 105 (241107) Job Location: Bardstown, KY Contractor: Hinkle Construction Services, LLC					Plant: 100 7/31/2026 7:55:01 PM		Tech: Jared - F PC: E. Bradley				
Structure ID: Str 2 CBIA											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht T/n							
P3) 24" x 120" - CB INLET KY A 10' TOP RIGHT F/G - 10" P2) 24" x 120" - CB INLET KY A 10' BOTTOM RIGHT T/G - 18" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht T/n - 32" 1) CASTING - HOE KY-206 F/C (KY CBI A) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18"					3398 lb 5270 lb 4491 lb 206 lb 0 lb 0 lb ----- Structure Total: 13364 lb		Structure Notes: ** KYTC STATE PROJECT ** STATION: 406+68.11, 25.82 RT 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. CASTING SUPPLIED BY ICAST (HOE KY-206 F/C (KY CBI A)). 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W. 5. RIM ELEVATION AS SHOWN ON THIS SUBMITTAL IS TO THE TOP OF CURB (8" ABOVE FLOW LINE ELEVATION PROVIDED IN PLANS).				
Rim: 656.4'		Rim to Invert: 5.37'		Slack: 4.44"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	651.03'	90°	26"	15" CMP	16"	Hole 18	18"	18"	-1.5"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

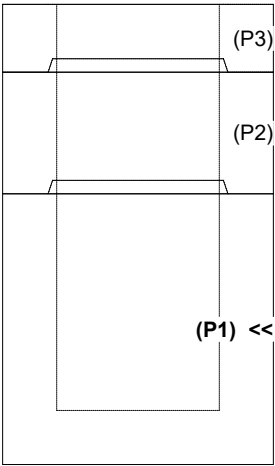


(P3)

(P2)


(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

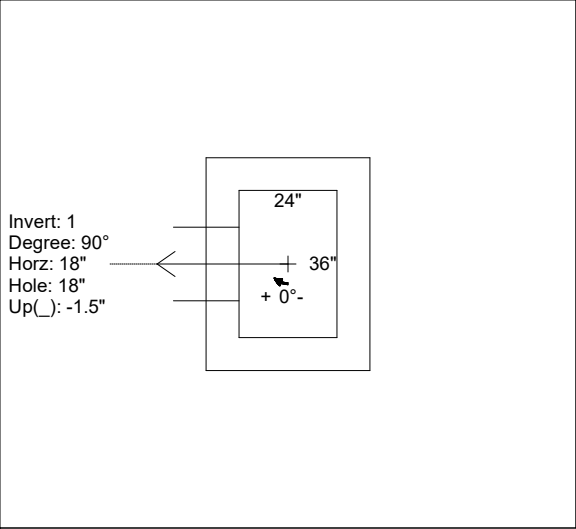


Invert: 1
Degree: 90°
Horz: 18"
Hole: 18"
Up(): -1.5"

UPSIDE-DOWN VIEW (int. dimenions)

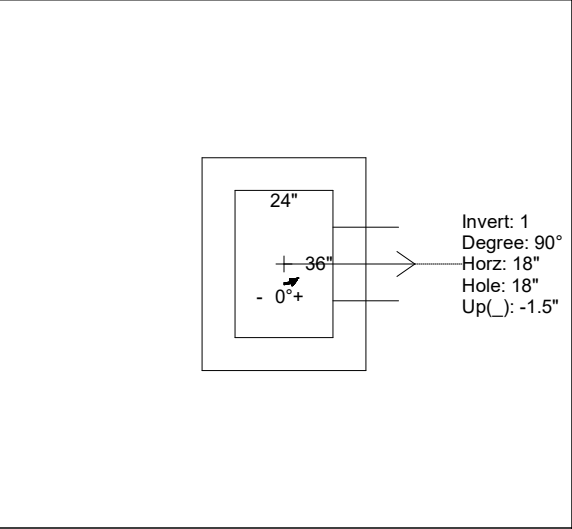

Invert: 1
Degree: 90°
Horz: 18"
Hole: 18"
Up(): -1.5"

INSIDE WALL DIMENSIONS

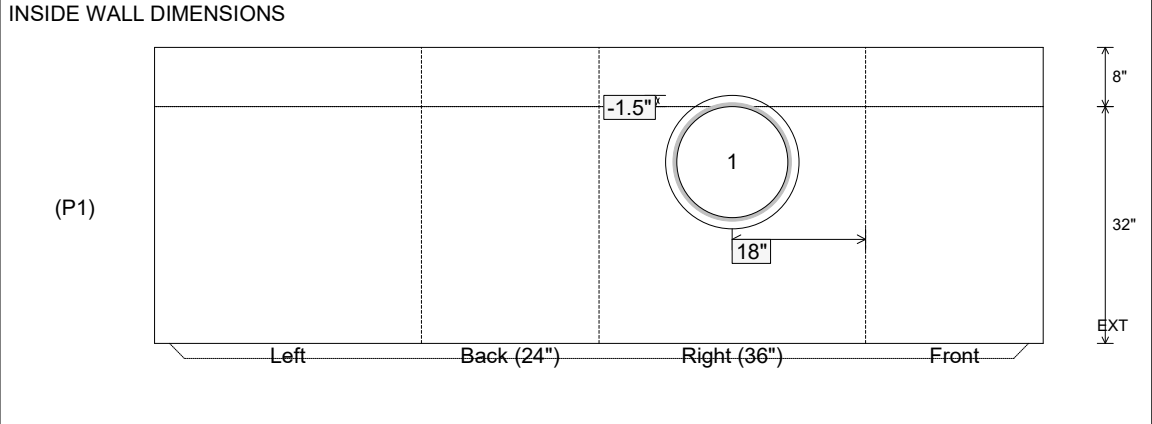

(P1)

Left Back (24") Right (36") Front

8"

32"

EXT

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 32" Height (Ext): 40"	Weight (Net): 4491 lb Volume (Net): 1.15cu.yd
----------------------------------	---------------------------------	--	--	--
