

Job Name: 24-3432P3 - Sheperdsville CityPark Addition
Job Location: Sheperdsville, KY
Contractor: Yockum Trucking & Excavating

Plant: 100

9/22/2026 12:27:36 PM

Tech: J. Horsley

PC: A. Chamber



Structure ID: 8" FT w//24"E

P1 MH048LD07ECC

MH FLAT TOP w/ 24" ECC Hole F/F


P1) 48" - MH FLAT TOP w/ 24" ECC Hole F/F - 7"
1) 24" - Conseal CS-102 1.00"

Structure Total:


1286 lb
0 lb
1286 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
 2. CONCRETE = 4,000 PSI AT 28 DAYS.
- .REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB = H20 LOADING.

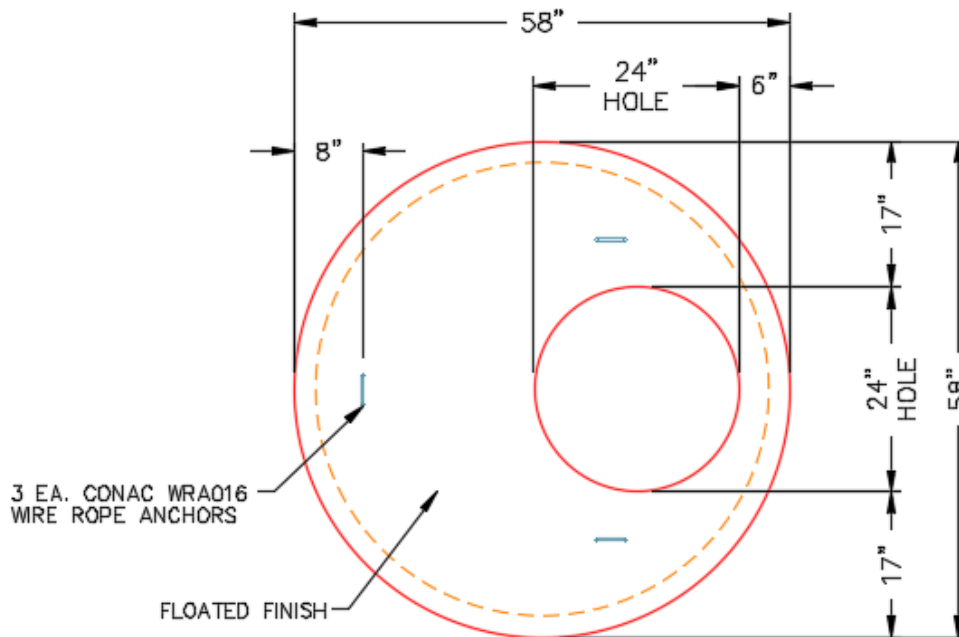

PLAN VIEW

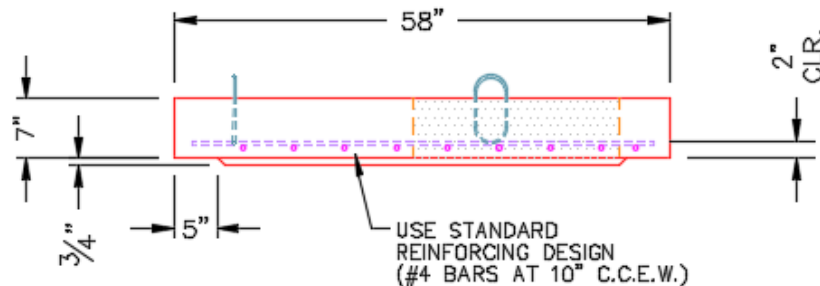

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 5"

Height (Ext): 7"

Weight (Net): 1286 lb
Volume (Net): 0.33cu.yd
