

Job Name: 24-3511 Coles Ferry Section 18 & 19
Job Location: Lebanon, TN
Contractor: Covenant Constructors, LLC

Plant: Beaver Dam, KY
6/18/2026 11:00:42 AM

Tech: J. Horsley
PC: A. Chambers



Structure ID: JB4



P2 MH060LD08

MH FLAT TOP w/ 24" ECC Hole F/F

- P3) 24" - CASTING HEIGHT - 7"
P2) 60" - MH FLAT TOP w/ 24" ECC Hole F/F - 8"
P1) 60" - MH BASE Custom Ht F/n - 36"
1) CASTING - JBS 1150 F/C STORM
1) 60" - Conseal CS-102 1.00"
1) 24" - Conseal CS-102 1.00" (Double)
1) Hole - 32
1) Hole - 26
1) Hole - 22
3) MH Step ML-10-TDS-NCR - 10"

0 lb
2429 lb
5598 lb
250 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 8277 lb

Structure Notes: 1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,500 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING BY ICAST (JBS 1150 F/C)
REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB H20 LOADING..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

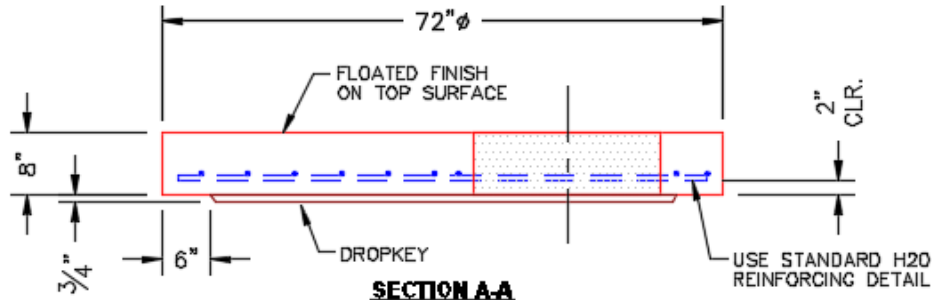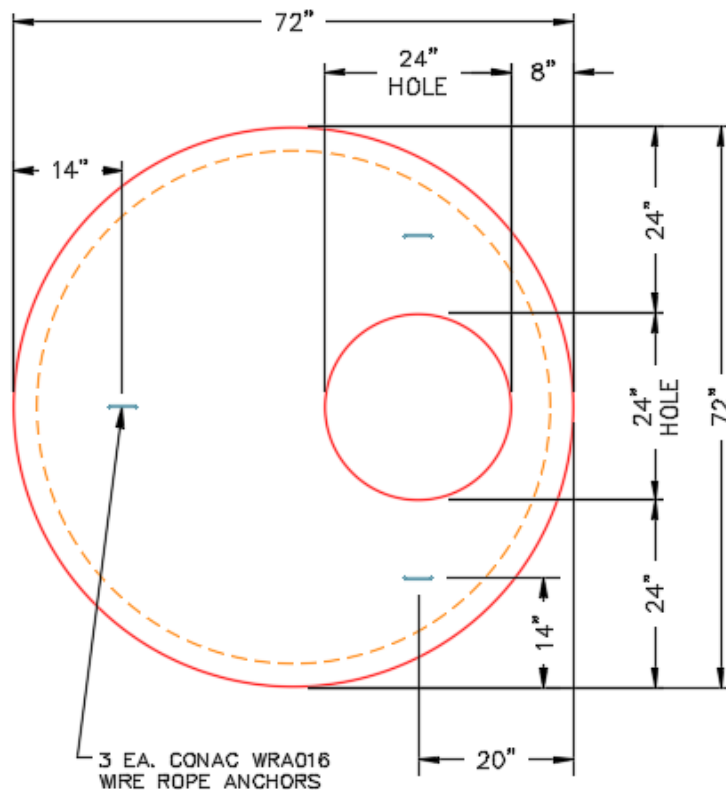

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 8"

Weight (Net): 2429 lb
Volume (Net): 0.62cu.yd
