

Contractor: Scotty's Contracting & Stone, LLC

PC:	C. Goff
TECH:	J. Horsley
Plant:	Beaver Dam



Size: 24" x 30"

Rim to Invert: 3.25'


Floor Height: 8"

Slack: 0.25"

4. HOE KY-460-11 FRAME & GRATE SUPPLIED BY ICAST



2) Hole - 24

Structure Total: 4319 lb



Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	543.14'							
Reducer								
Invert 1	539.89'	90°	18" HDPE	21.2"	24"	Hole 24	-1.625"	P1
Invert 2	539.89'	250°	18" HDPE	21.2"	24"	Hole 24	-1.625"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 30" - CASTING HEIGHT - 3.75" - (P2)

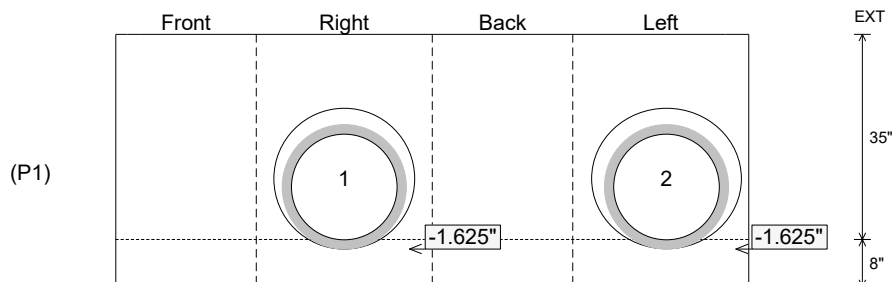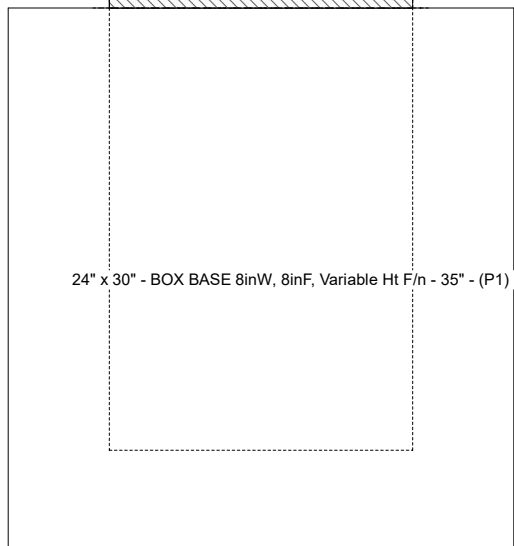

SUBMITTAL
APPROVED BY:
