

Contractor: Scotty's Contracting & Stone, LLC

TECH: J. Horsley

Plant: Beaver Dam



Size: 24" x 30"

Rim to Invert: 4.61'

Floor Height: 8"


Slack: 3.32"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

2) Hole - 4

0 lb

Structure Total: 5358 lb

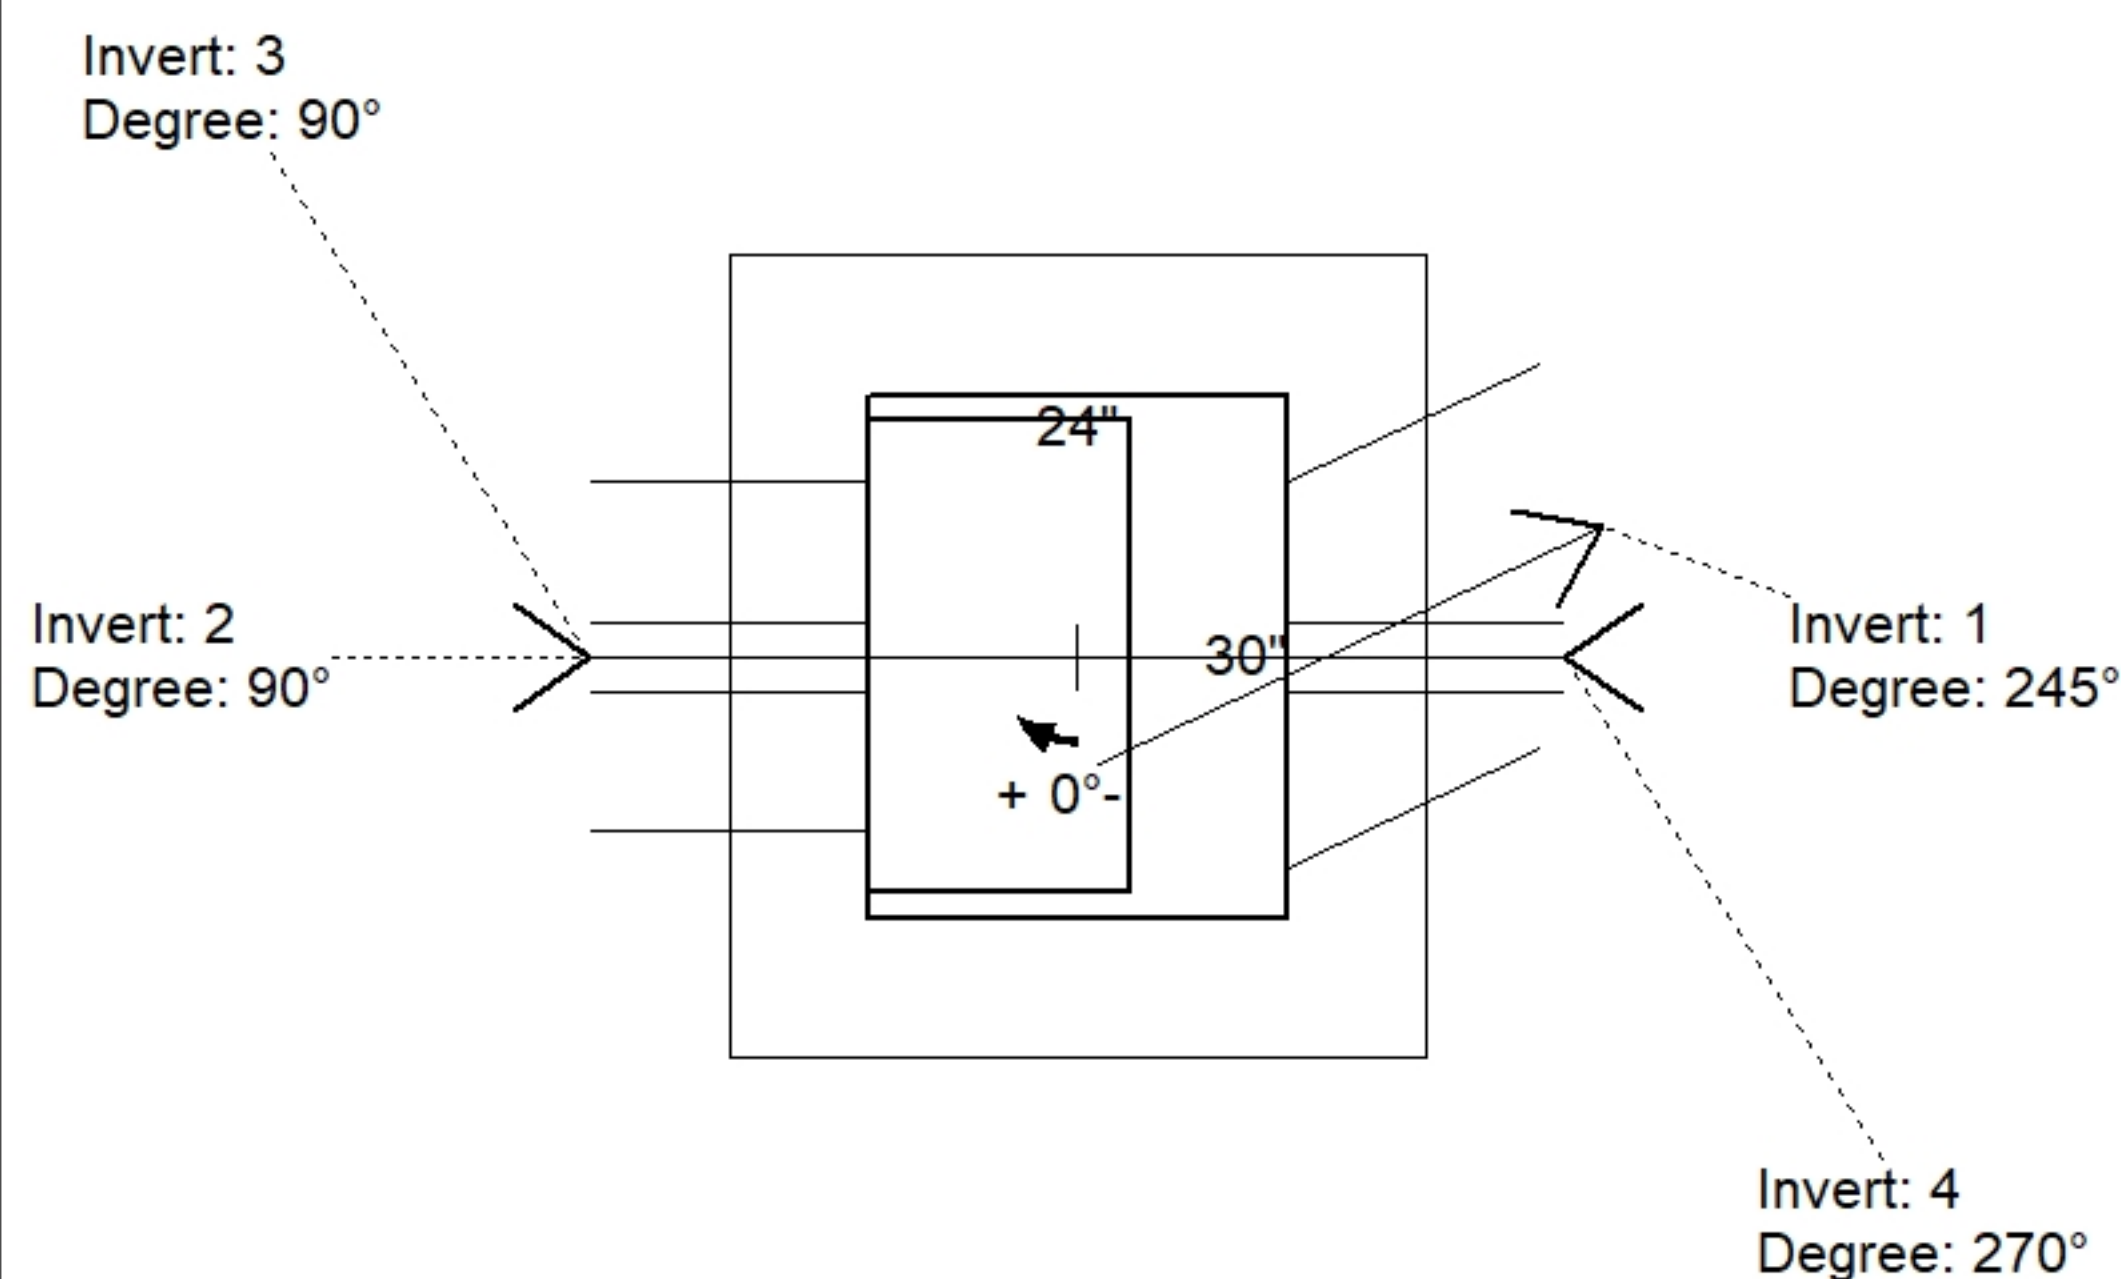


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	547.03'							
Reducer								
Invert 1	542.42'	245°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 2	542.42'	90°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 3	544.75'	90°	4" WEEP HOLE	4"	4"	Hole 4	27.96"	P1
Invert 4	544.75'	270°	4" WEEP HOLE	4"	4"	Hole 4	27.96"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

15" x 27" - P.I.P. - BY OTHERS - 8" - (P3)

24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8" - (P2)

24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 36" - (P1)

Default - Interior Dimensions

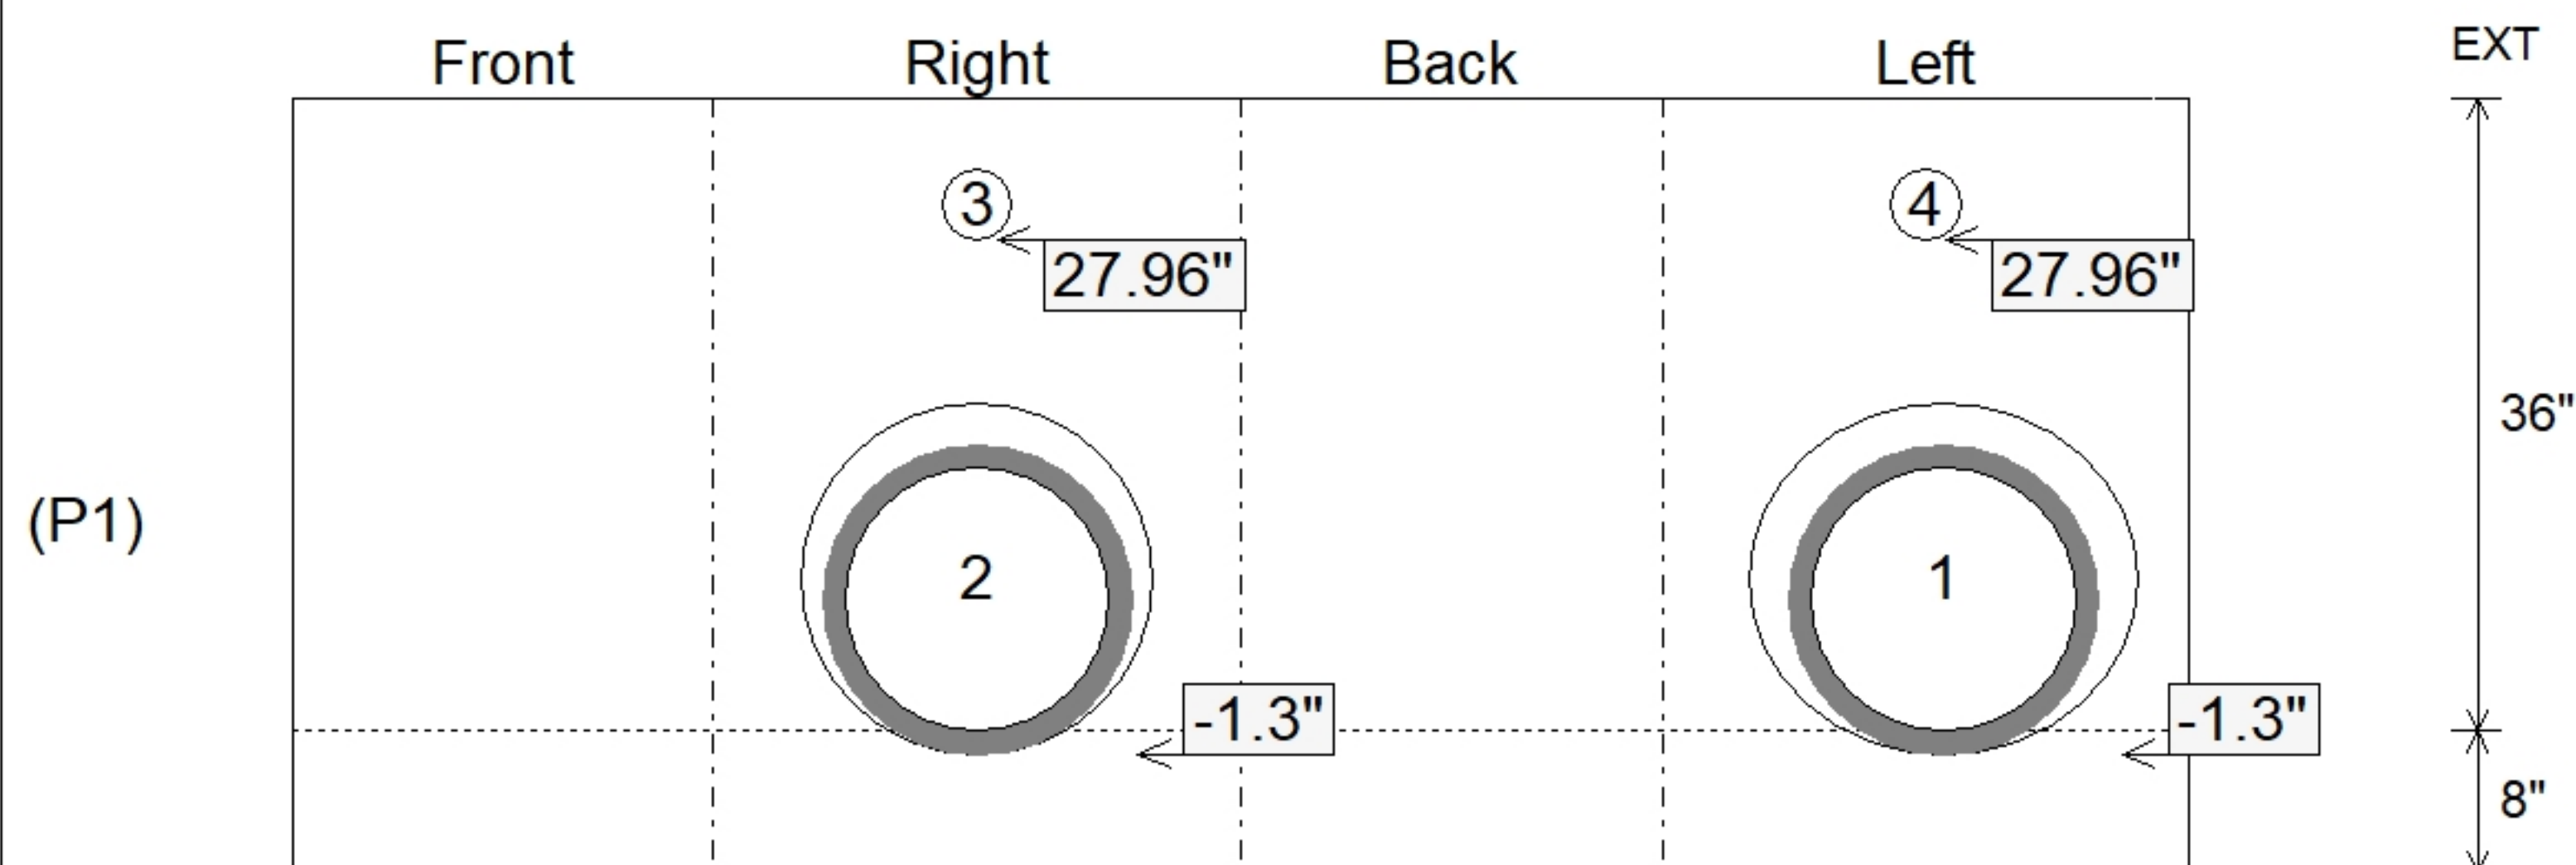

SUBMITTAL
APPROVED BY:
