

Contractor: Scotty's Contracting & Stone, LLC

TECH: J. Horsley

Plant: Beaver Dam



Size: 24" x 30"

Rim to Invert: 3.81'

Floor Height: 8"

Slack: 3.72"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

2) Hole - 4

0 | b

Structure Total: 4644 lb

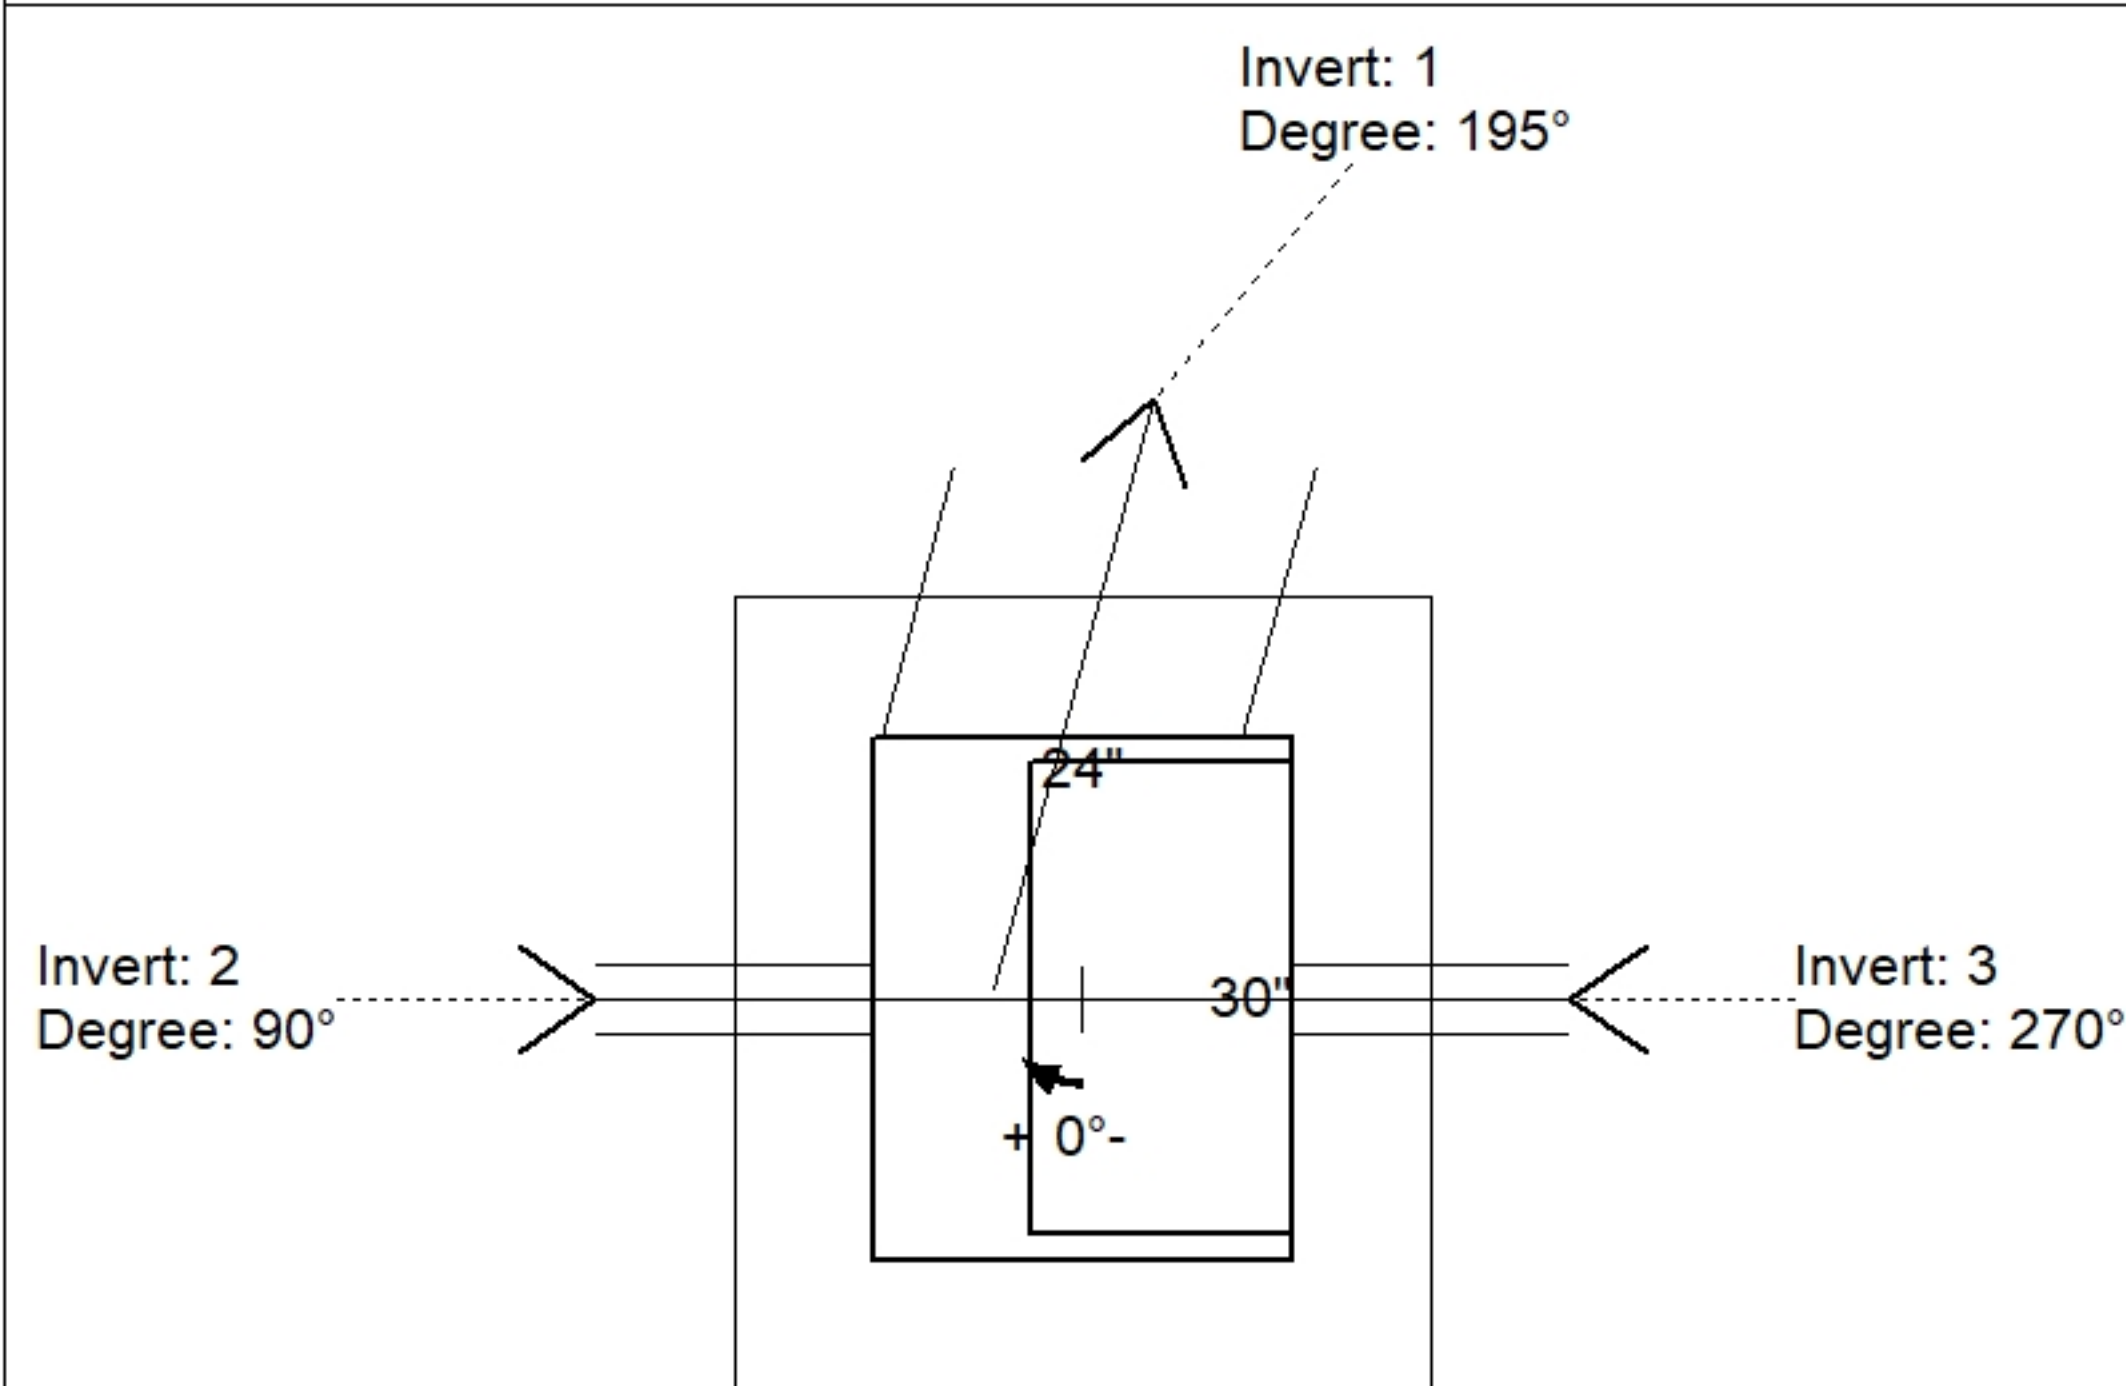


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	543.57'							
Reducer								
Invert 1	539.76'	195°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 2	541.26'	90°	4" WEEP HOLE	4"	4"	Hole 4	18"	P1
Invert 3	541.26'	270°	4" WEEP HOLE	4"	4"	Hole 4	18"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

15" x 27" - P.I.P. - BY OTHERS - 8" - (P3)

24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8" - (P2)

24" x 30" - BOX BASE 8inW, 8inF, Variable Ht F/n - 26" - (P1)

Default - Interior Dimensions

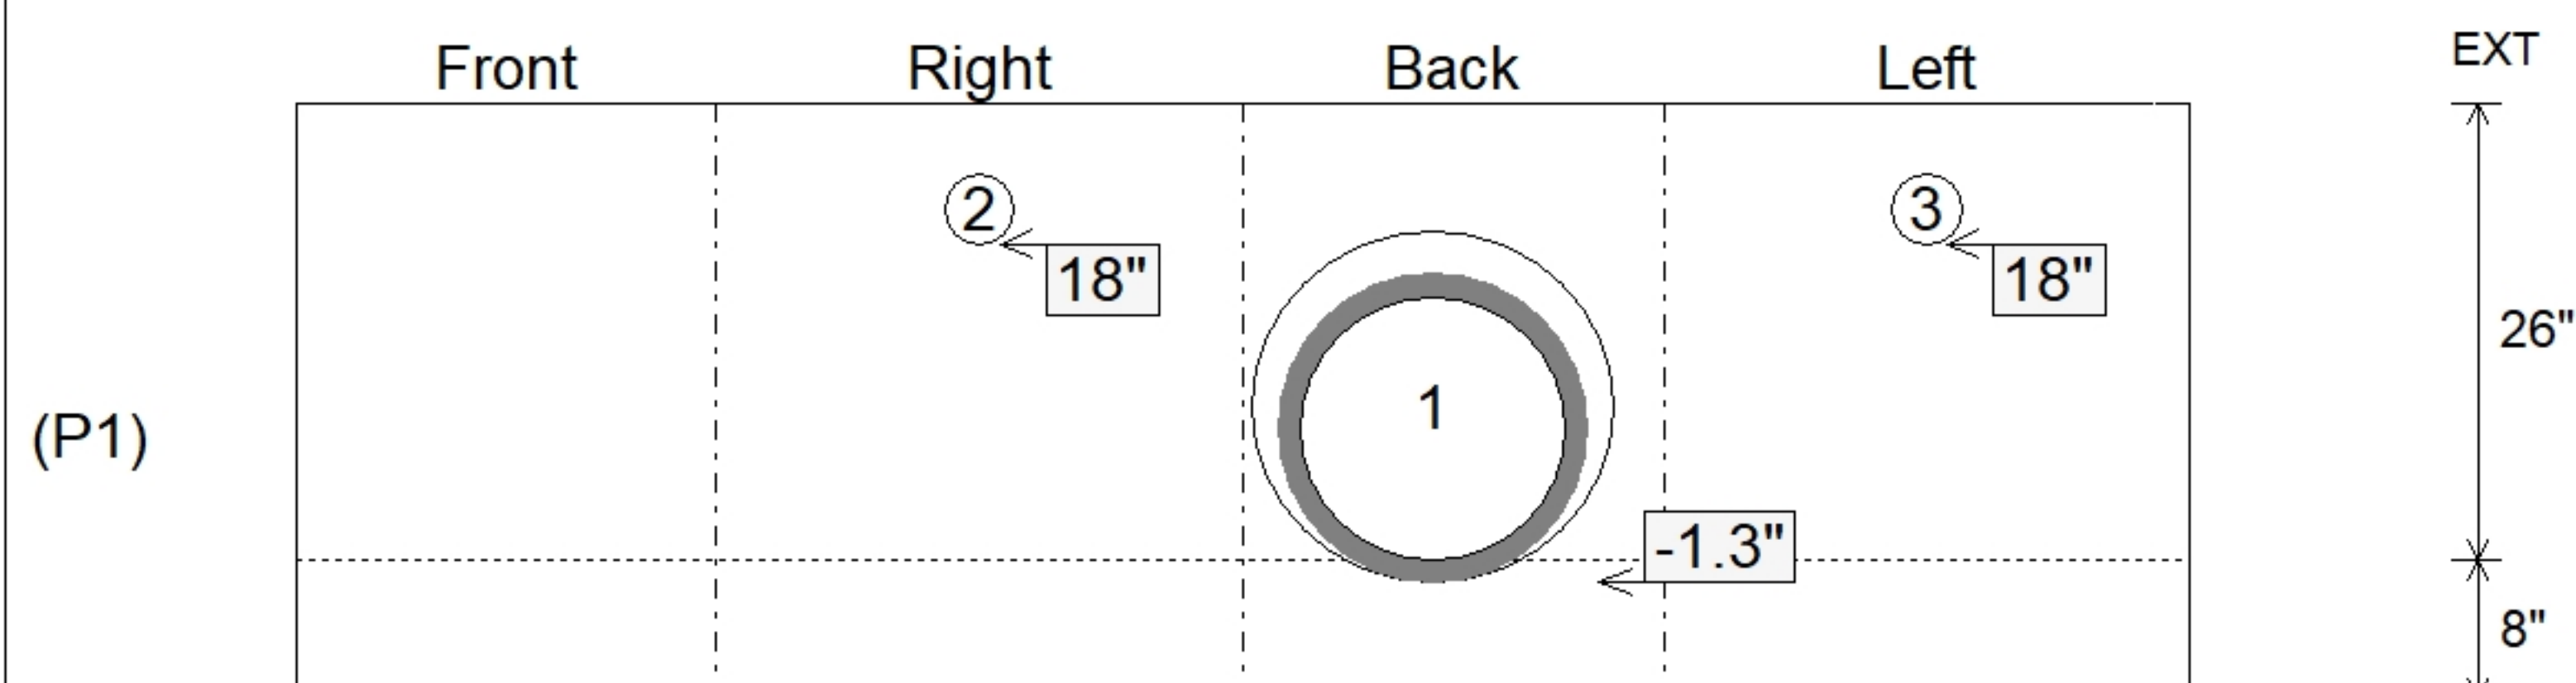

SUBMITTAL
APPROVED BY:
