


Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam





Slack: 0.12"

Structure Total: 16500 lb

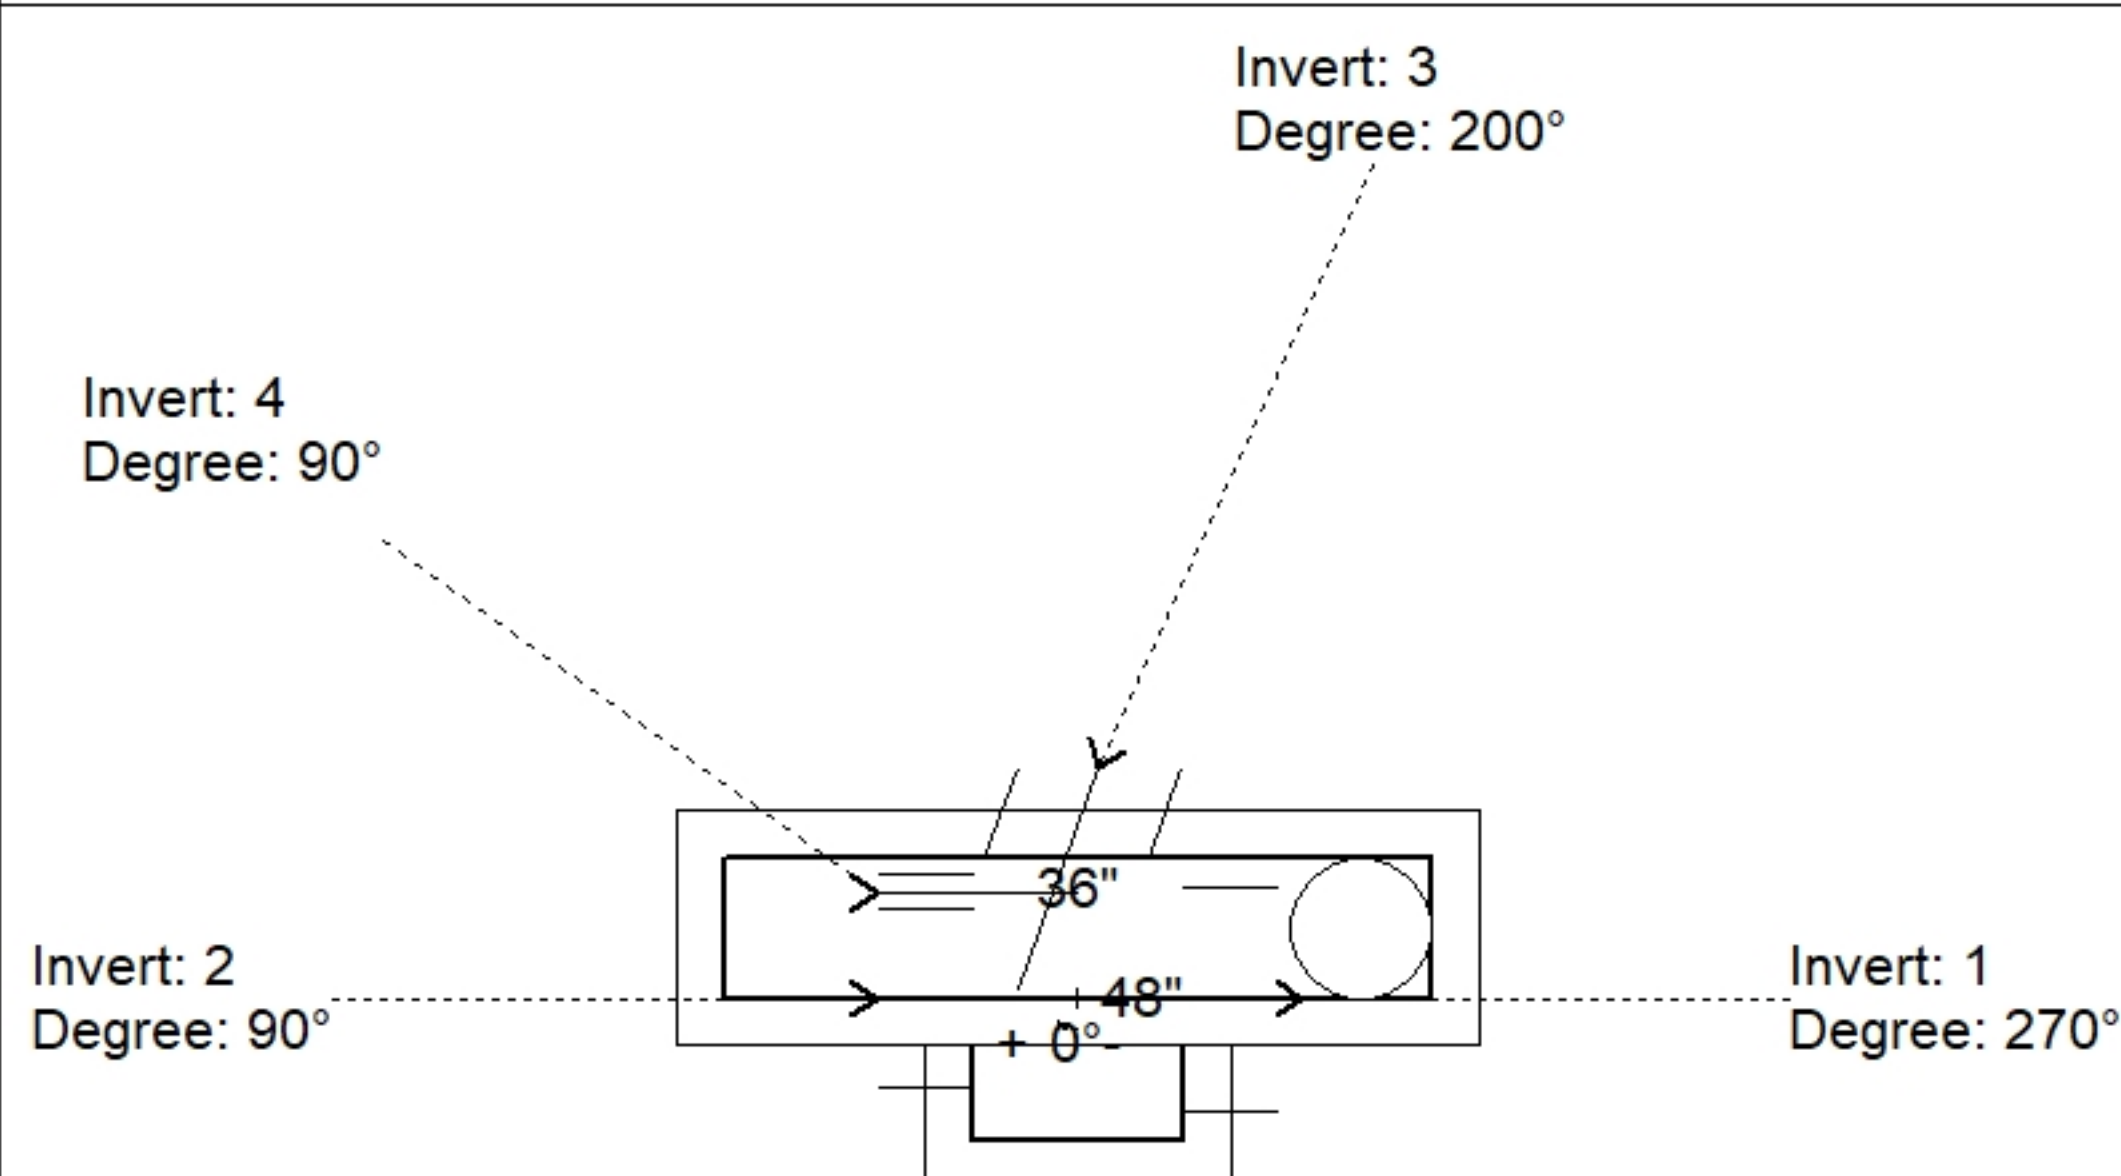

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	543.58'							
Reducer	540.403'							
Invert 1	537.07'	270°	30" HDPE	35.1"	38"	Hole 38	-2.55"	P1
Invert 2	537.57'	90°	24" HDPE	27.8"	30"	Hole 30	4.1"	P1
Invert 3	538.07'	200°	18" RCP B WALL	23"	26"	Hole 26	9.5"	P1
Invert 4	539.515'	90°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	28.94"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

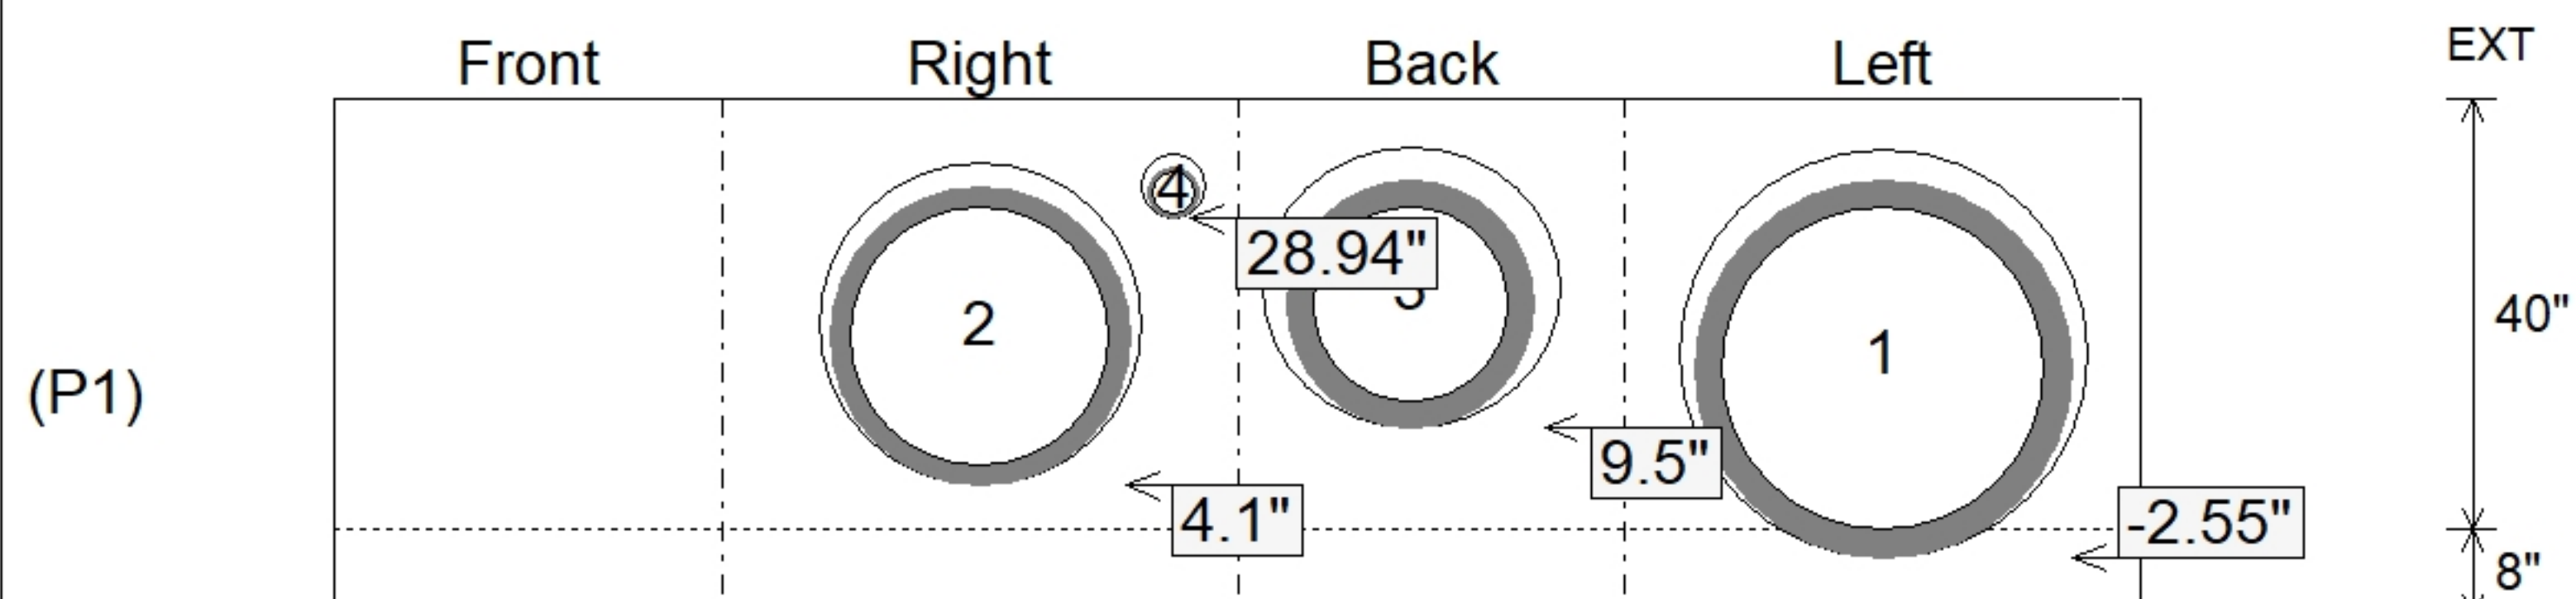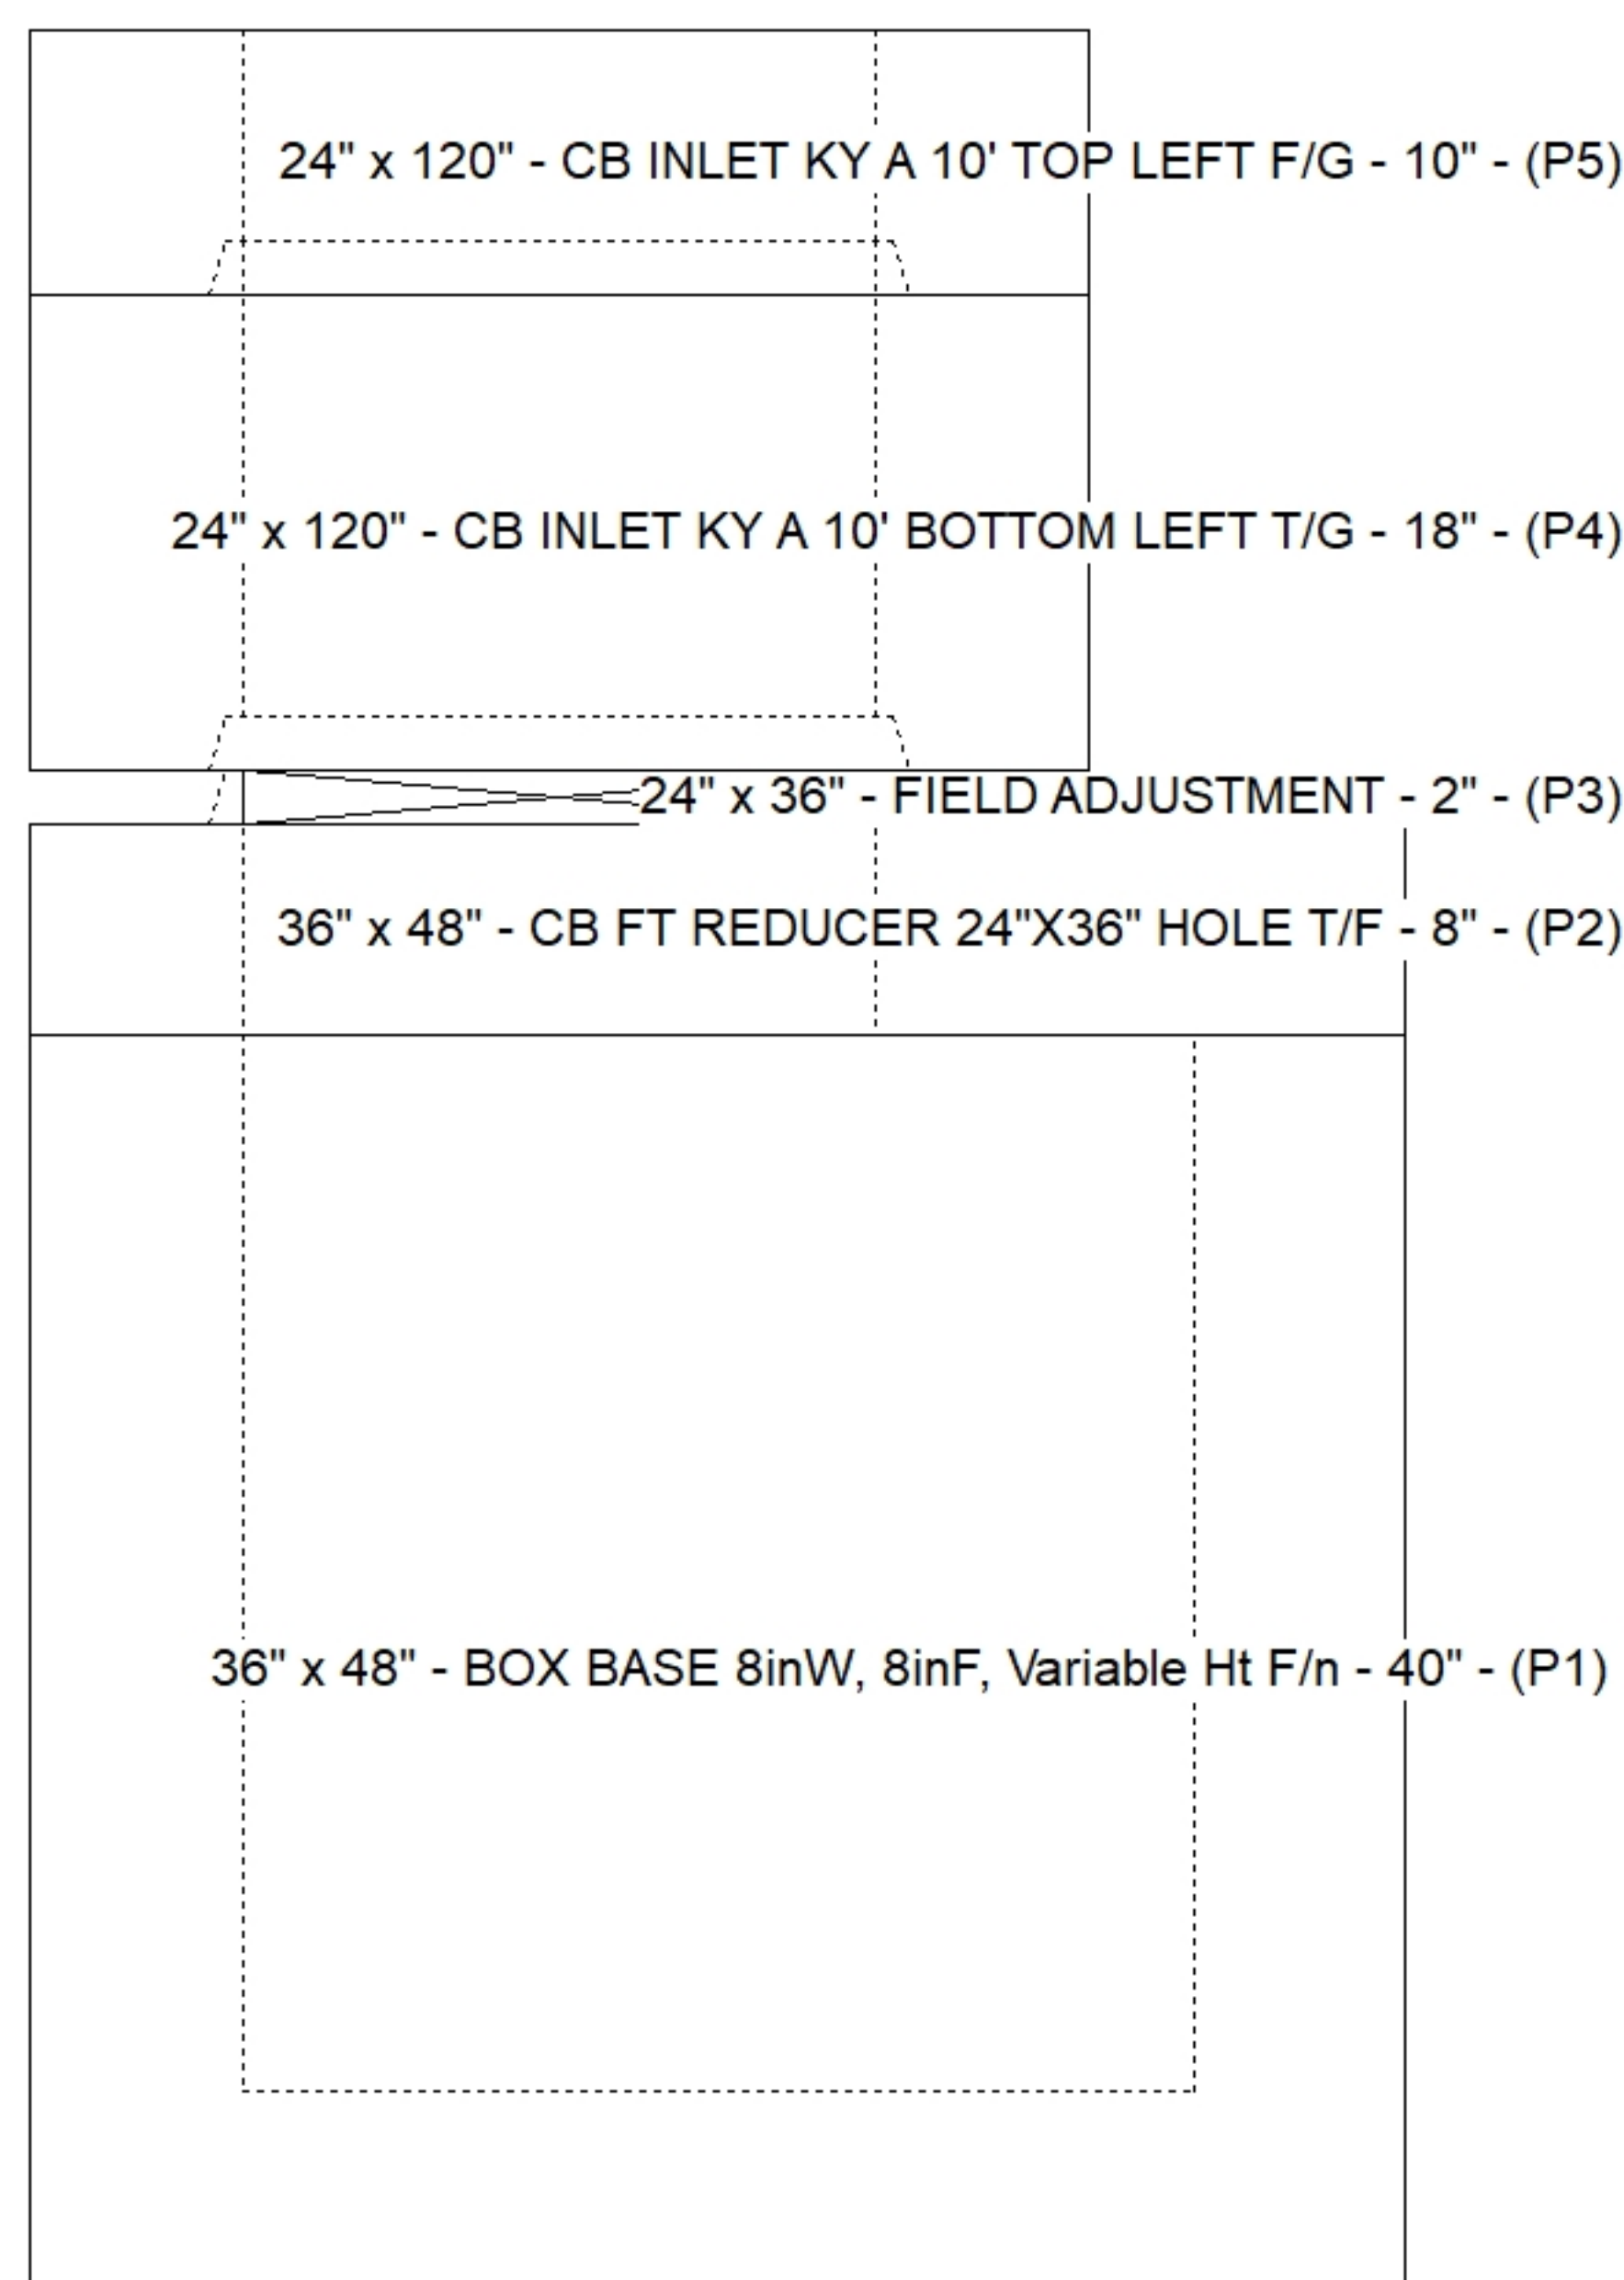

SUBMITTAL
APPROVED BY:
