

Contractor: Scotty's Contracting & Stone, LLC

PC:	C. Goff
TECH:	J. Horsley
Plant: Beaver Dam	



Size: 24" x 36"

Rim to Invert: 3.25'

Floor Height: 8"

Slack: 0"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P3) 15" x 27" - P.I.P. - BY OTHERS - 8"
P2) 24" x 36" - CB FLAT TOP 8"W w/15"x27" HOLE F/F - 8"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht F/n - 23"
1) CASTING - HOE KY-230-G F/G (GRADE)
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 20
2) Hole - 4

0 lb
1124 lb
3428 lb
237 lb
0 lb
0 lb
0 lb


Structure Total: 4789 lb

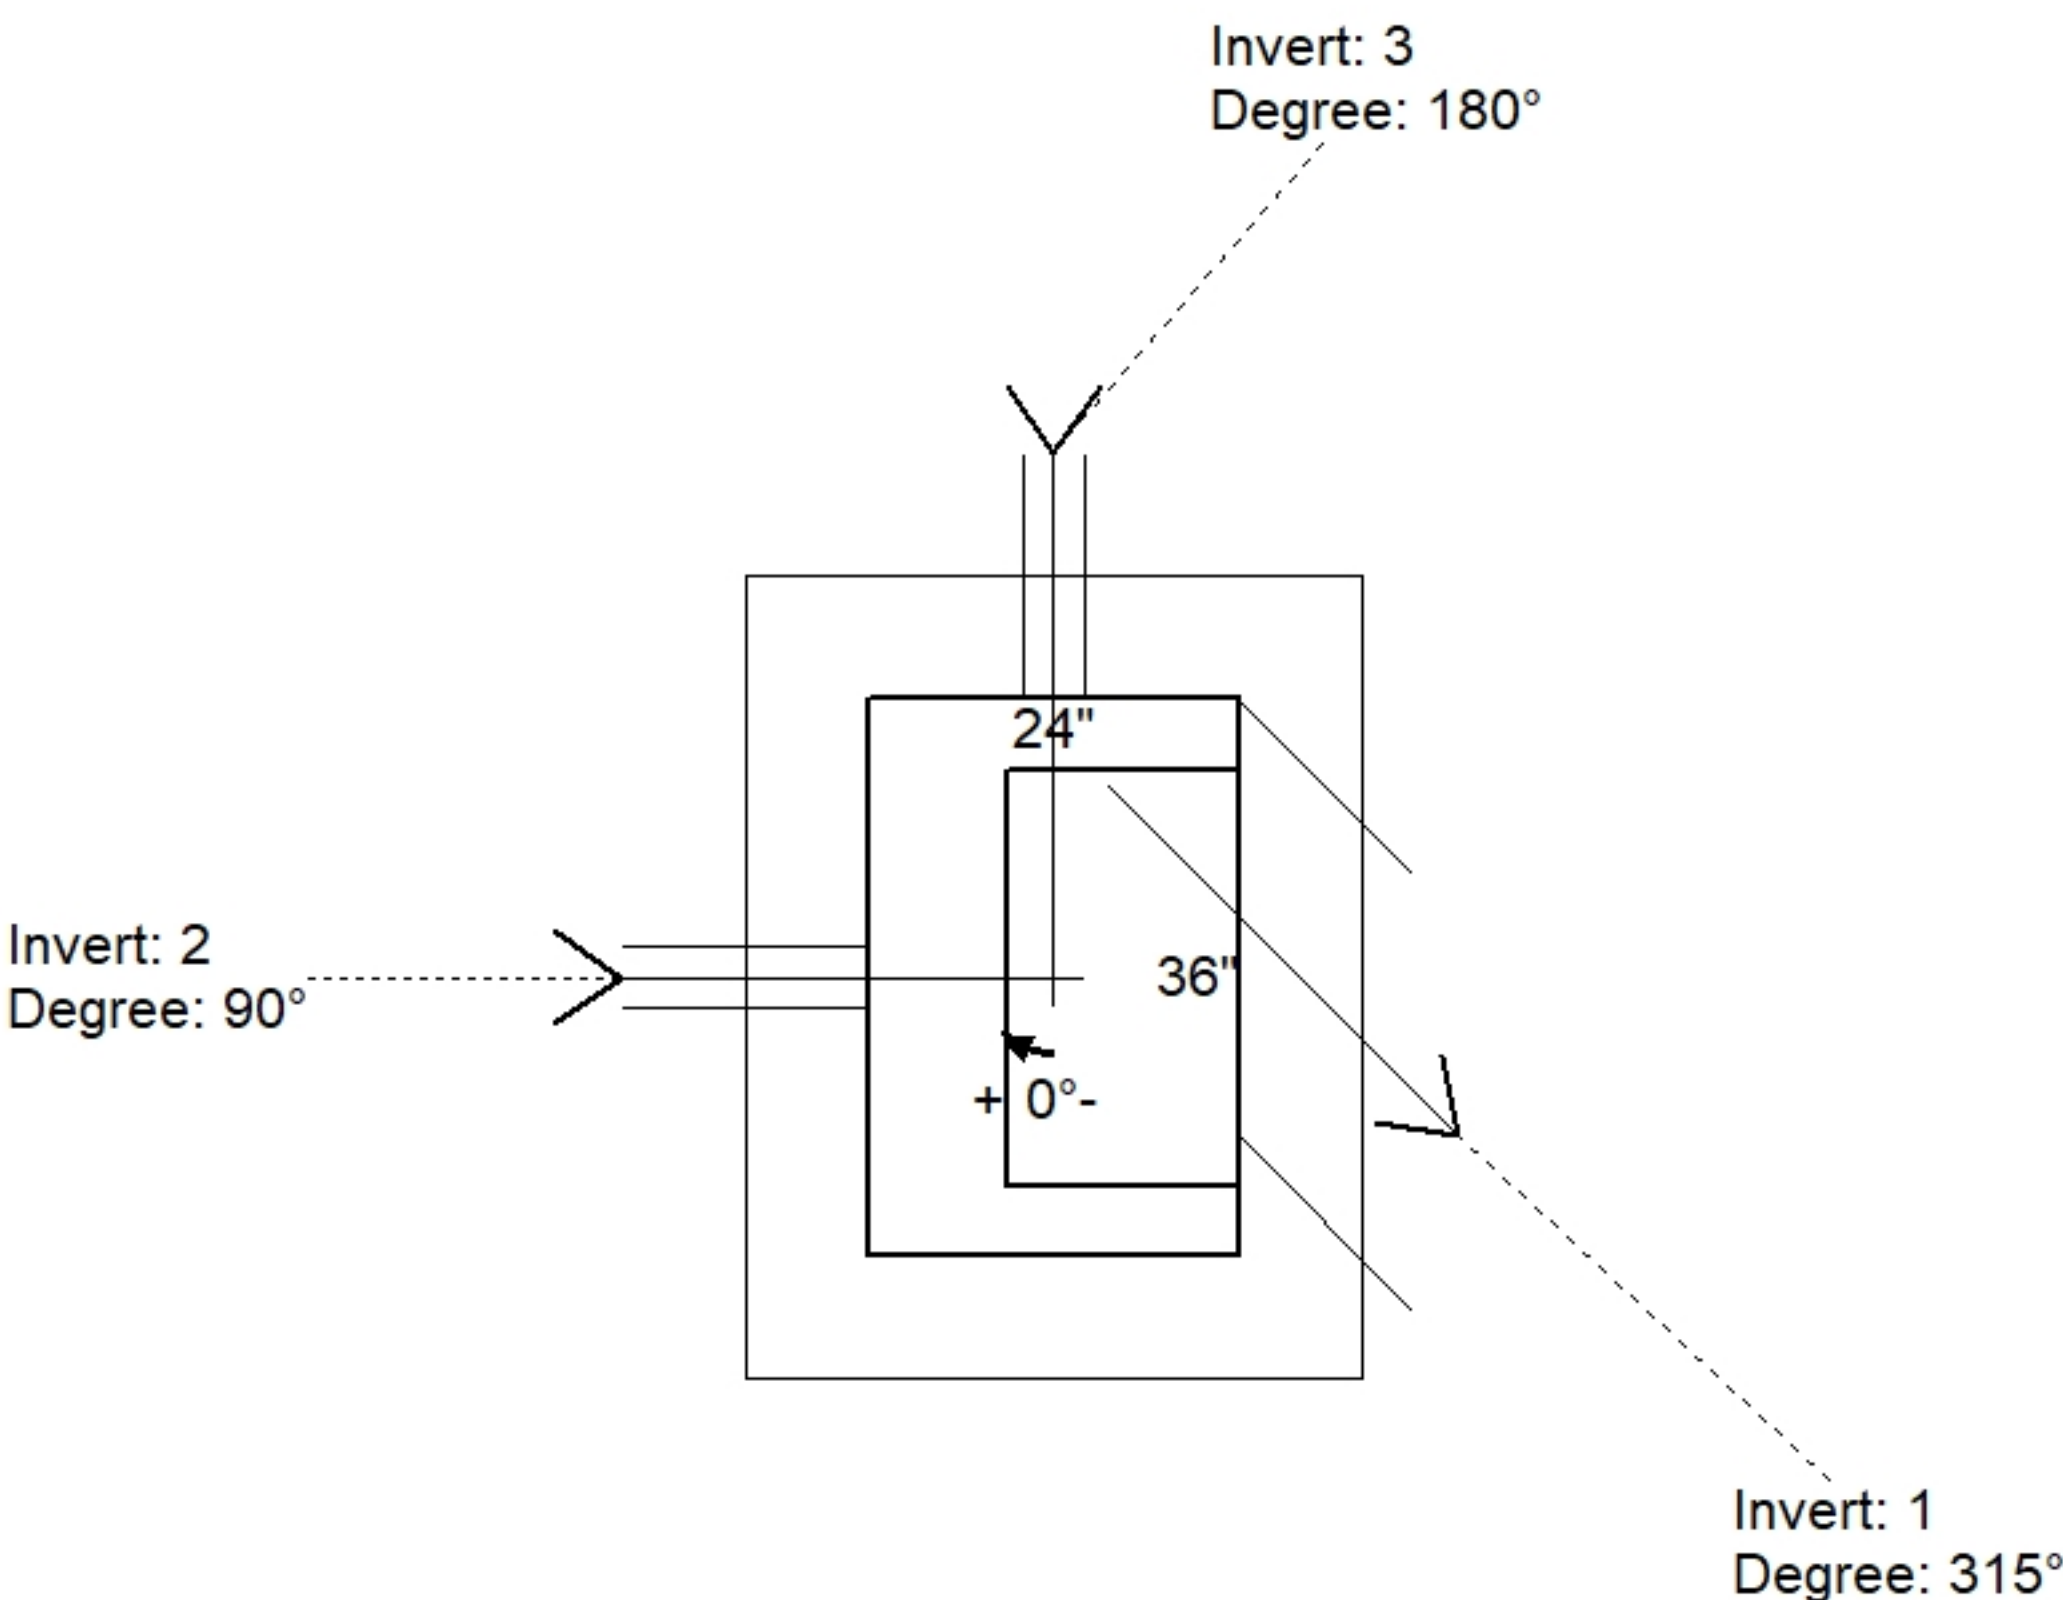

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	541.9'							
Reducer								
Invert 1	538.65'	315°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 2	539.75'	90°	4" WEEP HOLE	4"	4"	Hole 4	13.2"	P1
Invert 3	539.75'	180°	4" WEEP HOLE	4"	4"	Hole 4	13.2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

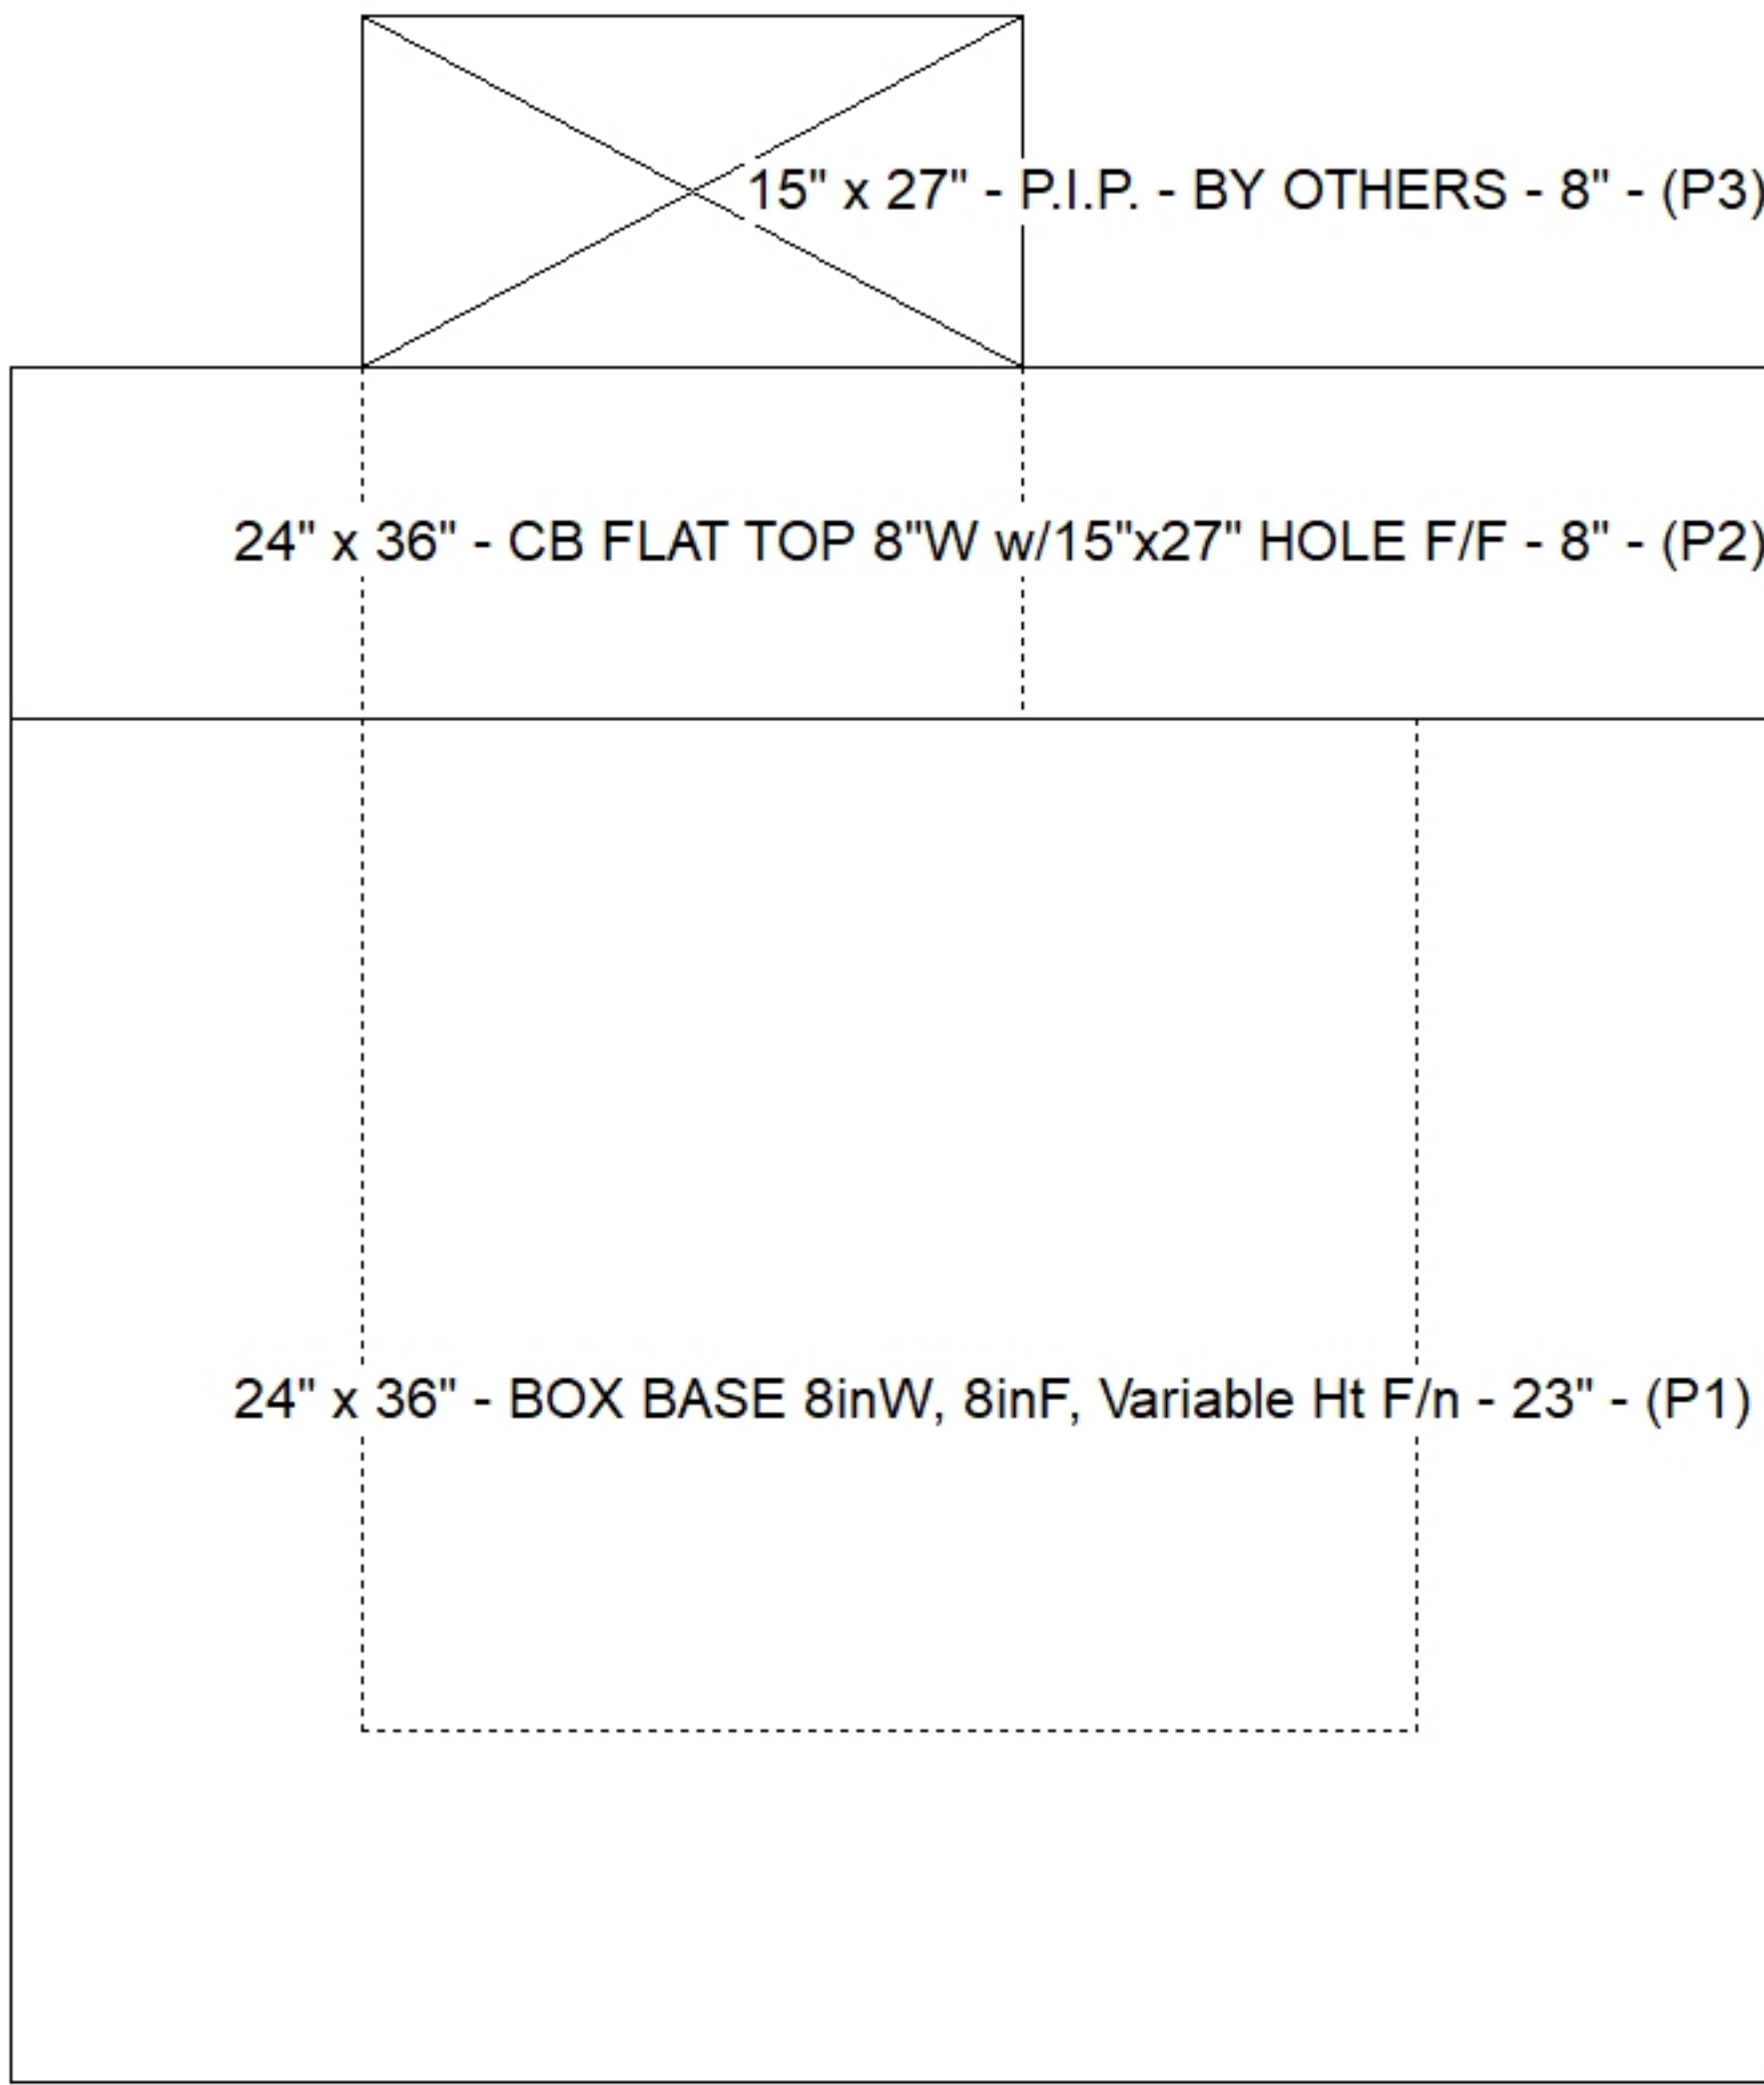

Default - Interior Dimensions

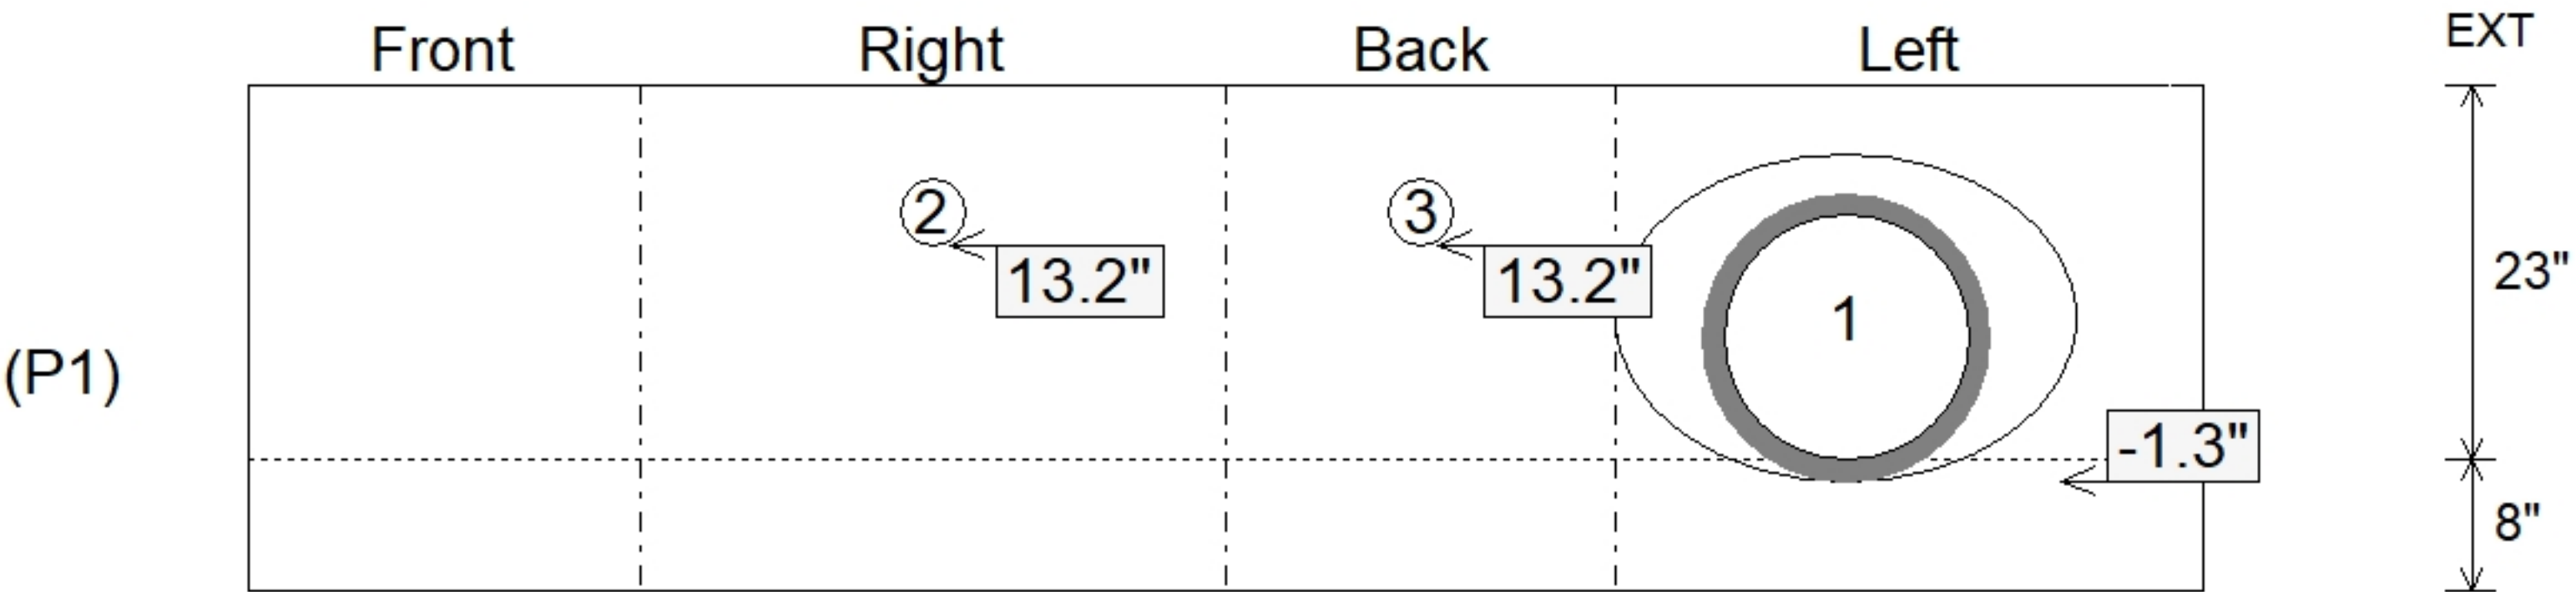

Submittal Drawing
7/30/2026 8:51:18 AM

SUBMITTAL
APPROVED BY:
