

Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam



Size: 24" x 60"

Rim to Invert: 4.88'

Floor Height: 8"



Slack: 0.06"

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


0 lb

Structure Total: 8206 lb

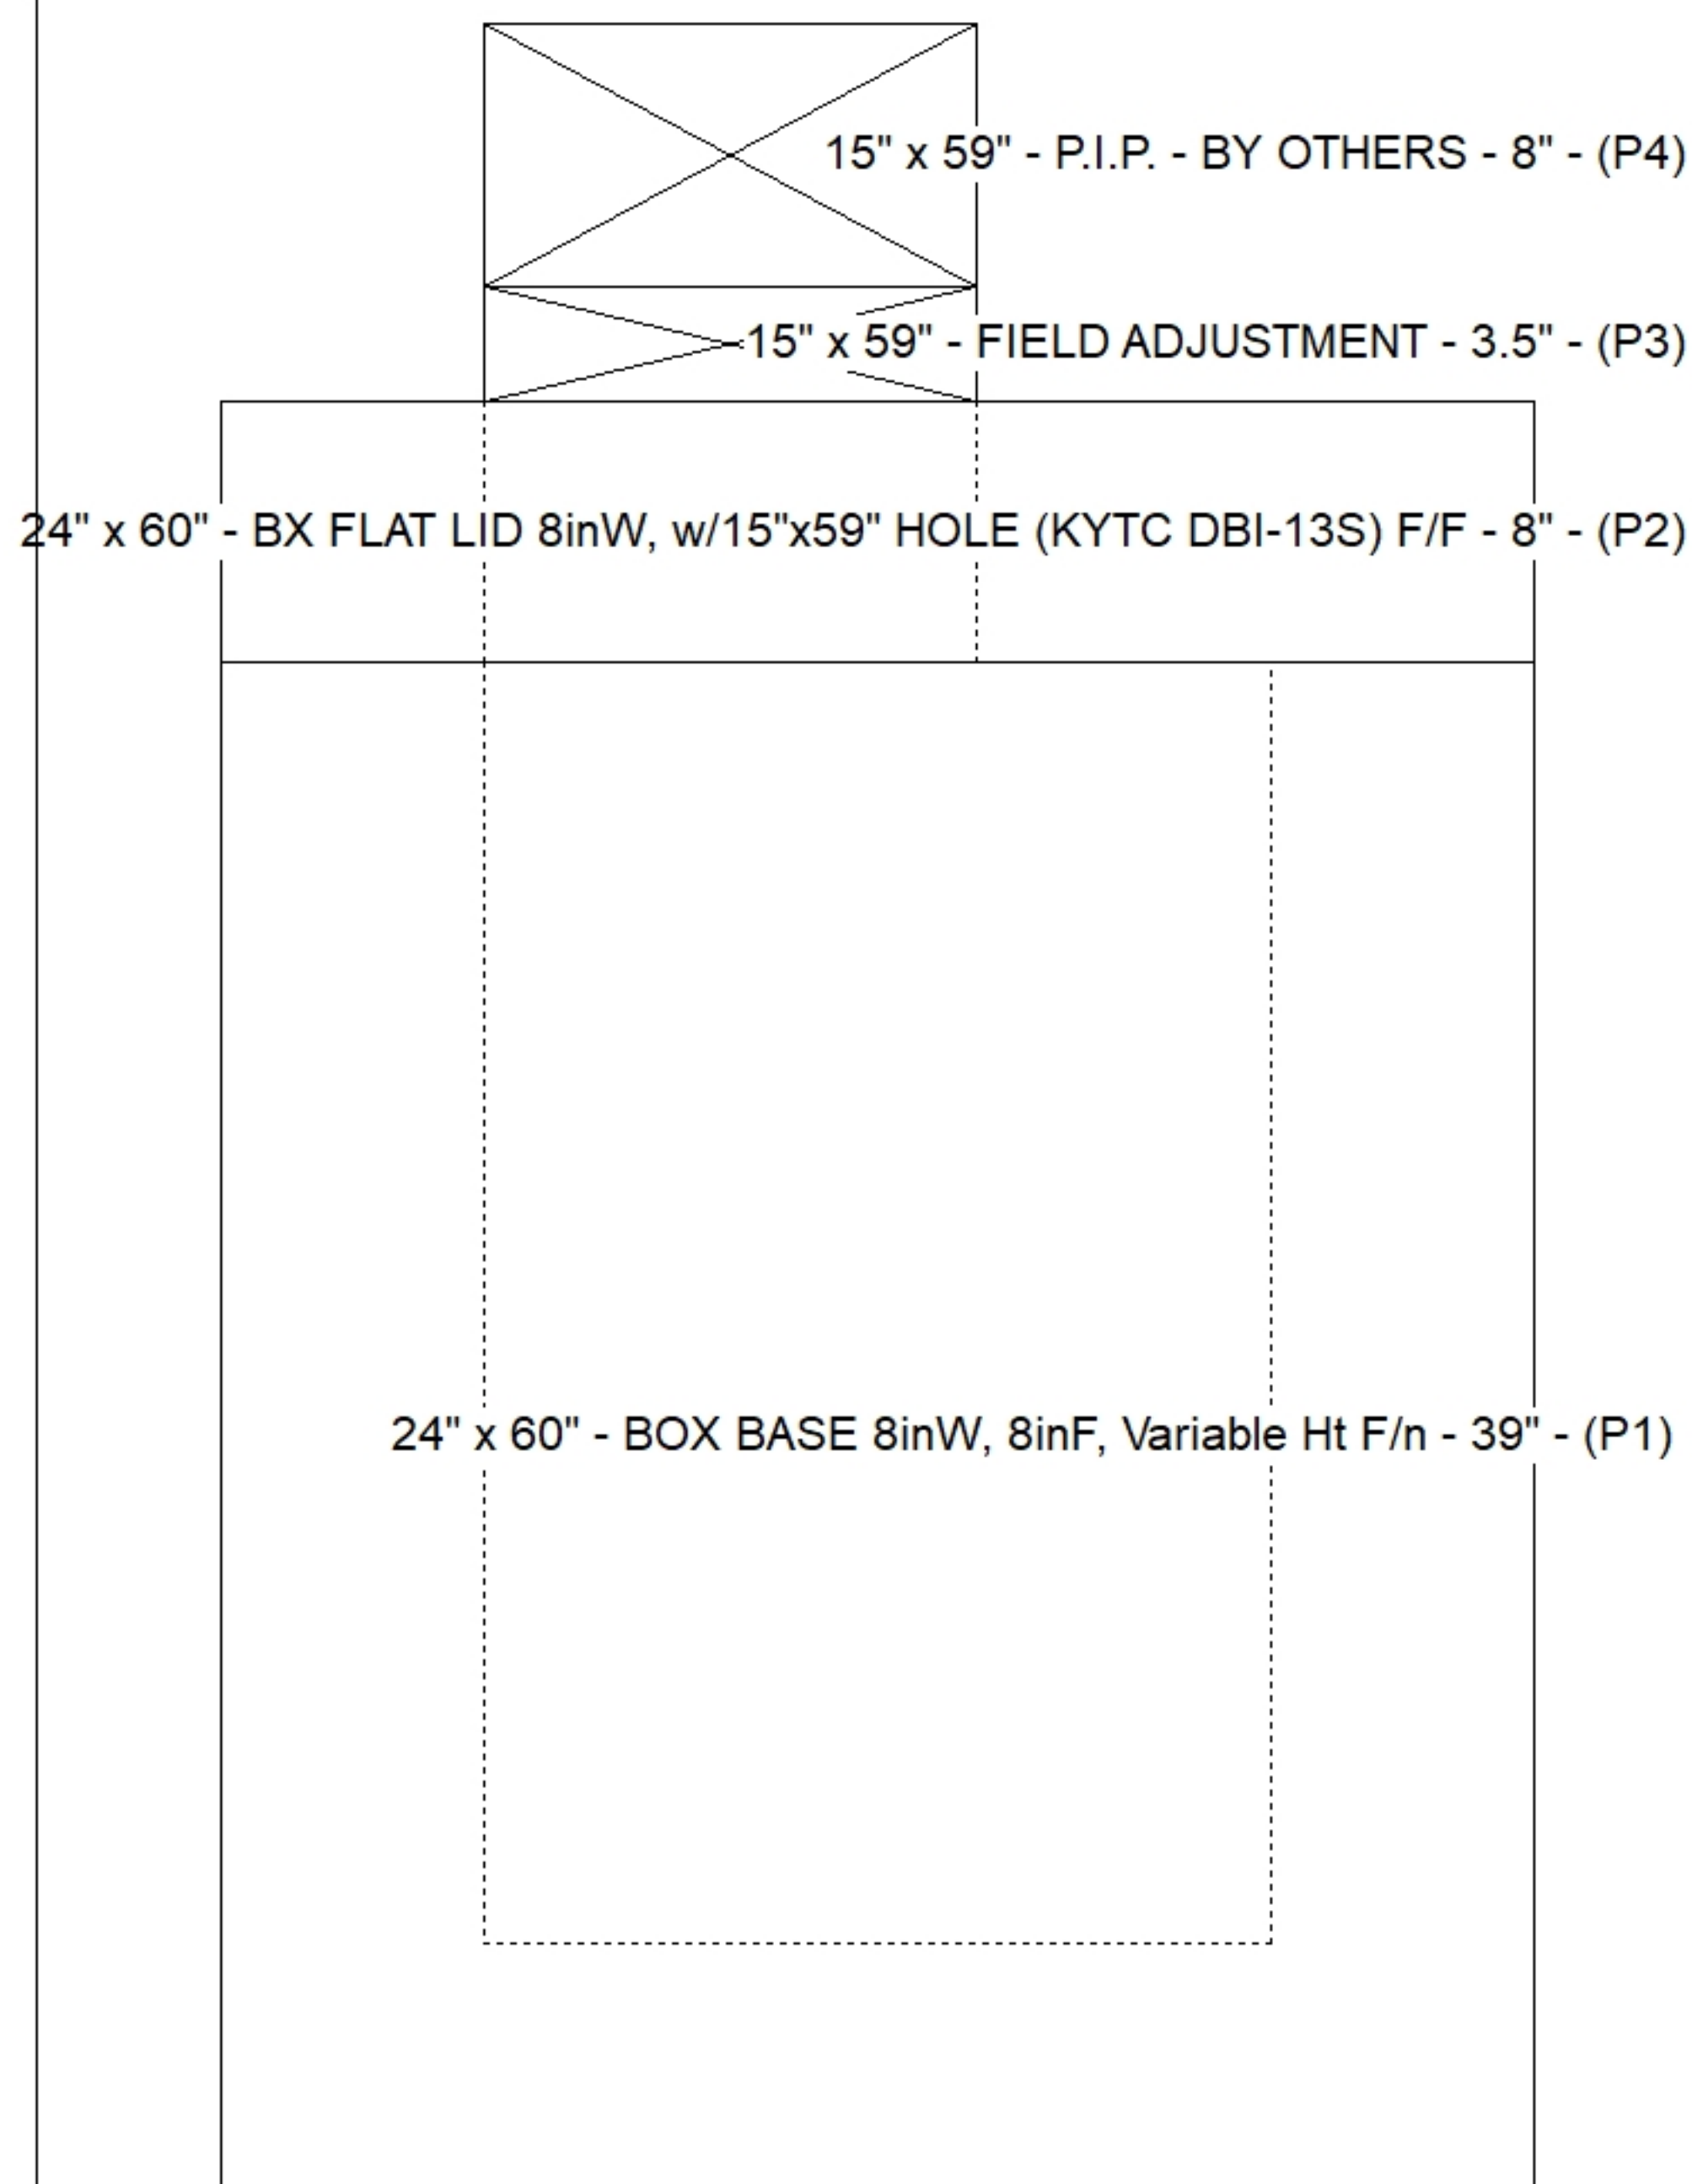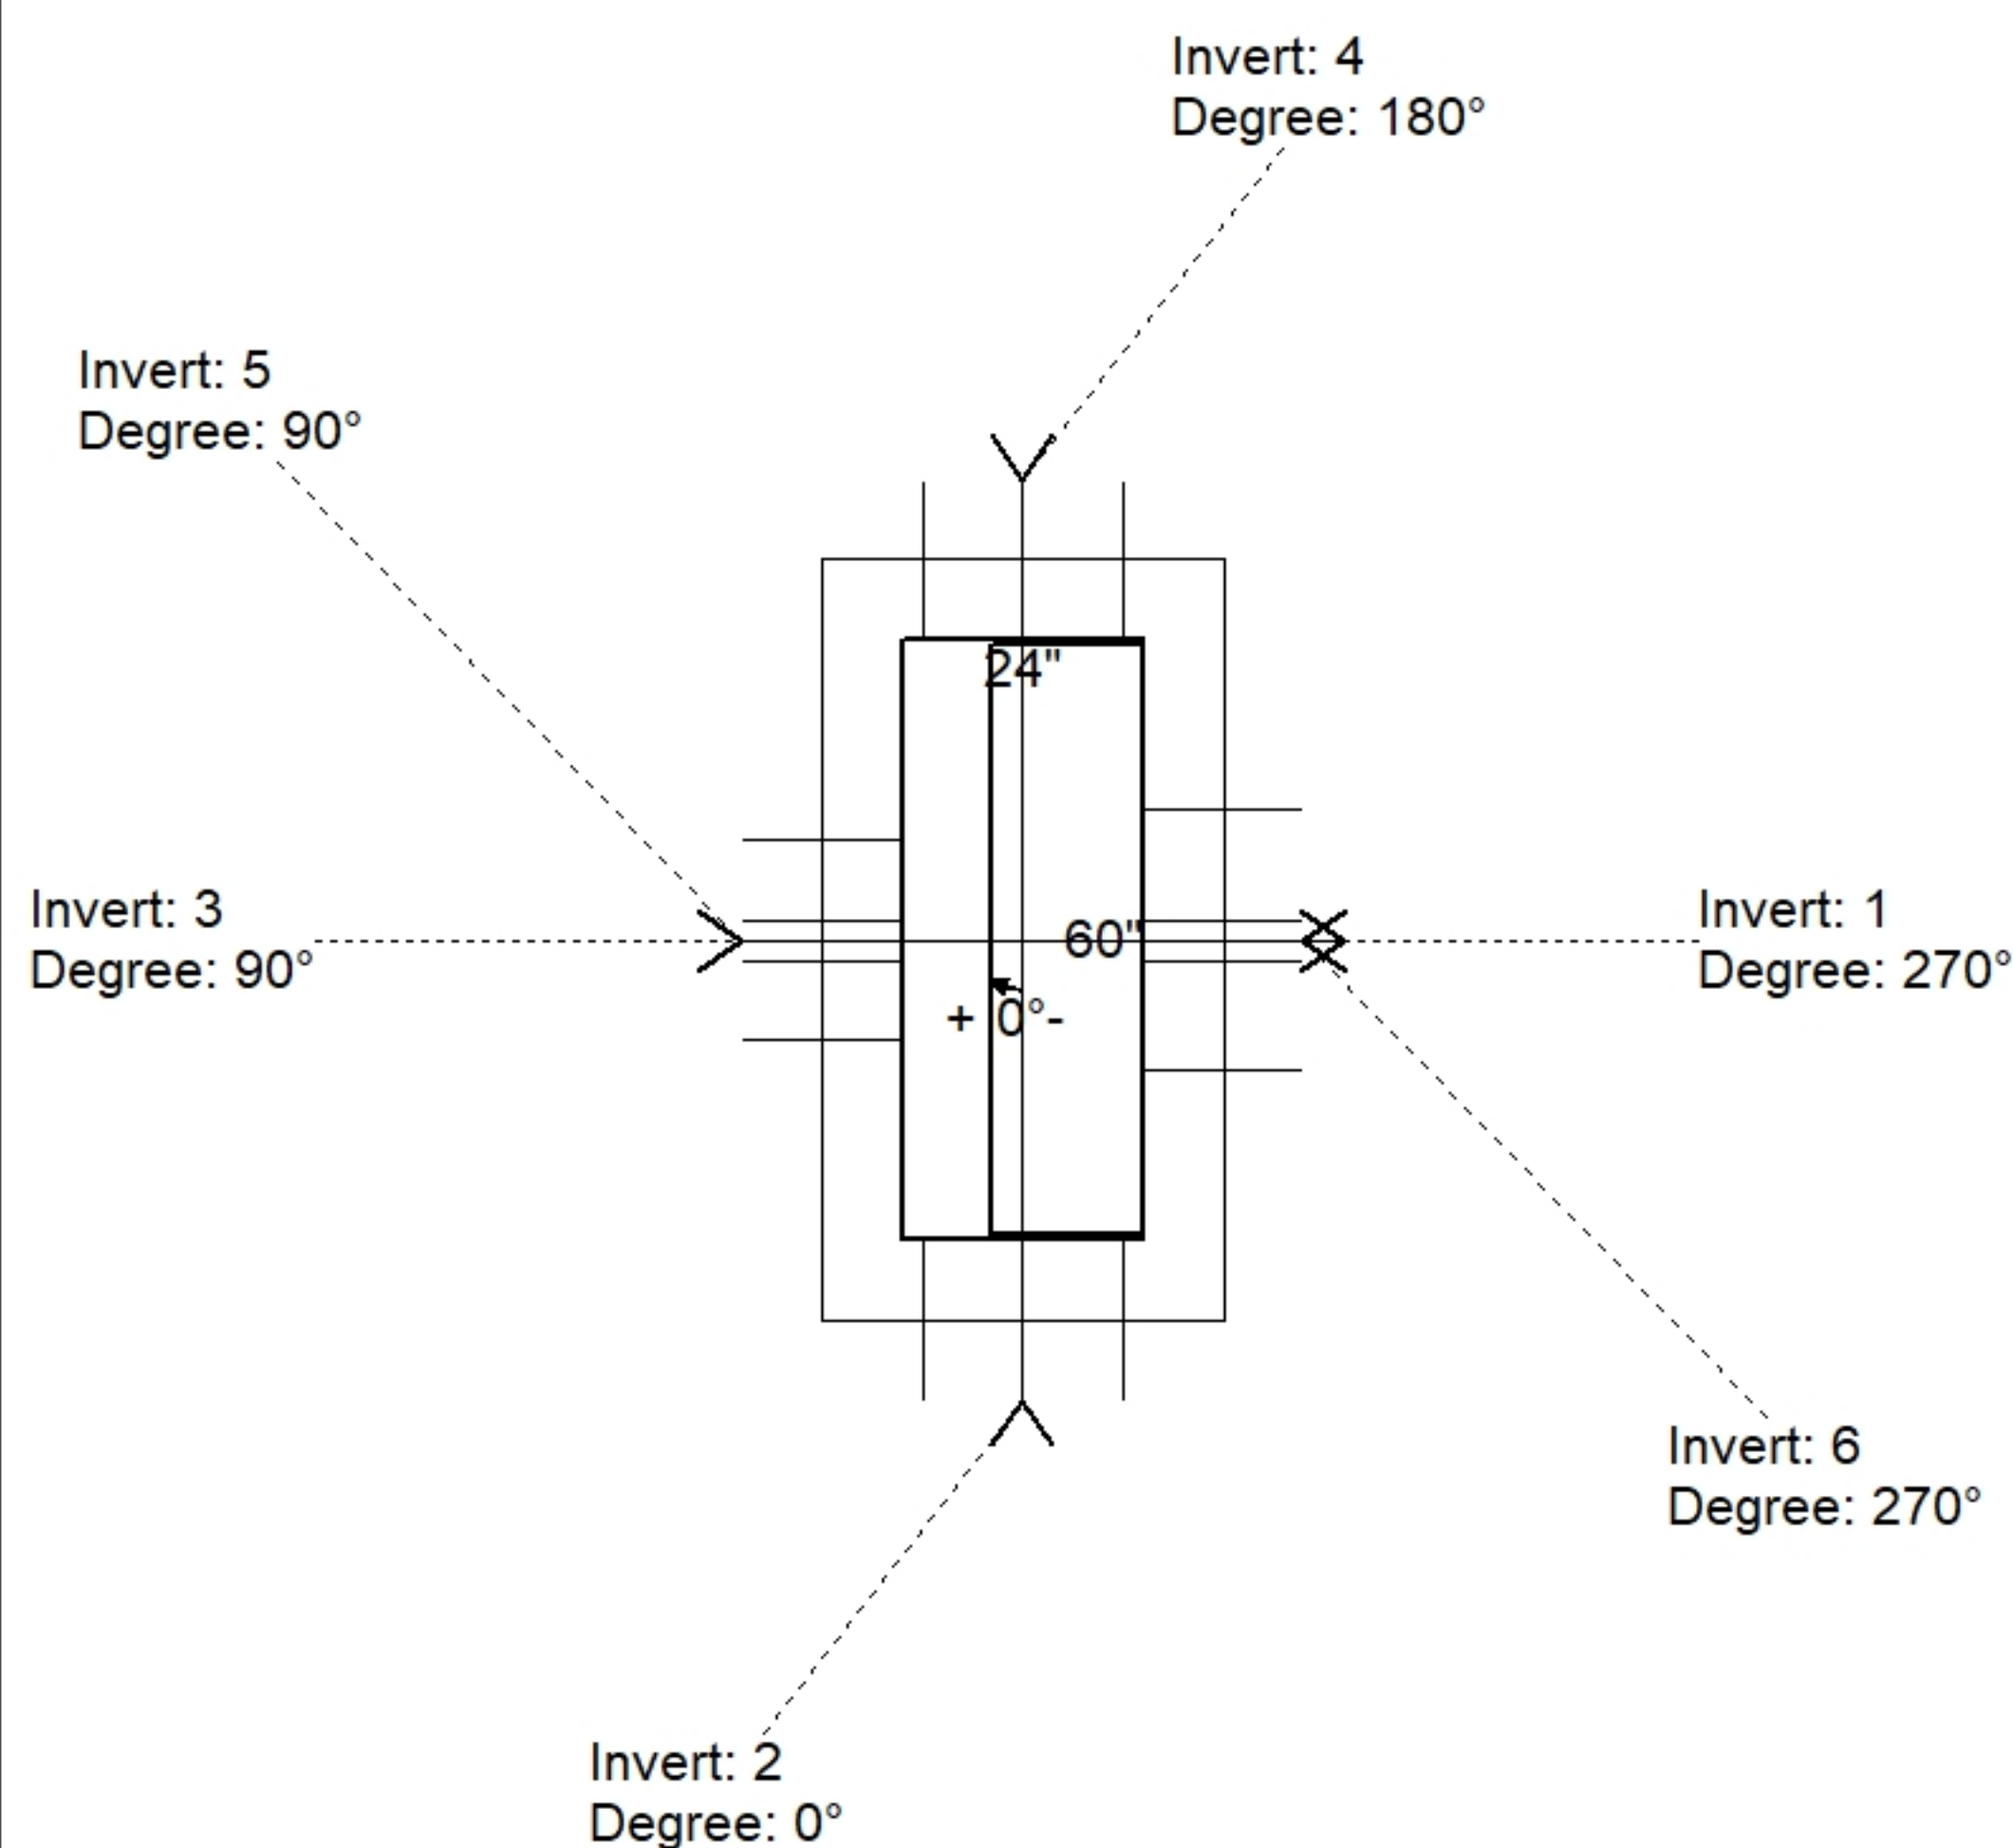

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	540.98'							
Reducer								
Invert 1	536.1'	270°	18" RCP B WALL	23"	26"	Hole 26	-2.5"	P1
Invert 2	536.35'	0°	15" HDPE	17.6"	20"	Hole 20	1.7"	P1
Invert 3	536.35'	90°	15" HDPE	17.6"	20"	Hole 20	1.7"	P1
Invert 4	536.35'	180°	15" HDPE	17.6"	20"	Hole 20	1.7"	P1
Invert 5	538.75'	90°	4" WEEP HOLE	4"	4"	Hole 4	31.8"	P1
Invert 6	538.75'	270°	4" WEEP HOLE	4"	4"	Hole 4	31.8"	P1
Invert 7								
Invert 8								

Default - Interior Dimensions

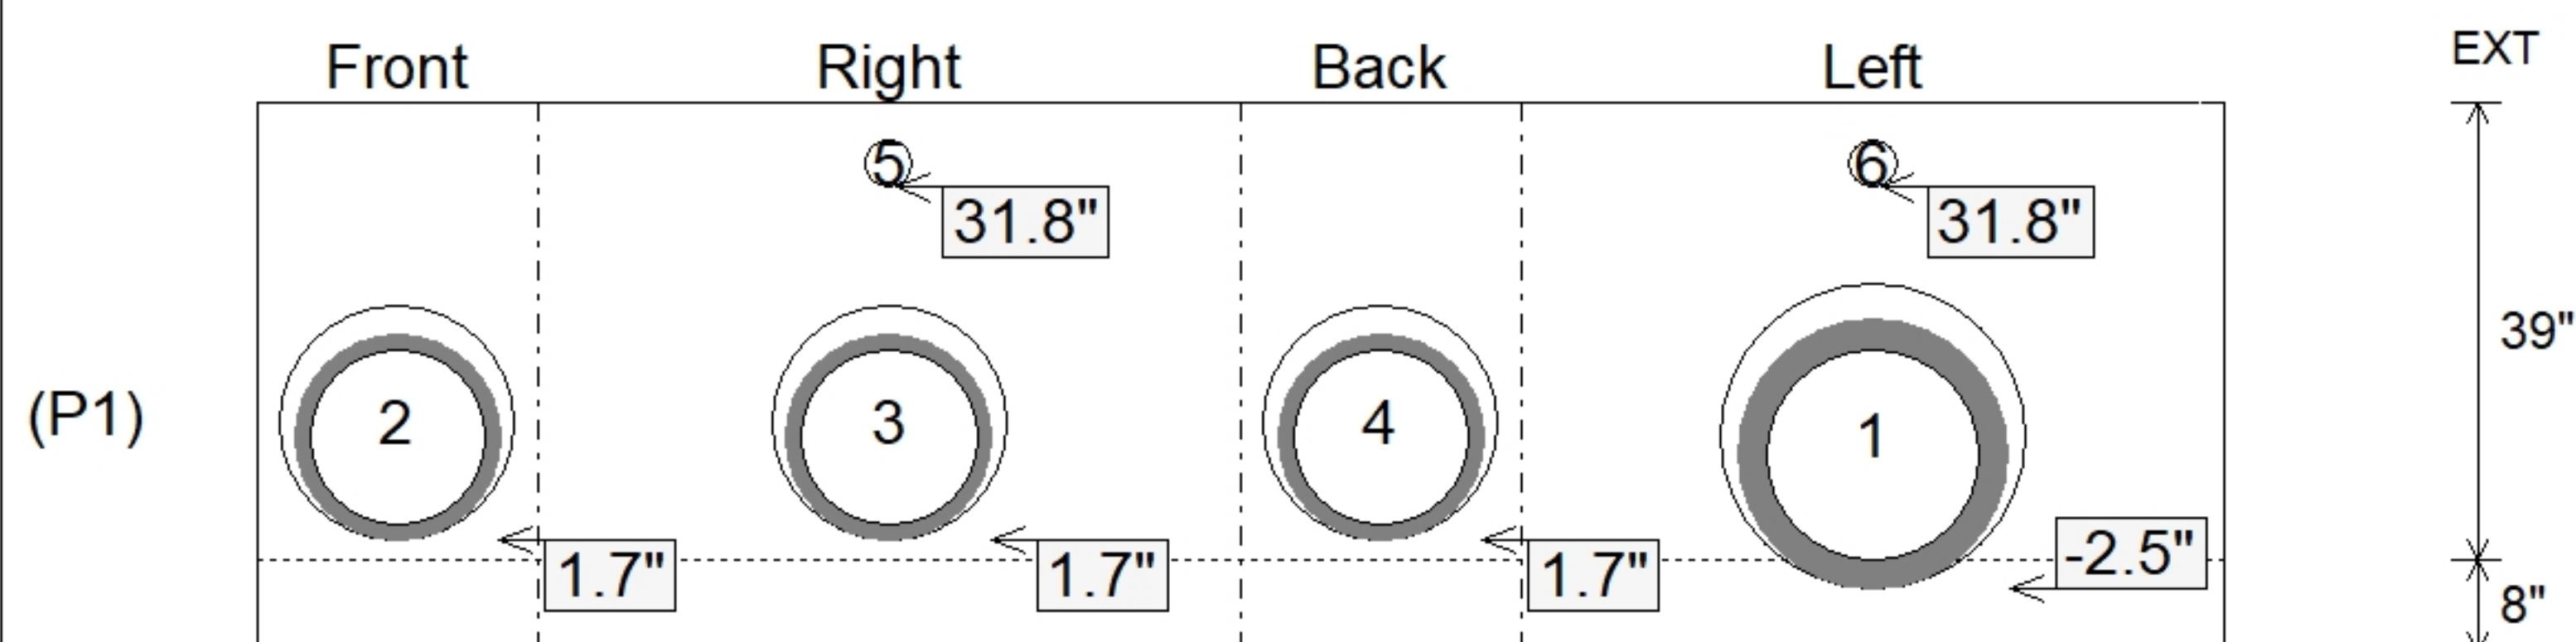

SUBMITTAL
APPROVED BY:
