




Weight (Net): 6625 lb
Volume (Net): 1.69cu.yd

Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 7/30/2026 8:55:42 AM		Tech: J. Horsley PC: C. Goff				
Structure ID: 259 (432+75 LT)											
P1		BX2460-08BA36		BOX BASE 8inW, 8inF F/n							
P4) 15" x 59" - P.I.P. - BY OTHERS - 8" P3) 15" x 59" - FIELD ADJUSTMENT - 3" P2) 24" x 60" - BX FLAT LID 8inW, w/15"x59" HOLE (KYTC DBI-13S) F/F - 8" P1) 24" x 60" - BOX BASE 8inW, 8inF F/n - 36" 1) CASTING - HOE KY-230-S F/G (SAG) 1) 24" x 60" - Conseal CS-102 1.00" 1) Hole - 20 2) Hole - 6					0 lb 0 lb 1461 lb 6625 lb 474 lb 0 lb 0 lb 0 lb ----- Structure Total: 8560 lb		Structure Notes: . **KYTC STATE PROJECT** 1. KYTC DBI TYPE 13S / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (2x JBS 3413 F&G's) 4. STUB #5 BARS 4" OUT TOP OF TOP SLAB (SPA AT 12" C/C) AROUND 15"x59" HOLE. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 543.1'		Rim to Invert: 4.61'		Slack: 0.32"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	538.49'	270°	38"	15" HDPE	17.6"	Hole 20	20"	20"	-1.3"	0"	
Invert 2	540.69'	90°	38"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	26"	0"	
Invert 3	540.69'	270°	38"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	26"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

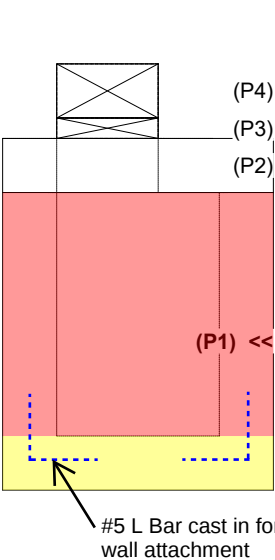

UPSIDE-DOWN VIEW (int. dimensions)


2-Stage Pour Required

Second pour drawing

First pour weight = 2,040 LBS

Second pour weight = 4,585 LBS

INSIDE WALL DIMENSIONS

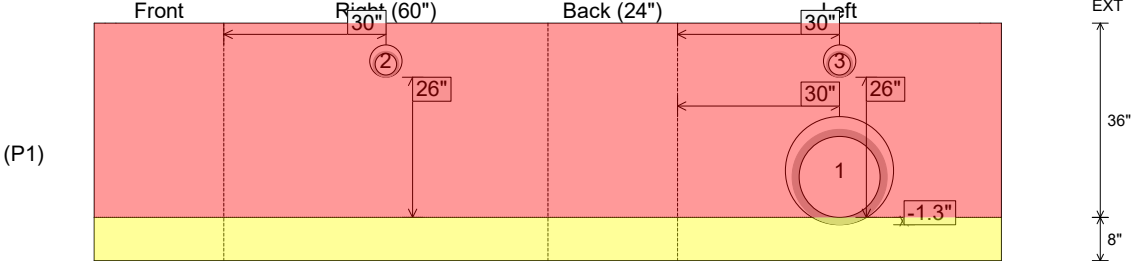

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 36" Height (Ext): 44"	Weight (Net): 6625 lb Volume (Net): 1.69cu.yd
----------------------------------	-------------------------------	--	--	--
