


Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC				Plant: Beaver Dam 7/30/2026 8:55:43 AM		Tech: J. Horsley PC: C. Goff						
Structure ID: 260 (433+35 LT)												
P1 BX2460-08BAVF				BOX BASE 8inW, 8inF, Variable Ht F/n								
P4) 15" x 59" - P.I.P. - BY OTHERS - 8" P3) 15" x 59" - FIELD ADJUSTMENT - 3.5" P2) 24" x 60" - BX FLAT LID 8inW, w/15"x59" HOLE (KYTC DBI-13S) F/F - 8" P1) 24" x 60" - BOX BASE 8inW, 8inF, Variable Ht F/n - 40" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 24" x 60" - Conseal CS-102 1.00" 2) Hole - 20 2) Hole - 4						0 lb 0 lb 1461 lb 6918 lb 206 lb 0 lb 0 lb 0 lb ----- Structure Total: 8585 lb		Structure Notes: **KYTC STATE PROJECT** 1. KYTC DBI TYPE 13S / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (2x JBS 3413 F&G's) 4. STUB #5 BARS 4" OUT TOP OF TOP SLAB (SPA AT 12" C/C) AROUND 15"x59" HOLE. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 543.21'				Rim to Invert: 4.98'		Slack: 0.26"		Sump: 0"		Step Position:		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	538.23'	330°	15.83"	15" HDPE	17.6"	Hole 20	20"	23.094"	-1.3"	15.388"		
Invert 2	538.23'	115°	41.809"	15" HDPE	17.6"	Hole 20	20"	22.068"	-1.3"	-5"		
Invert 3	540.73'	90°	38"	4" WEEP HOLE	4"	Hole 4	4"	4"	30"	0"		
Invert 4	540.73'	270°	38"	4" WEEP HOLE	4"	Hole 4	4"	4"	30"	0"		
Invert 5												
Invert 6												
Invert 7												
Invert 8												

RIGHT-SIDE UP VIEW (int. dimensions)

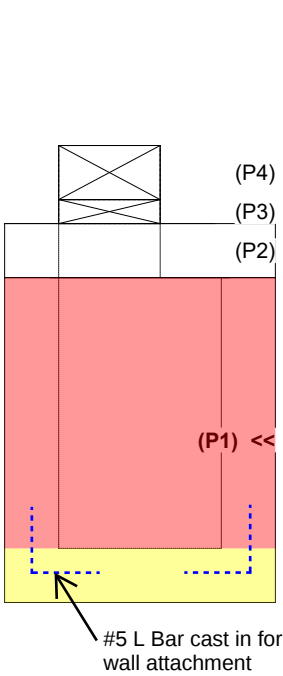


UPSIDE-DOWN VIEW (int. dimensions)

2-Stage Pour Required

First pour drawing
First pour weight = 2,040 LBS
Second pour weight = 4,878 LBS


INSIDE WALL DIMENSIONS

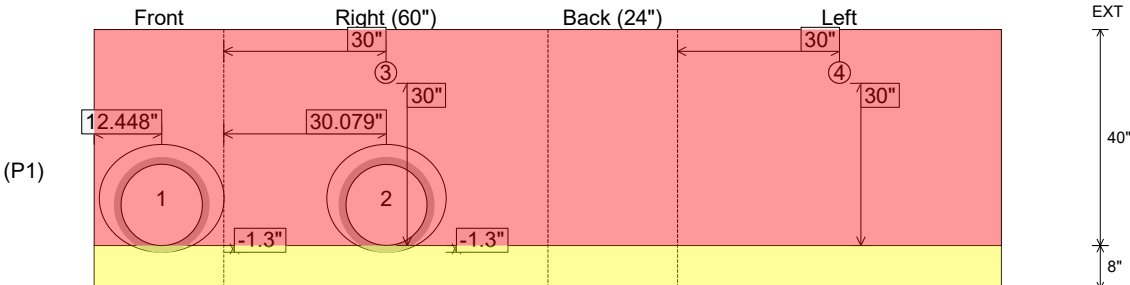

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 40" Height (Ext): 48"	Weight (Net): 6918 lb Volume (Net): 1.77cu.yd
----------------------------------	-------------------------------	--	--	--

Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 7/30/2026 8:55:43 AM		Tech: J. Horsley PC: C. Goff				
Structure ID: 260 (433+35 LT)											
P1		BX2460-08BAVF		BOX BASE 8inW, 8inF, Variable Ht F/n							
P4) 15" x 59" - P.I.P. - BY OTHERS - 8" P3) 15" x 59" - FIELD ADJUSTMENT - 3.5" P2) 24" x 60" - BX FLAT LID 8inW, w/15"x59" HOLE (KYTC DBI-13S) F/F - 8" P1) 24" x 60" - BOX BASE 8inW, 8inF, Variable Ht F/n - 40" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 24" x 60" - Conseal CS-102 1.00" 2) Hole - 20 2) Hole - 4						0 lb 0 lb 1461 lb 6918 lb 206 lb 0 lb 0 lb 0 lb		Structure Notes: **KYTC STATE PROJECT** 1. KYTC DBI TYPE 13S / ASTM C-913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (2x JBS 3413 F&G's) 4. STUB #5 BARS 4" OUT TOP OF TOP SLAB (SPA AT 12" C/C) AROUND 15"x59" HOLE. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT). - WALLS (As .31) #5 BARS AT 12" C.C.E.W.. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 543.21' Rim to Invert: 4.98' Slack: 0.26" Sump: 0" Step Position:						Structure Total: 8585 lb					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	538.23'	330°	15.83"	15" HDPE	17.6"	Hole 20	20"	23.094"	-1.3"	15.388"	
Invert 2	538.23'	115°	41.809"	15" HDPE	17.6"	Hole 20	20"	22.068"	-1.3"	-5"	
Invert 3	540.73'	90°	38"	4" WEEP HOLE	4"	Hole 4	4"	4"	30"	0"	
Invert 4	540.73'	270°	38"	4" WEEP HOLE	4"	Hole 4	4"	4"	30"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

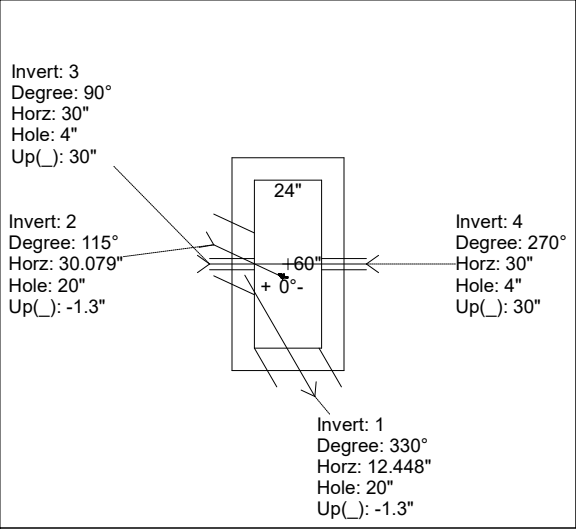


UPSIDE-DOWN VIEW (int. dimensions)

2-Stage Pour Required

Second pour drawing
First pour weight = 2,040 LBS
Second pour weight = 4,878 LBS

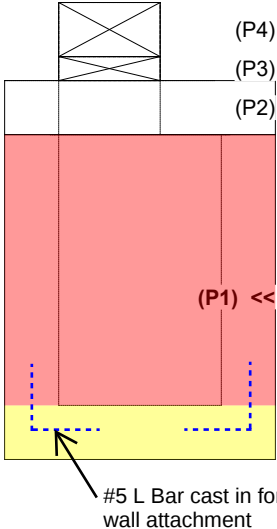

INSIDE WALL DIMENSIONS

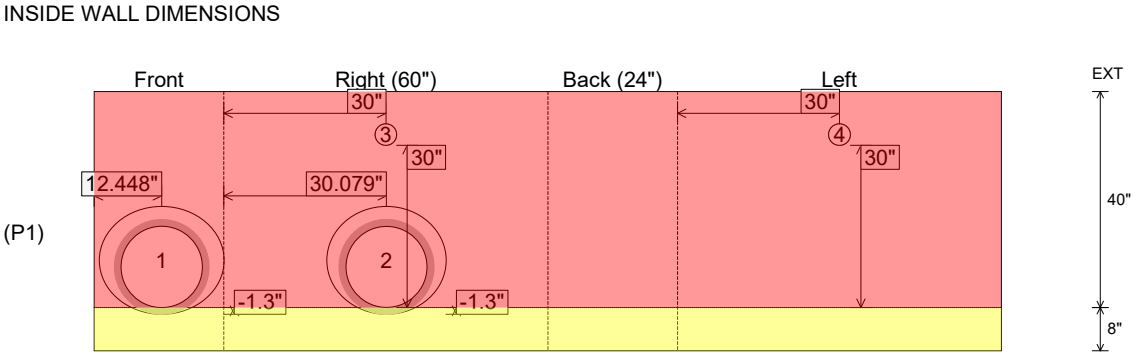

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 40" Height (Ext): 48"	Weight (Net): 6918 lb Volume (Net): 1.77cu.yd
----------------------------------	-------------------------------	--	--	--
