



Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC					Plant: Beaver Dam 7/30/2026 8:59:19 AM		Tech: J. Horsley PC: C. Goff						
Structure ID: 264 (434+55 RT)													
P4		BX2436-08R48		BOX RISER 8inW F/G									
P7) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P6) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P5) 24" x 36" - FIELD ADJUSTMENT - 4.5" P4) 24" x 36" - BOX RISER 8inW F/G - 48" P3) 24" x 36" - BOX RISER 8inW T/G - 18" P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE T/F - 8" P1) 36" x 48" - BOX BASE 8inW, 8inF F/n - 60" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 36" x 48" - Conseal CS-102 1.00" 3) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 44 1) Hole - 20 1) Hole - 6						3400 lb 5270 lb 0 lb 4668 lb 1837 lb 1654 lb 8248 lb 206 lb 0 lb 0 lb 0 lb 0 lb 0 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. HOE KY-206 F/C CAST INTO TOP SLAB. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT) - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 546.62' Rim to Invert: 13.91' Slack: 0.42" Sump: 0" Step Position:						Structure Total: 25282 lb							
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1													
Invert 2	540.97'	0°	20"	15" HDPE	17.6"	Hole 20	20"	20"	9.82"	0"			
Invert 3													
Invert 4	542.83'	270°	26"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	33.04"	0"			
Invert 5													
Invert 6													
Invert 7													
Invert 8													

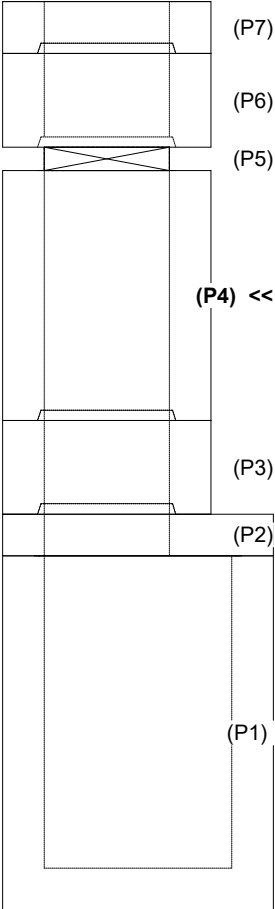


(P7)
(P6)
(P5)
(P4) <<
(P3)
(P2)
(P1)

RIGHT-SIDE UP VIEW (int. dimensions)

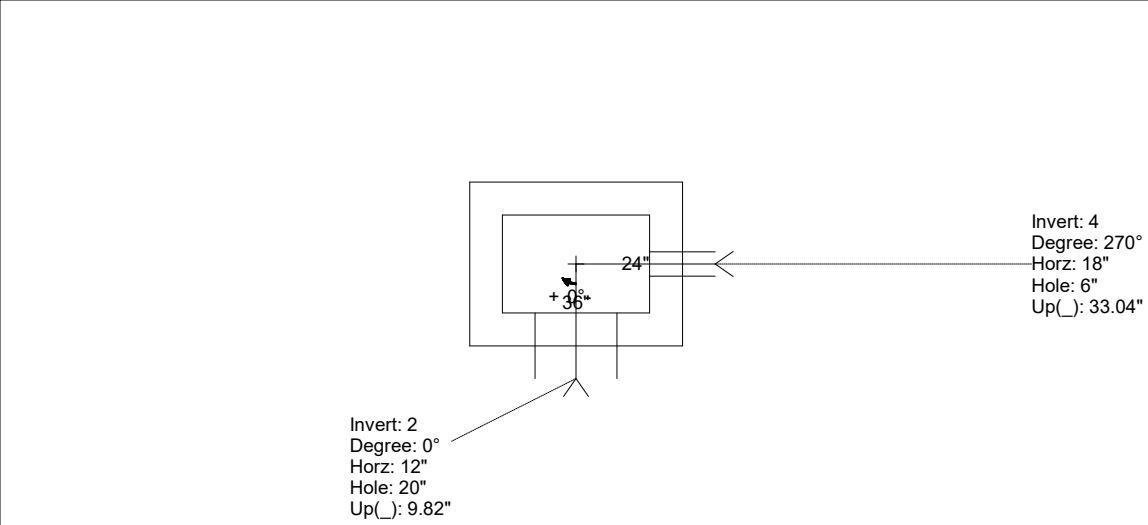

Invert: 2
Degree: 0°
Horz: 12"
Hole: 20"
Up(): 9.82"

Invert: 4
Degree: 270°
Horz: 18"
Hole: 6"
Up(): 33.04"

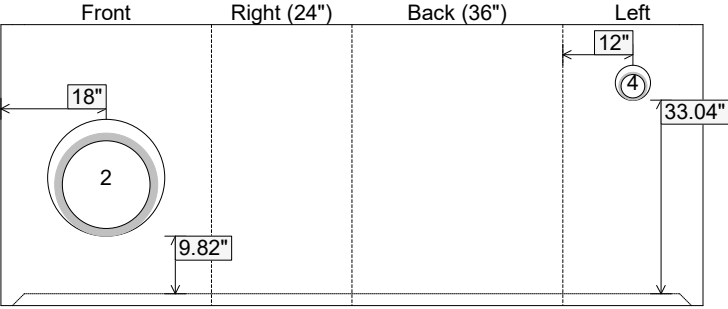INSIDE WALL DIMENSIONS				
(P4)				
	EXT 48"			

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 8" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 4668 lb Volume (Net): 1.19cu.yd
----------------------------------	----------------------------------	--	--	--
