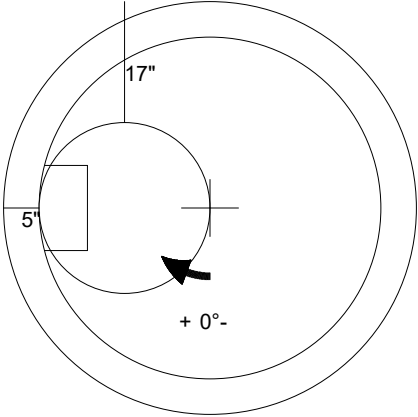



Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018)		Plant: Beaver Dam		Tech: J. Horsley		
Job Location: Hopkinsville, KY		7/30/2026 8:57:35 AM		PC: C. Goff		
Contractor: Scotty's Contracting & Stone, LLC						
Structure ID: 267 (435+52 RT)						
P4 MH048CN42		ECC CONE w/ 24" HOLE F/G				
P6) 24" - CASTING HEIGHT - 8" P5) 24" - GRADE RING F/F - 4" P4) 48" - ECC CONE w/ 24" HOLE F/G - 42" P3) 48" - MH RISER T/G - 48" P2) 48" x 48" - CB FT REDUCER 48" HOLE T/F - 8" P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/08EF F/n - 60" 1) CASTING - HOE KY-510 F/C (KY TY.2) 1) 48" x 48" - Conseal CS-102 1.00" 2) 48" - Conseal CS-102 1.00" 2) Hole - 44		0 lb 270 lb 3200 lb 3353 lb 1535 lb 13425 lb 510 lb 0 lb 0 lb 0 lb ----- Structure Total: 22293 lb		Structure Notes: ** KYTC STATE PROJECT** 1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-510 F/C) 4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE (8"WD x 12" THICK). . REINFORCING PER ASTM A615 (GRADE 60). - TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT). - WALLS #5's AT 6" C.C.E.W. - FLOOR #5's AT 12" C.C.E.W..		
						
 48" - ECC CONE w/ 24" HOLE F/G - 42" - (P4)						
Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3200 lb Volume (Net): 0.5cu.yd	
