

Contractor: Scotty's Contracting & Stone, LLC

PC:	C. Goff
TECH:	J. Horsley
Plant:	Beaver Dam



Size: 24" x 30"

Rim to Invert: 3.52'


Floor Height: 8"

Slack: 0.49"


REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

1) Hole - 20


Structure Total: 5017 lb

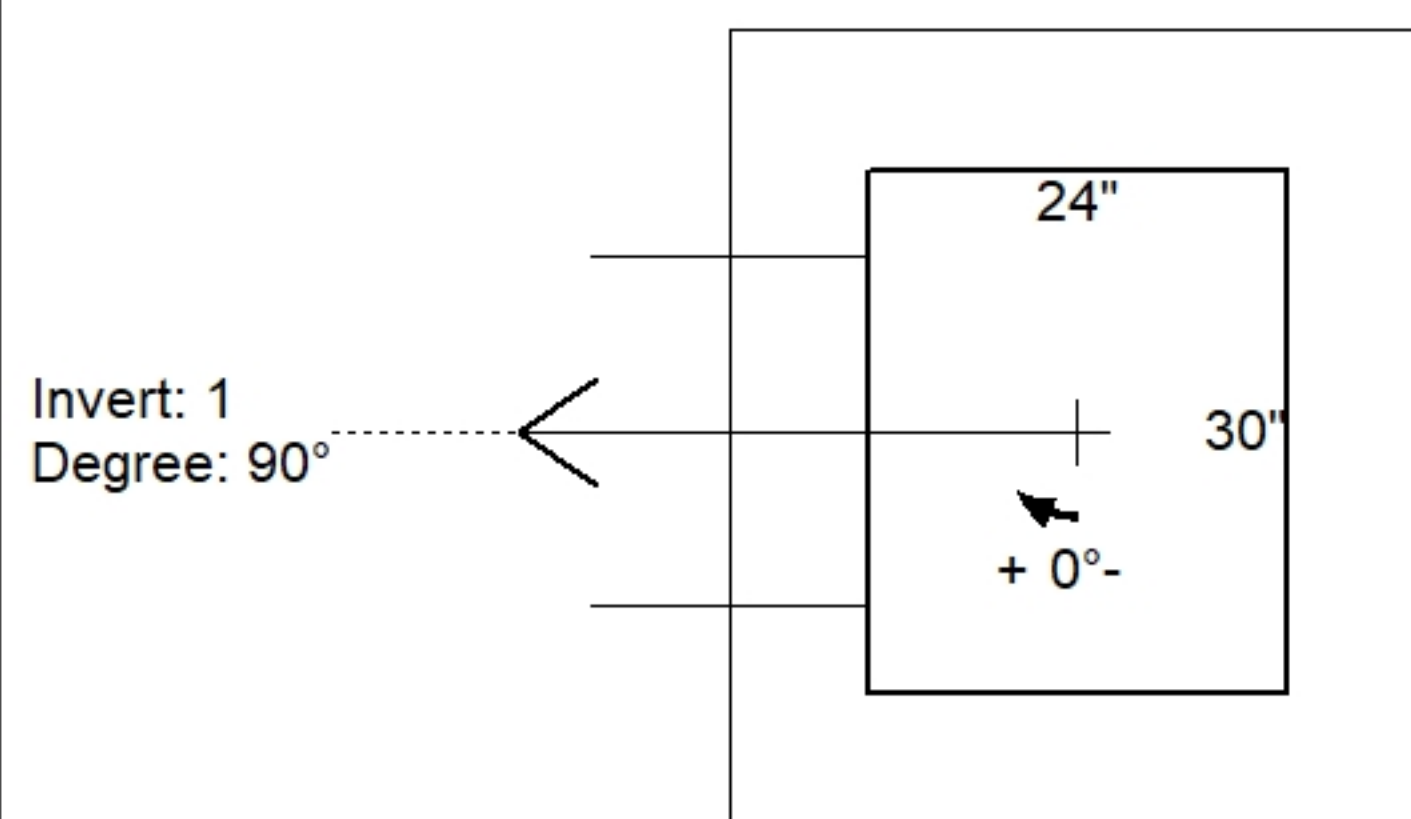

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	545.44'							
Reducer								
Invert 1	541.92'	90°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

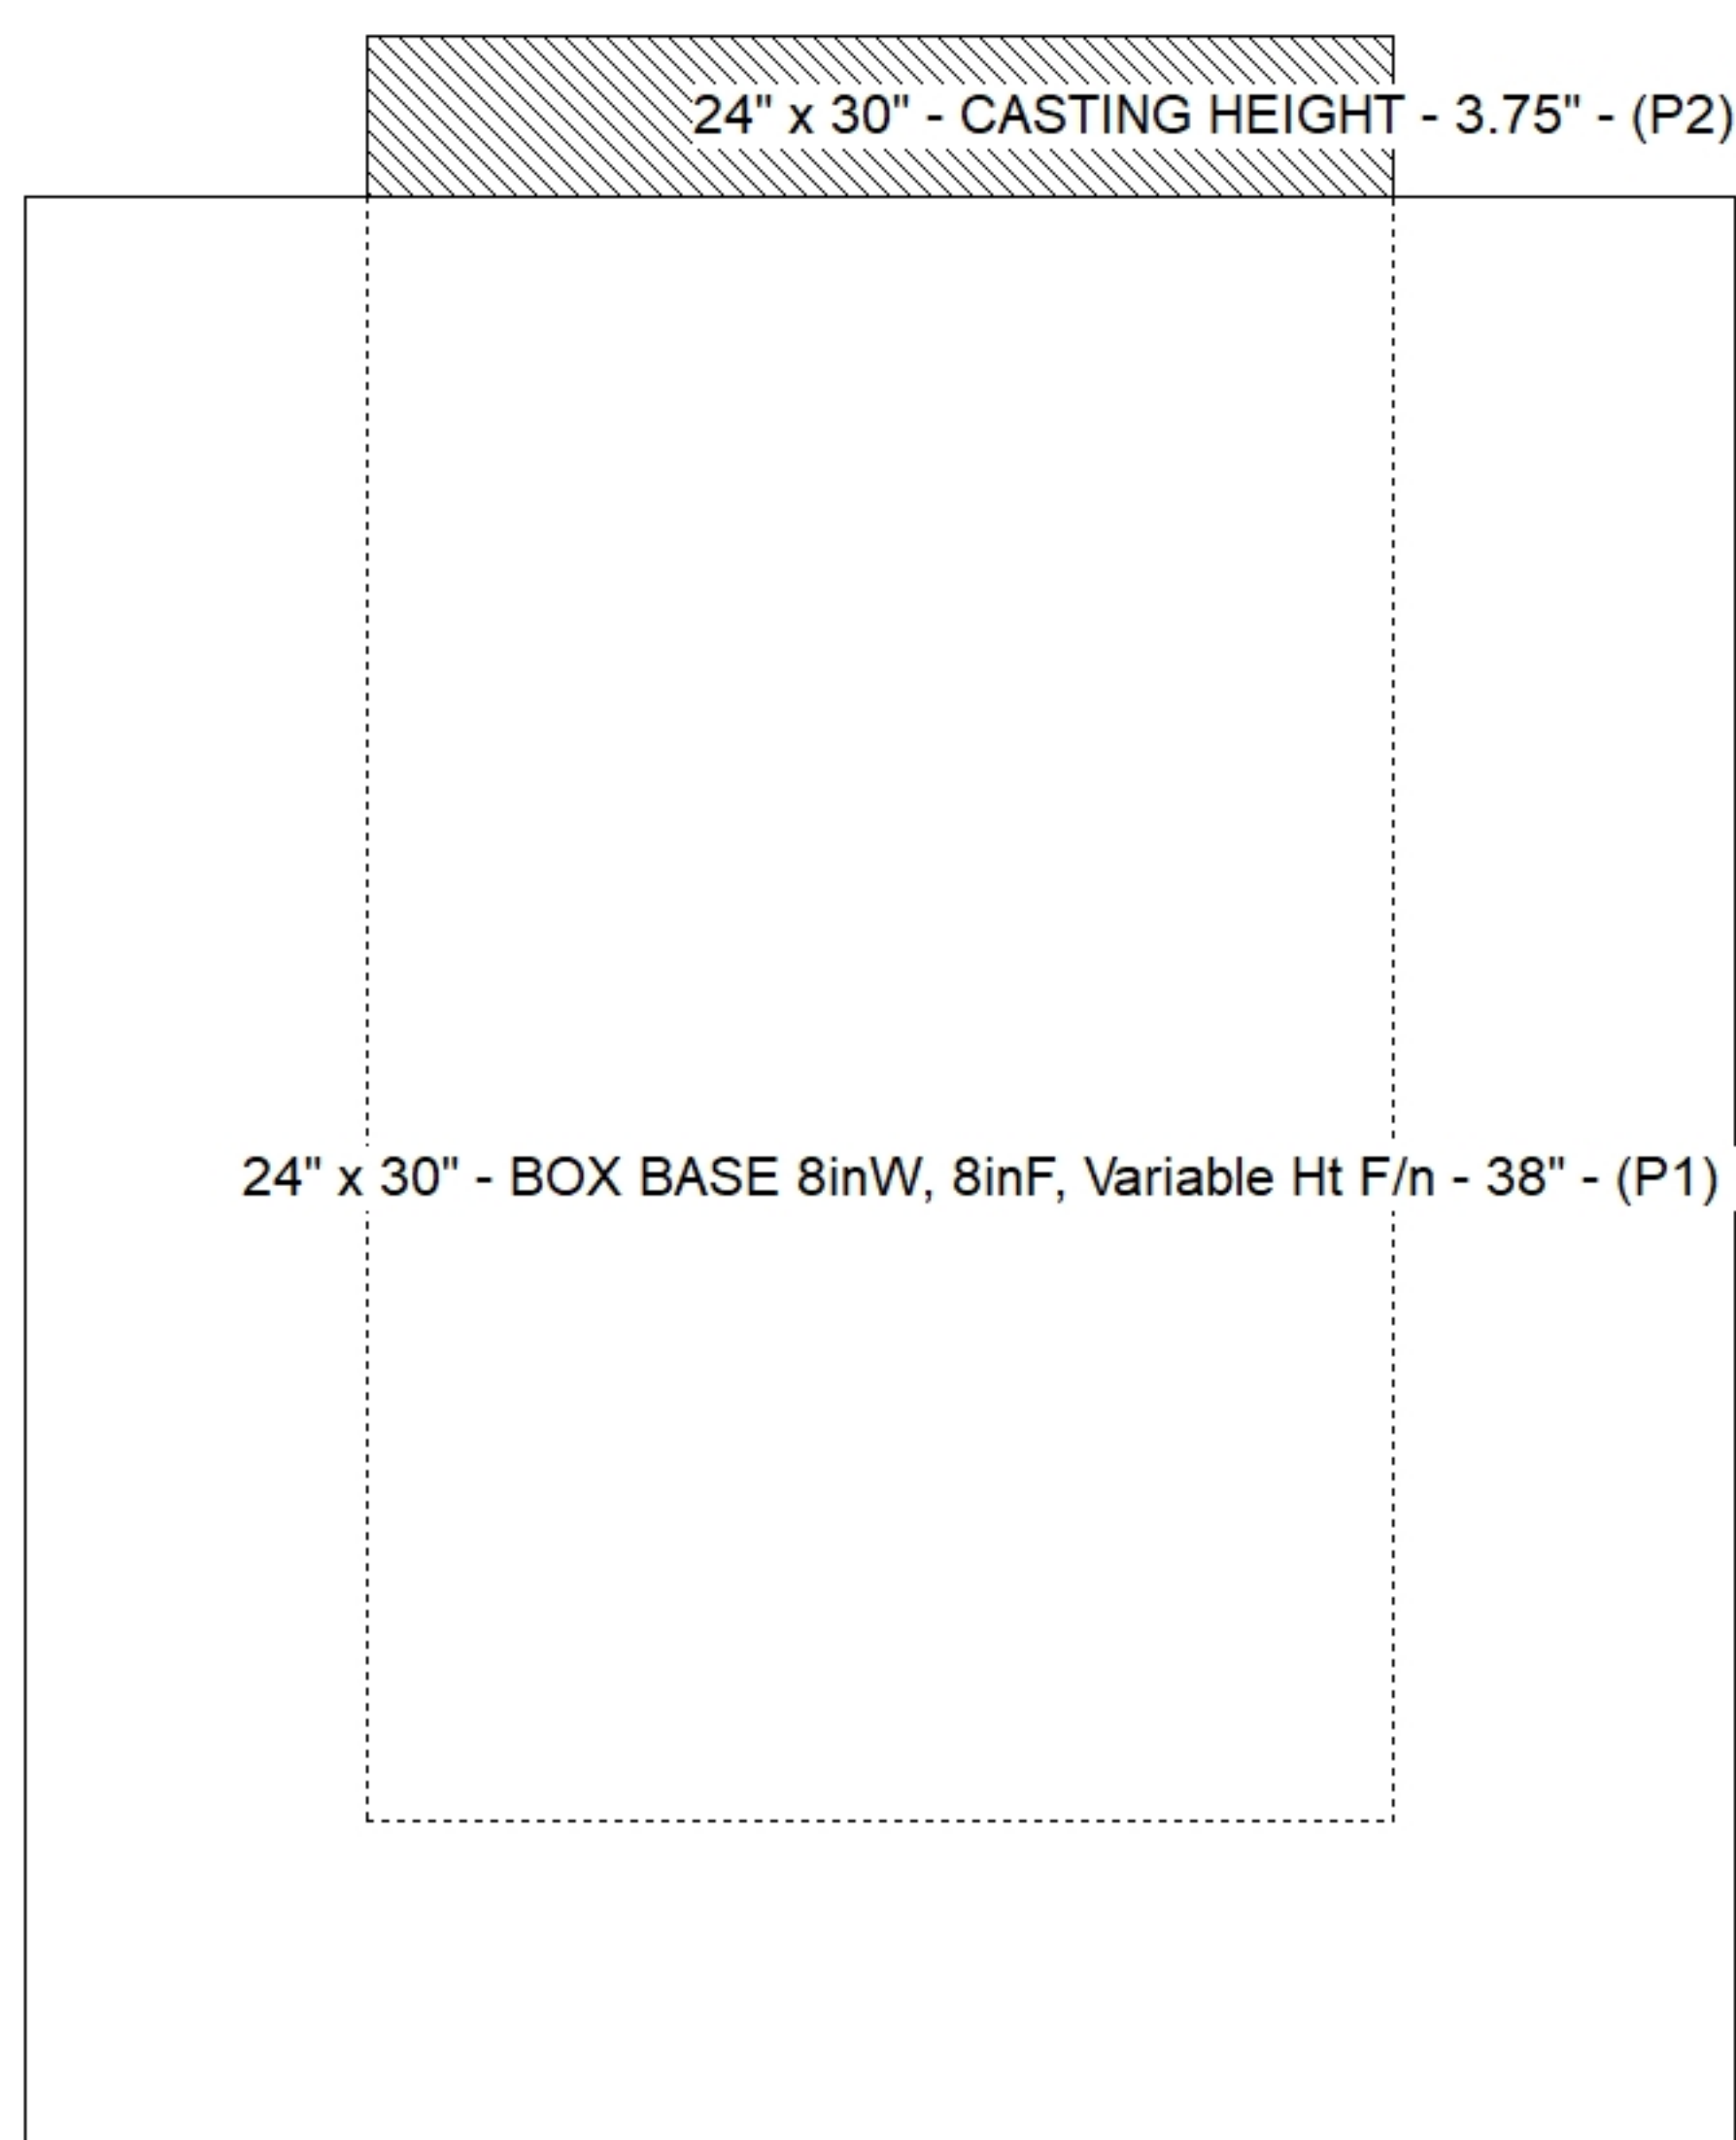

Default - Interior Dimensions

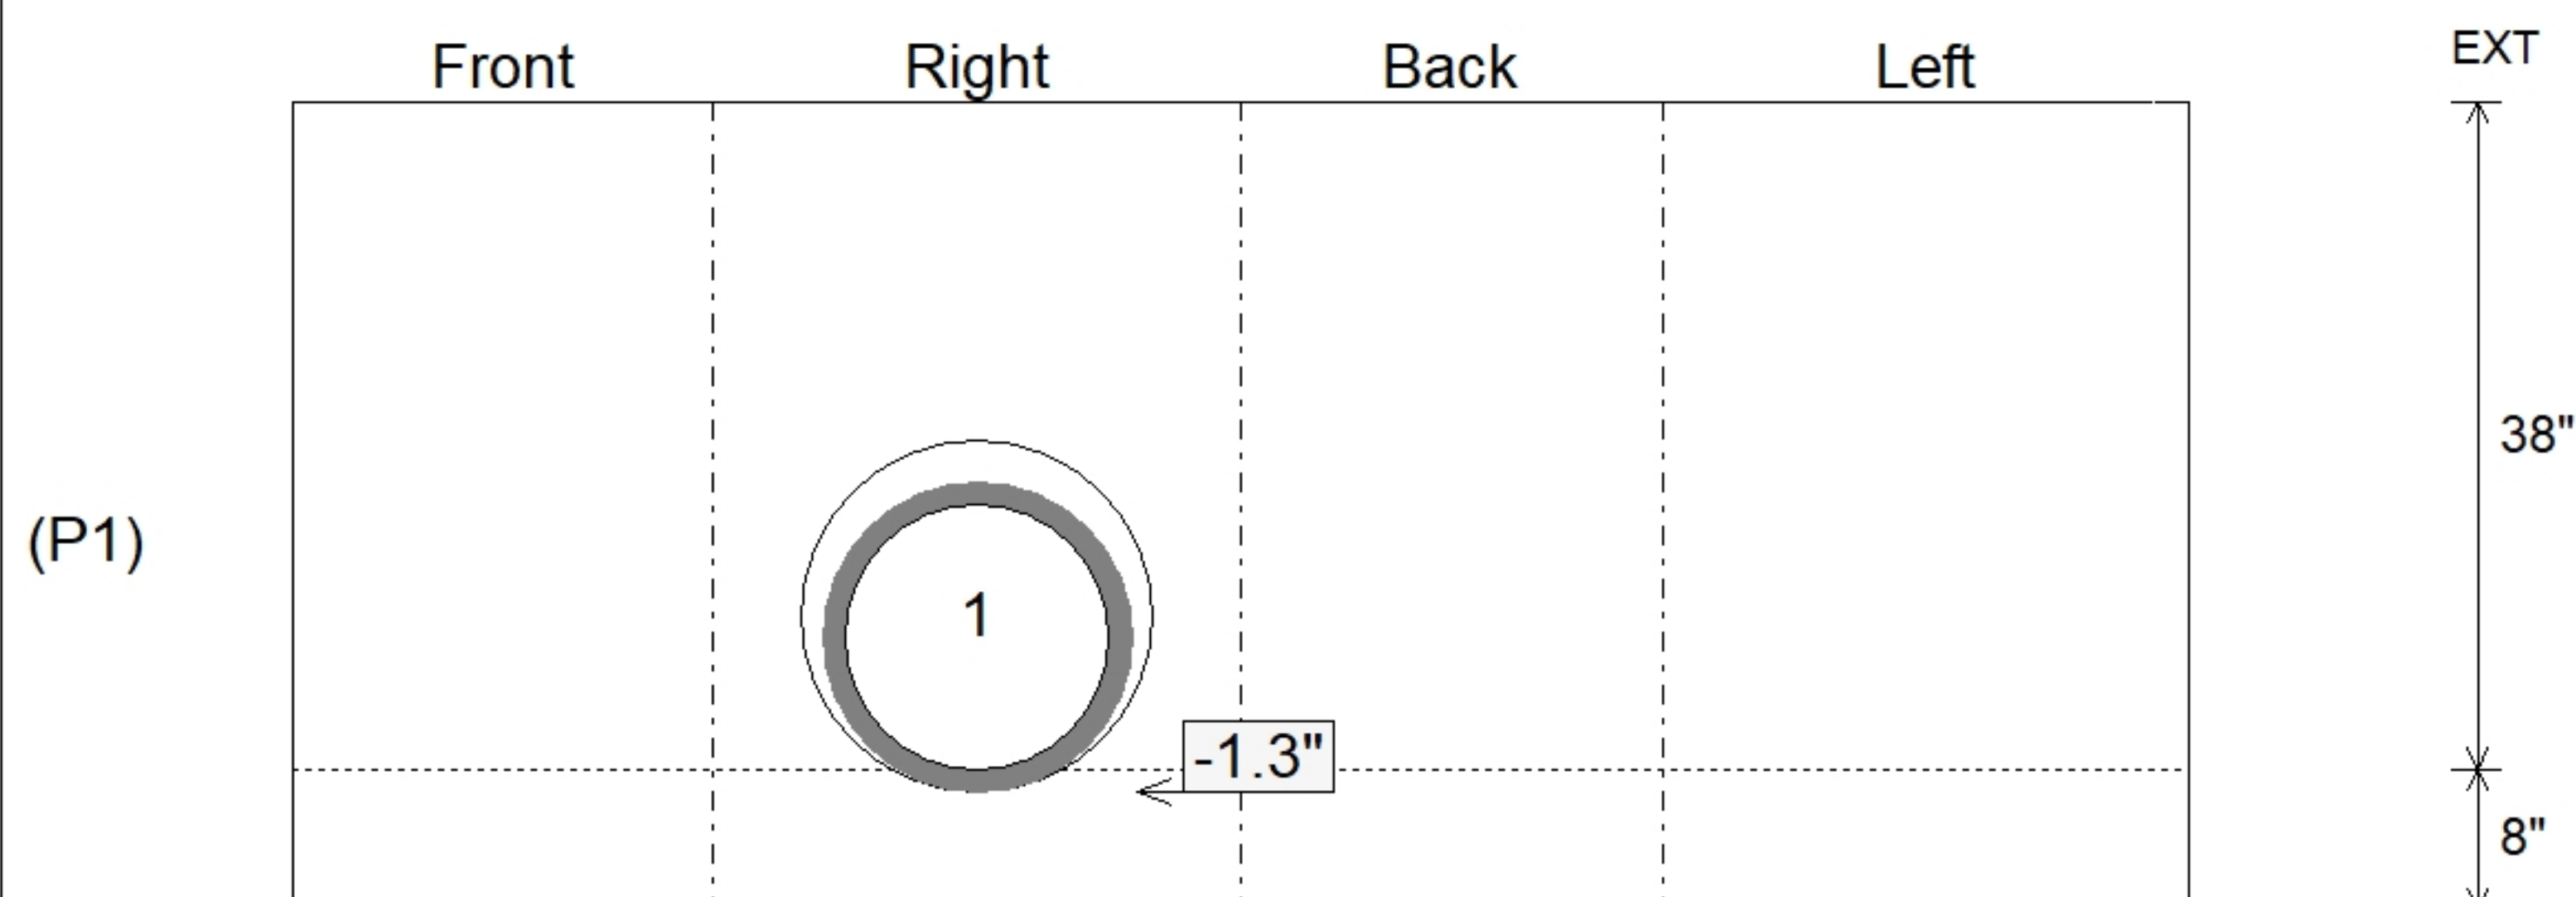

Submittal Drawing
7/30/2026 8:51:32 AM

SUBMITTAL
APPROVED BY:
