

Contractor: Scotty's Contracting & Stone, LLC

PC:	C. Goff
TECH:	J. Horsley
Plant: Beaver Dam	



Size: 24" x 30"

Rim to Invert: 3.25'

Floor Height: 8"


Slack: 0.25"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


1) Hole - 20

0 lb
4314 lb
421 lb
0 lb
0 lb


Structure Total: 4735 lb

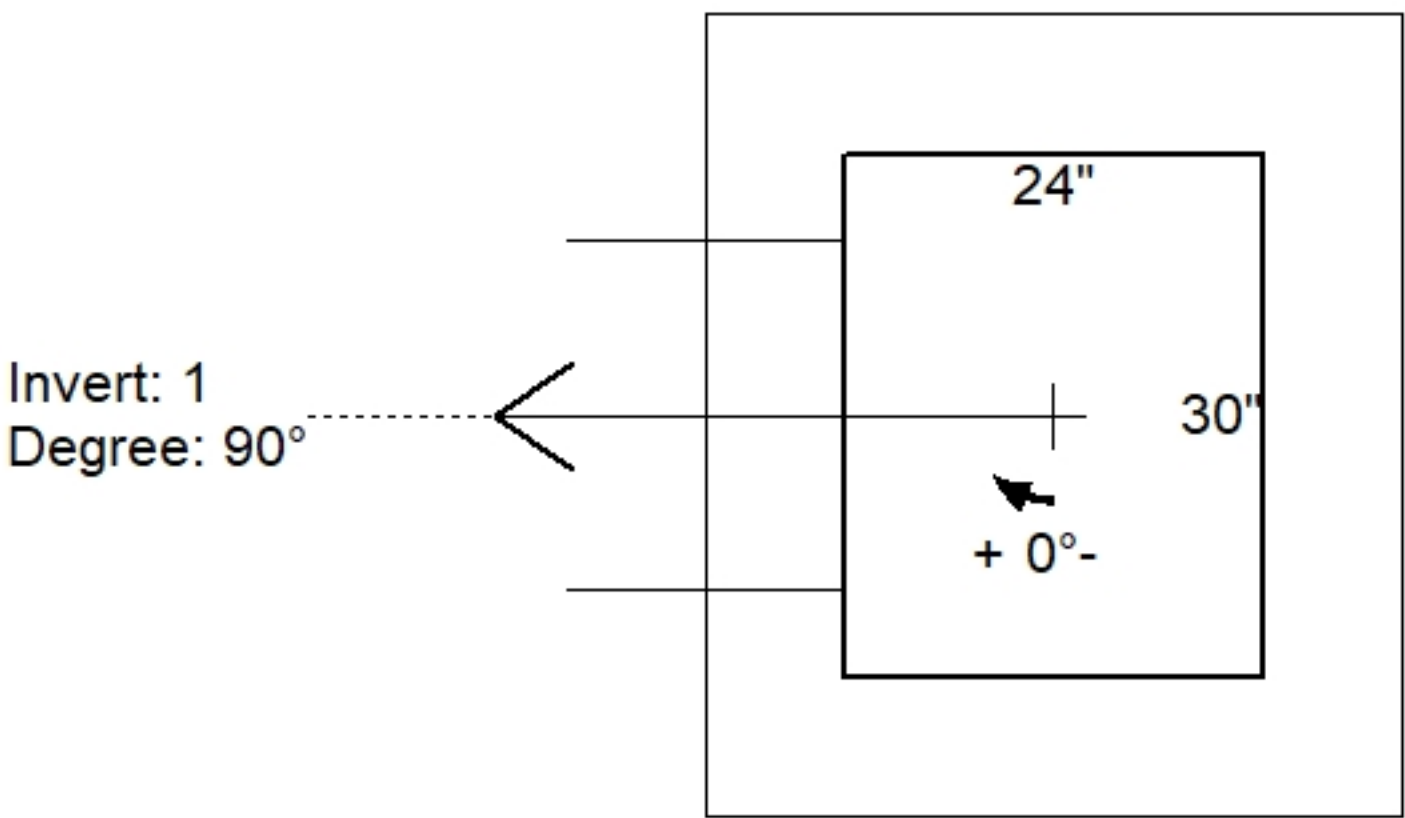

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	535.25'							
Reducer								
Invert 1	532'	90°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

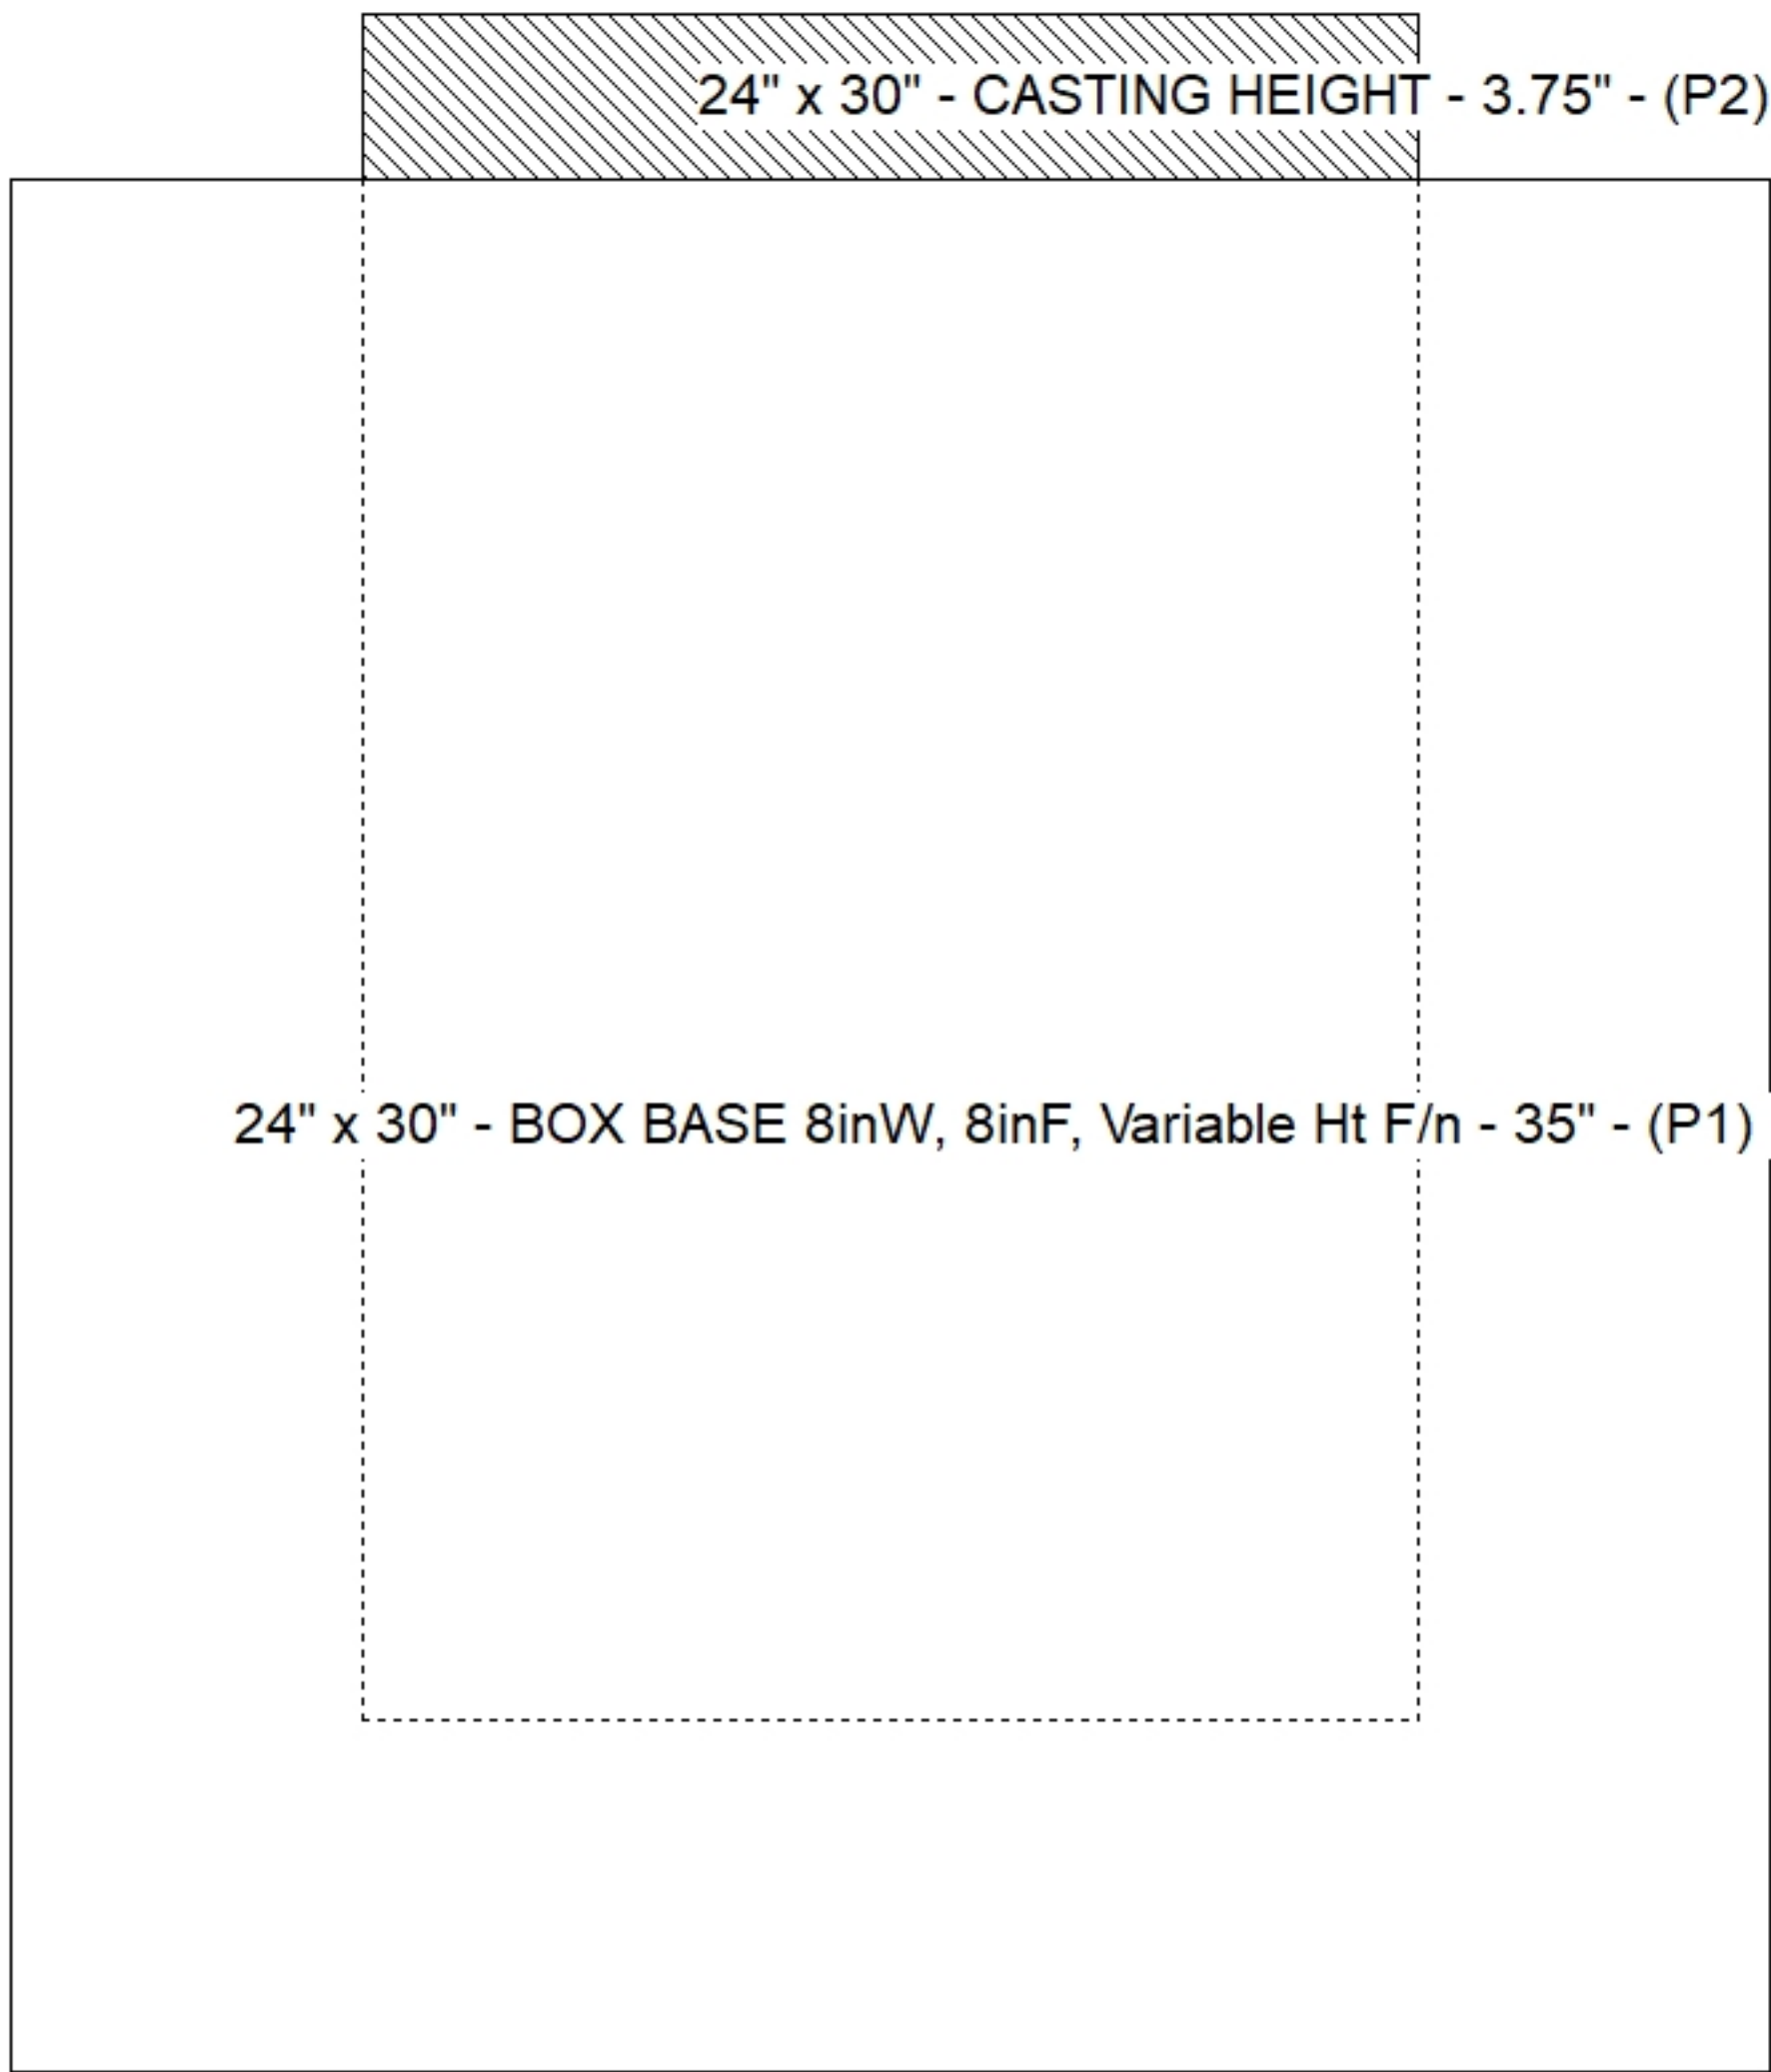

Default - Interior Dimensions

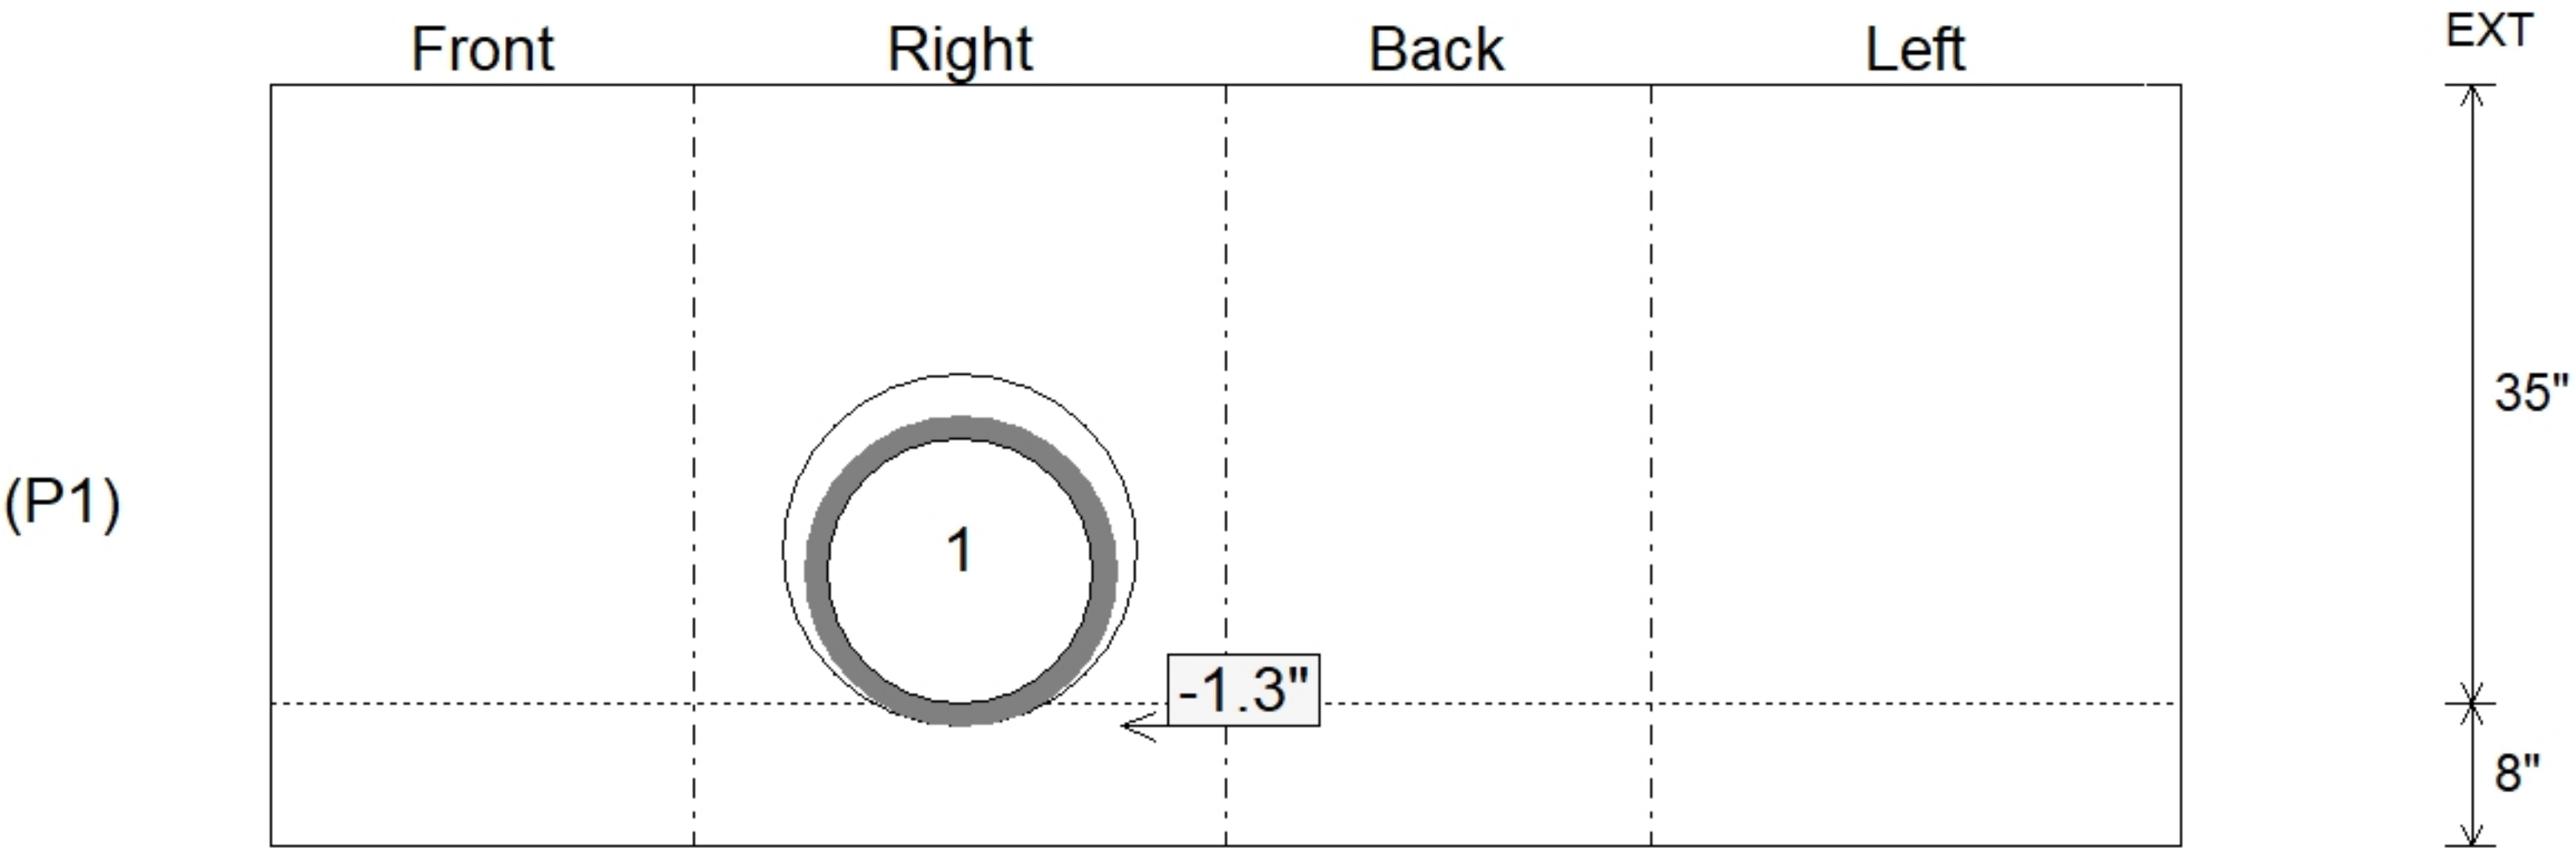

Submittal Drawing
8/3/2026 4:17:59 PM

SUBMITTAL
APPROVED BY:
