


Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC				Plant: Beaver Dam 8/3/2026 4:22:13 PM		Tech: J. Horsley PC: C. Goff						
Structure ID: 289 (446+10 RT)												
P1 BX3660-08BA54				BOX BASE 8inW, 8inF F/n								
P4) 24" x 120" - CB INLET KY A 10' TOP LEFT F/G - 10" P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT T/G - 18" P2) 36" x 60" - CB FT REDUCER 24"X36" HOLE T/F - 8" P1) 36" x 60" - BOX BASE 8inW, 8inF F/n - 54" 1) CASTING - HOE KY-206 F/C (KY TY1) 1) 36" x 60" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 50 1) Hole - 20 1) Hole - 6						3400 lb 5270 lb 2073 lb 7907 lb 206 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 18855 lb		Structure Notes: ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE A / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. HOE KY-206 F/C CAST INTO TOP SLAB. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT) - WALLS (As .31) #5 BARS AT 6" C.C.E.W. - FLOOR (As .31) #5 BARS AT 6" C.C.E.W.				
Rim: 527.25'		Rim to Invert: 7.5'		Slack: 0"		Sump: 0"		Step Position:				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	519.75'	270°	38"	42" HDPE	47.7"	Hole 50	50"	50"	-3.15"	0"		
Invert 2	521'	0°	26"	15" HDPE	17.6"	Hole 20	20"	20"	13.7"	0"		
Invert 3	519.75'	90°	38"	42" HDPE	47.7"	Hole 50	50"	50"	-3.15"	0"		
Invert 4	523.25'	90°	62"	4" HDPE (perf pipe)	4.8"	Hole 6	6"	6"	41.6"	24"		
Invert 5												
Invert 6												
Invert 7												
Invert 8												

RIGHT-SIDE UP VIEW (int. dimensions)

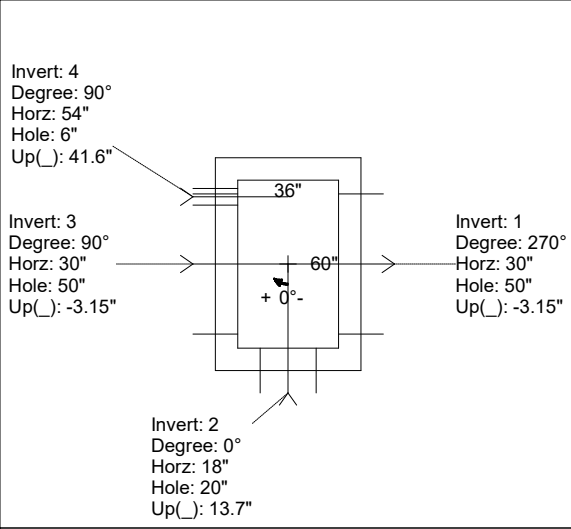


UPSIDE-DOWN VIEW (int. dimensions)

2-Stage Pour Required

First pour drawing

First pour weight = 2,653 LBS

Second pour weight = 5,254 LBS

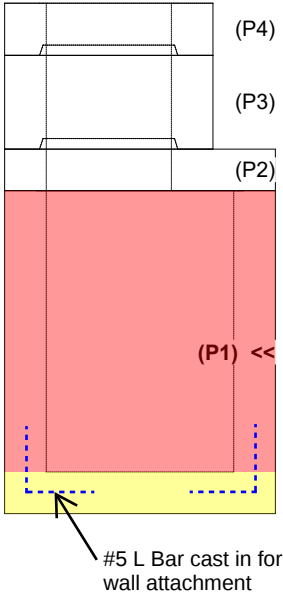

(P4)


(P3)

(P2)

(P1) <<

#5 L Bar cast in for wall attachment

INSIDE WALL DIMENSIONS

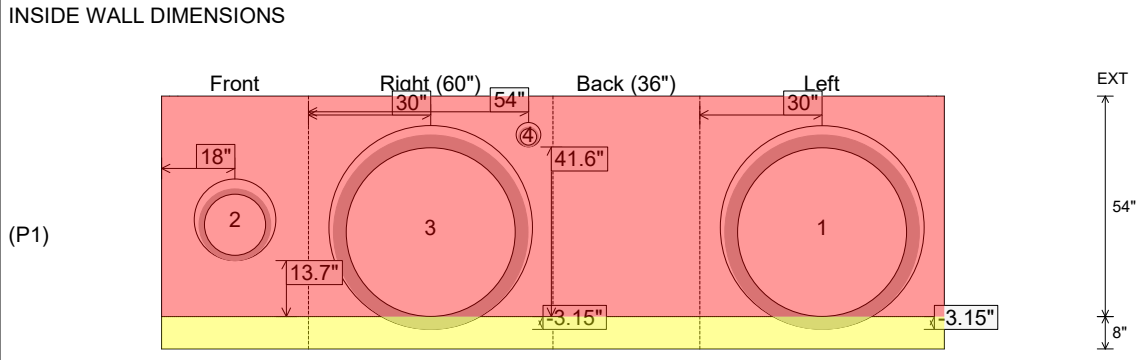

Front

Right (60")

Back (36")

Left

EXT

54"

8"

18"

30"

54"

41.6"

13.7"

3.15"

3.15"


2

3

1

(P1)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 54" Height (Ext): 62"	Weight (Net): 7907 lb Volume (Net): 2.02cu.yd
----------------------------------	-------------------------------	--	--	--



Weight (Net): 7907 lb
Volume (Net): 2.02cu.yd
