

Contractor: Scotty's Contracting & Stone, LLC

TECH: J. Horsley

Plant: Beaver Dam



Size: 36" x 36"

Rim to Invert: 7.91'



Floor Height: 8"

Slack: 0.42"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


22C 1b

Structure Total: 17336 lb

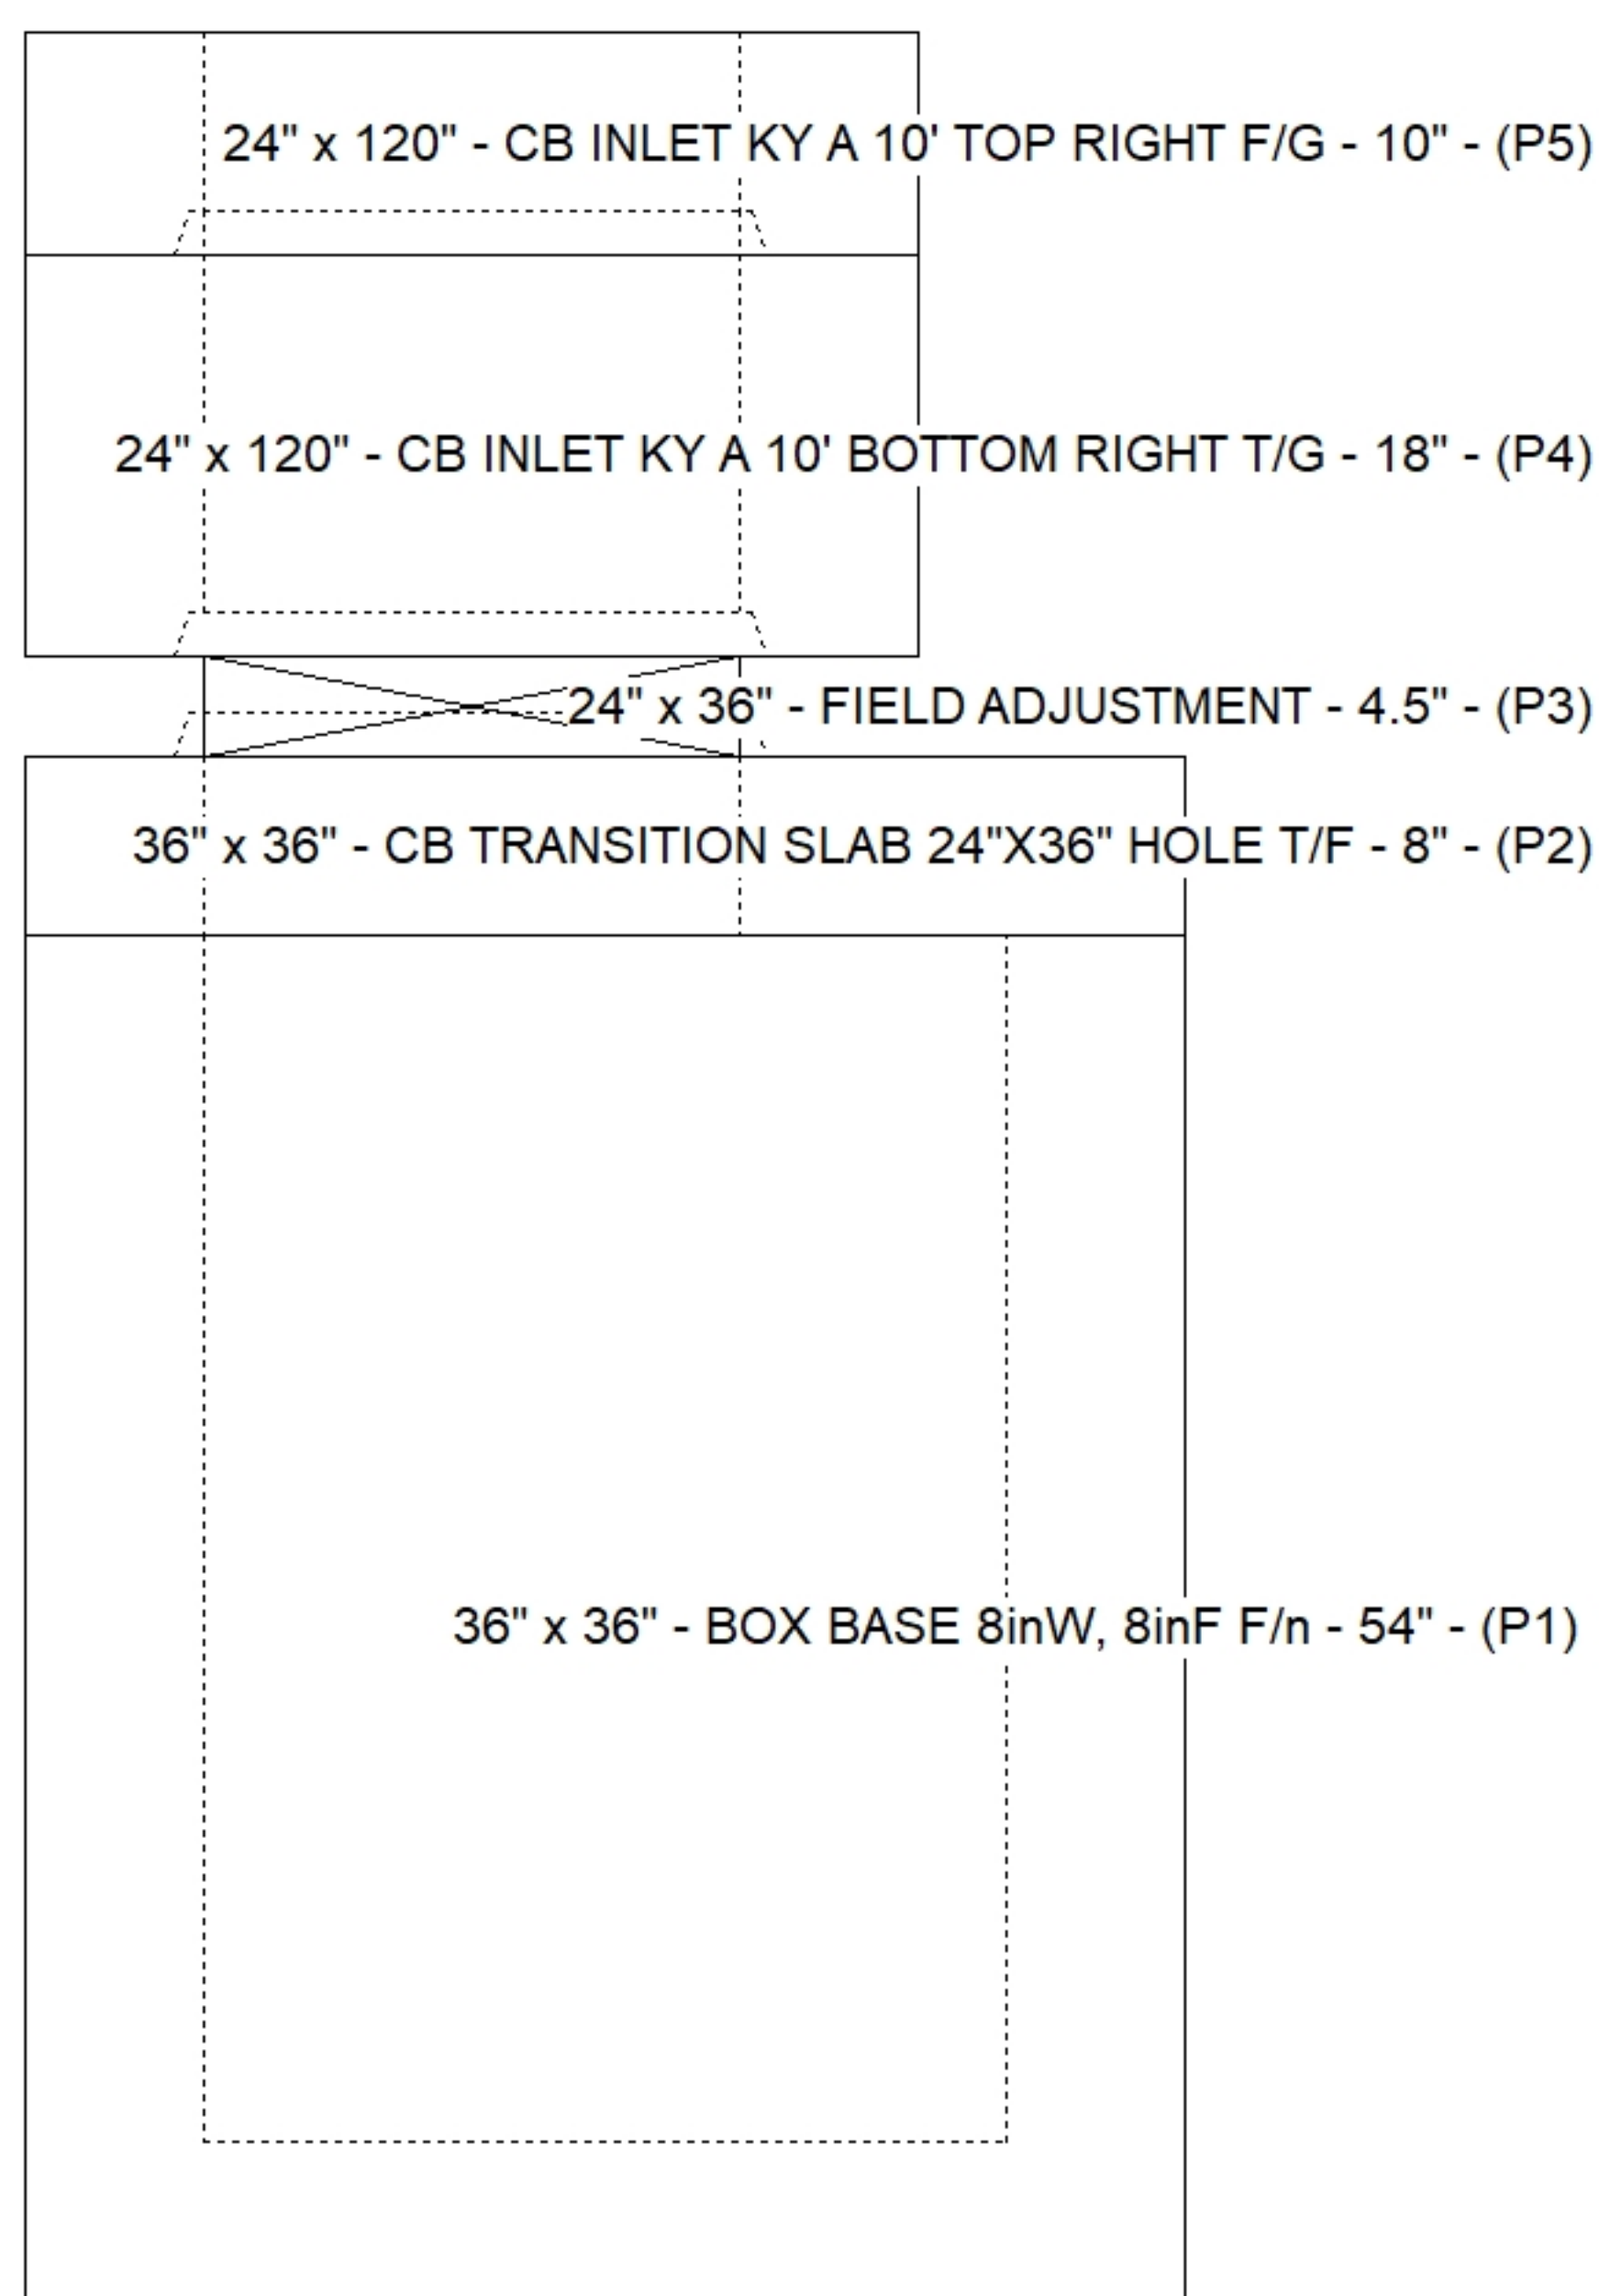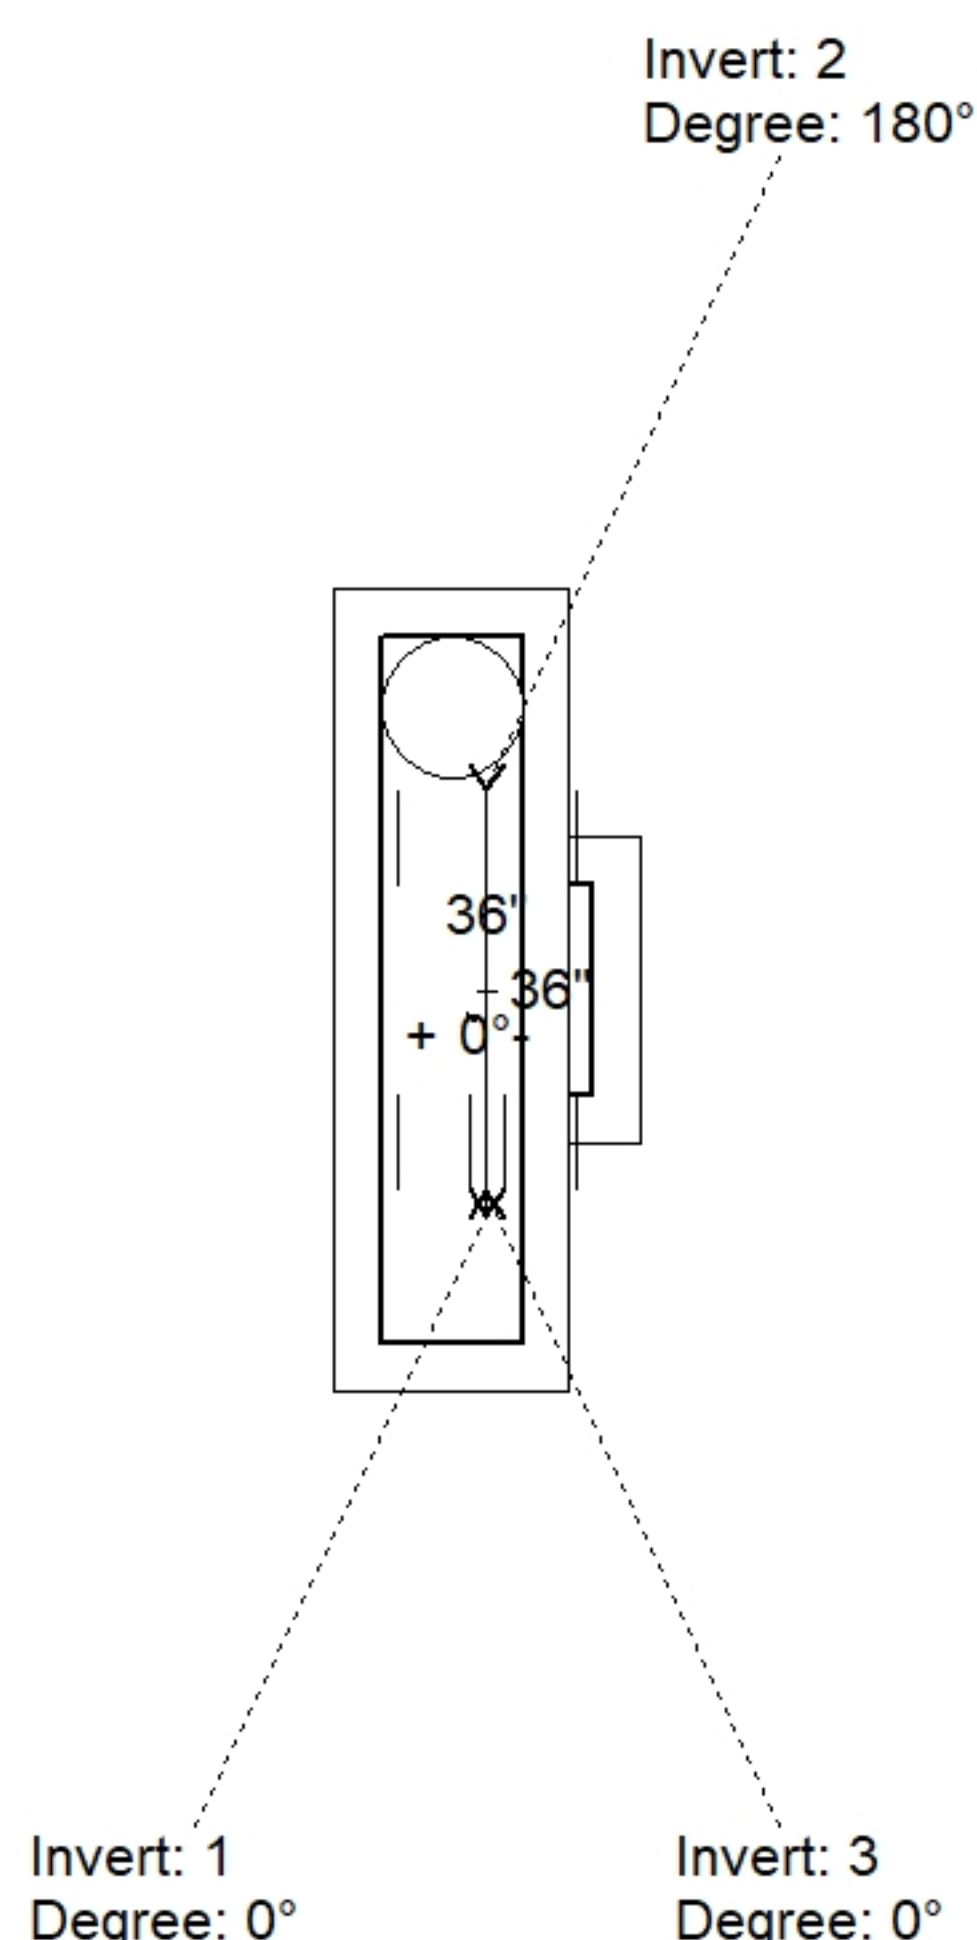

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	527.62'							
Reducer	524.21'							
Invert 1	519.71'	0°	24" HDPE	27.8"	30"	Hole 30	-1.9"	P1
Invert 2	519.71'	180°	24" HDPE	27.8"	30"	Hole 30	-1.9"	P1
Invert 3	523.33'	0°	4" HDPE (perf pipe)	4.8"	6"	Hole 6	43.04"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

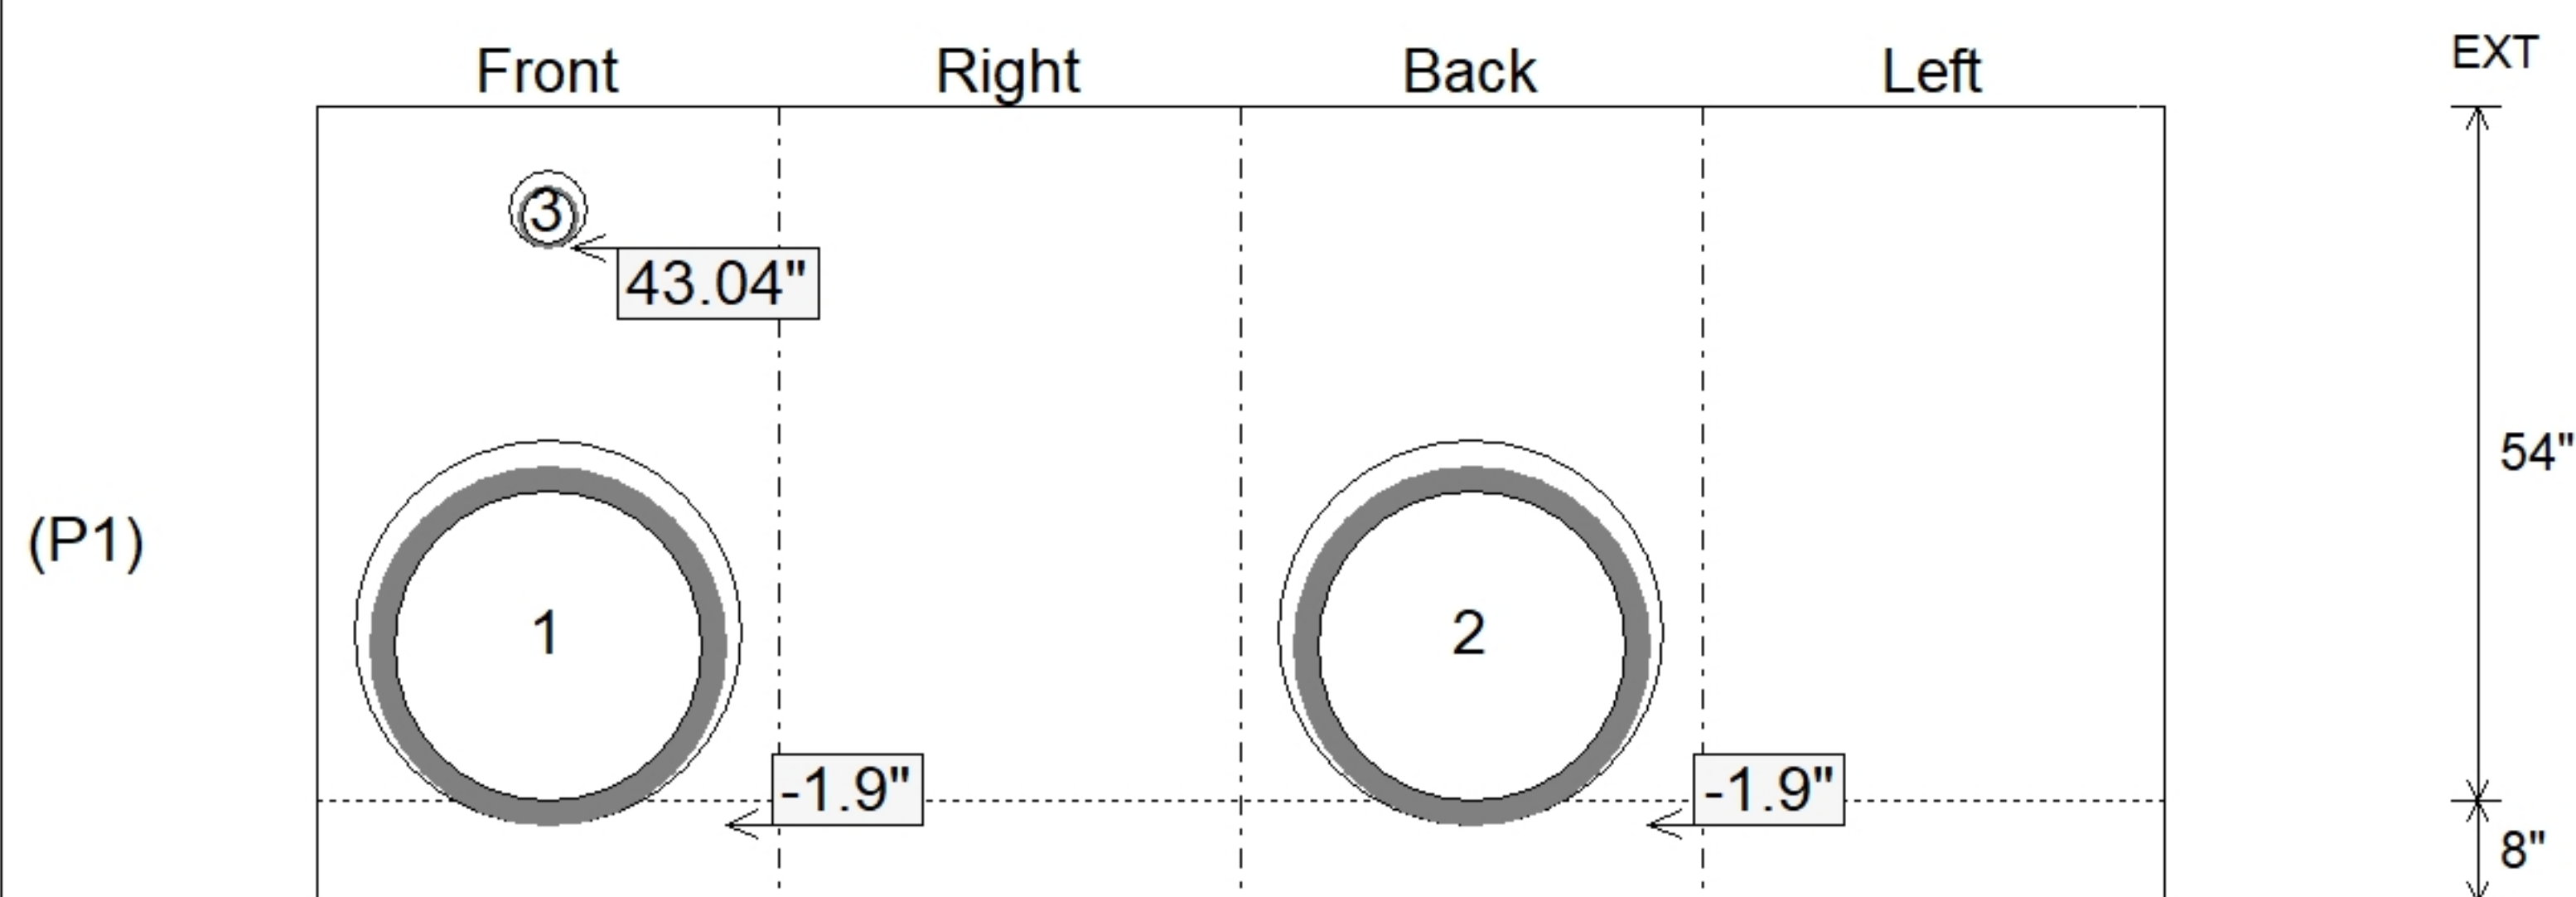

Submittal Drawing
8/3/2026 4:18:23 PM

SUBMITTAL
APPROVED BY:
