


Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam




Slack: 0.26"

Structure Total:	11080 lb
------------------	----------

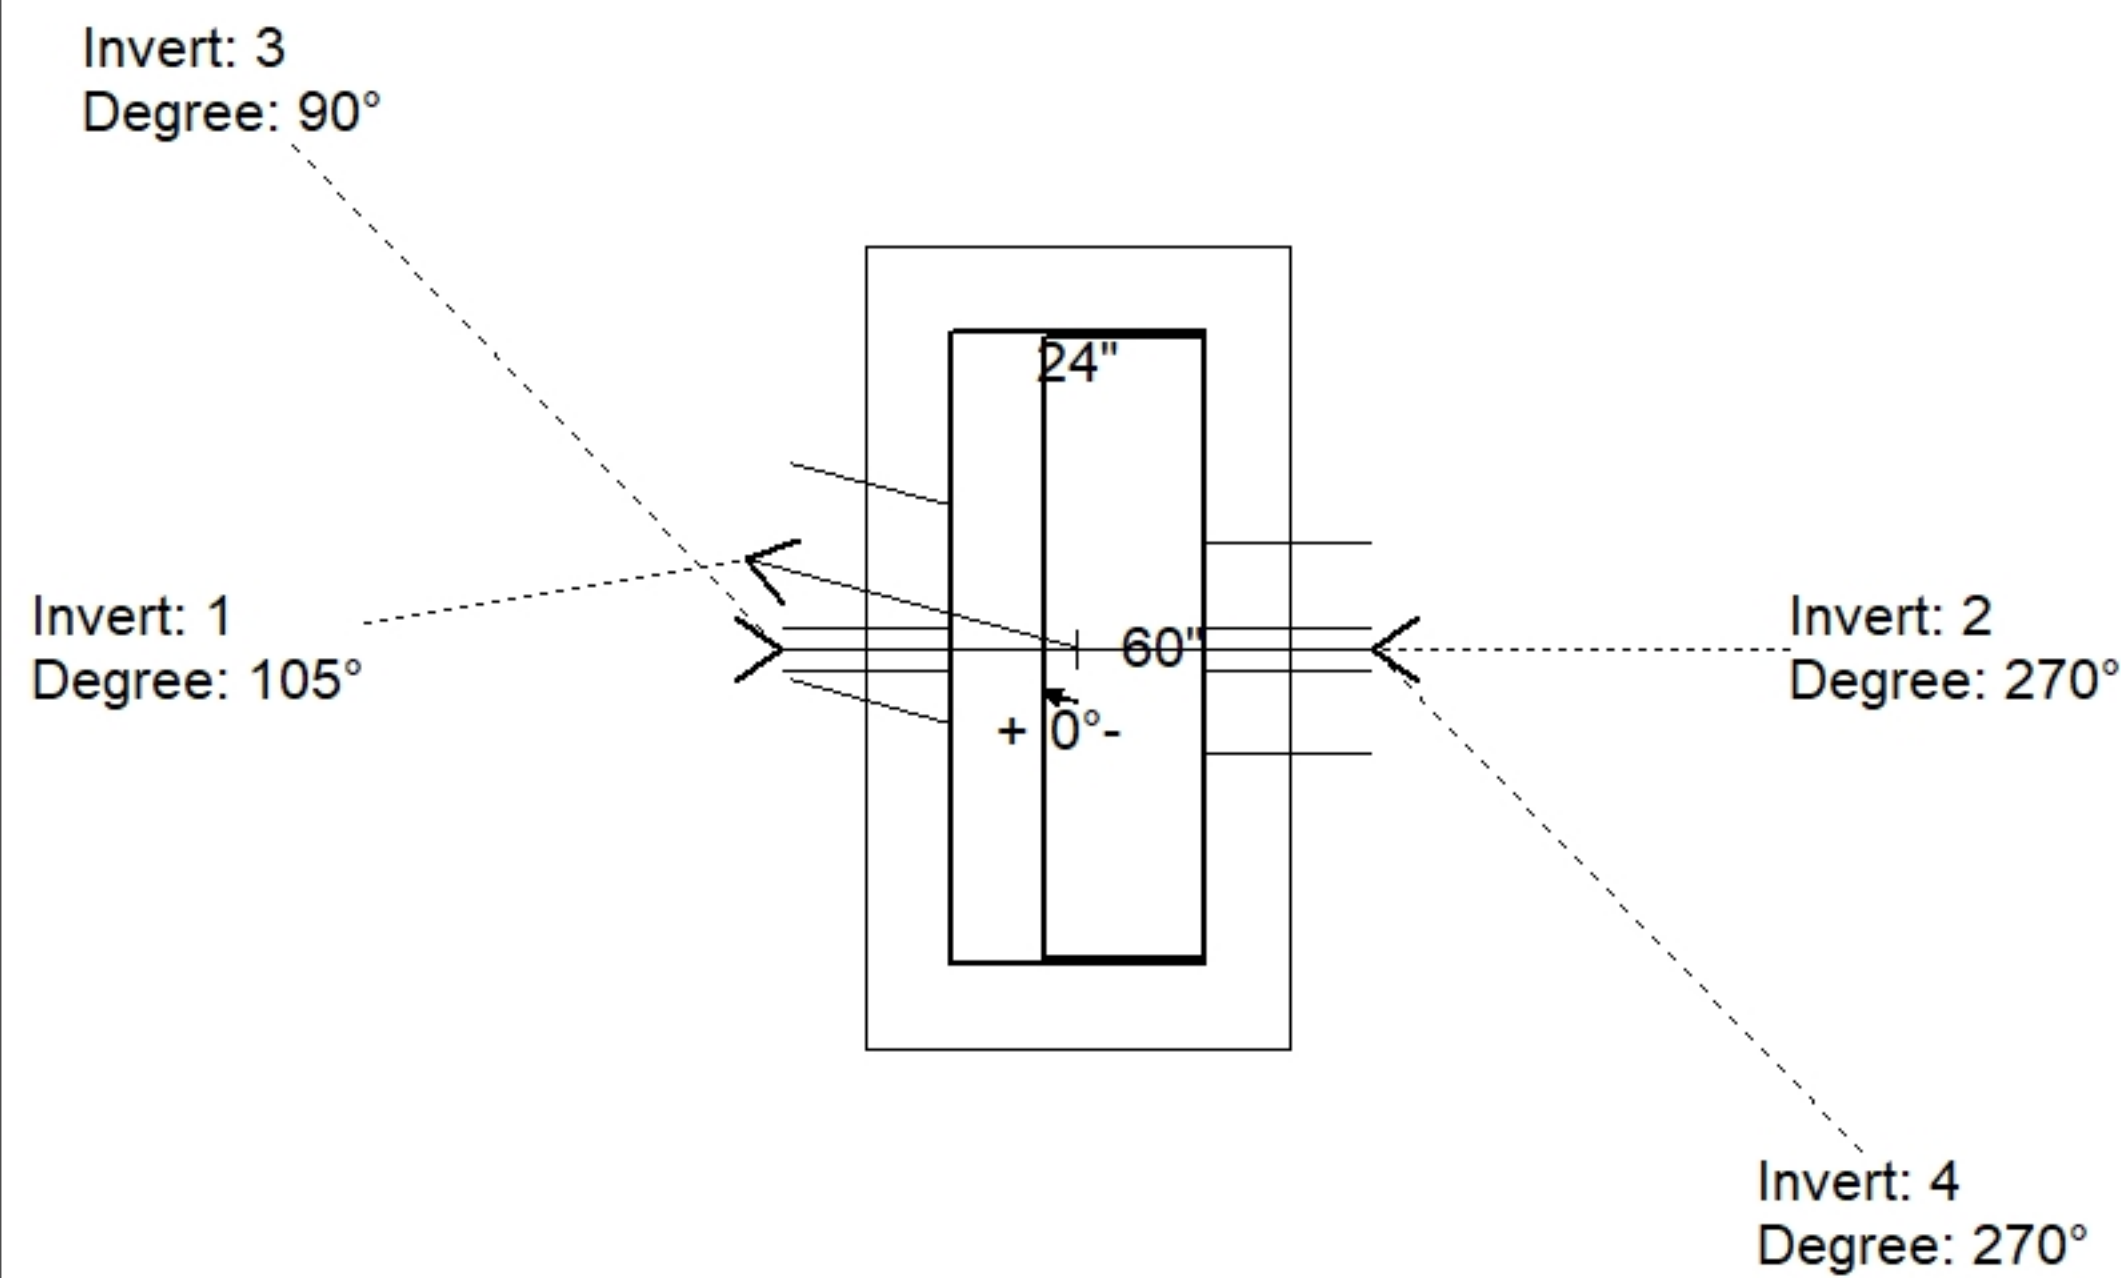

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	526.71'							
Reducer								
Invert 1	520.23'	105°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 2	520.23'	270°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 3	524.4'	90°	4" WEEP HOLE	4"	4"	Hole 4	50.04"	P1
Invert 4	524.4'	270°	4" WEEP HOLE	4"	4"	Hole 4	50.04"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 60" - BOX BASE 8inW, 8inF, Variable Ht F/n - 58" - (P1)

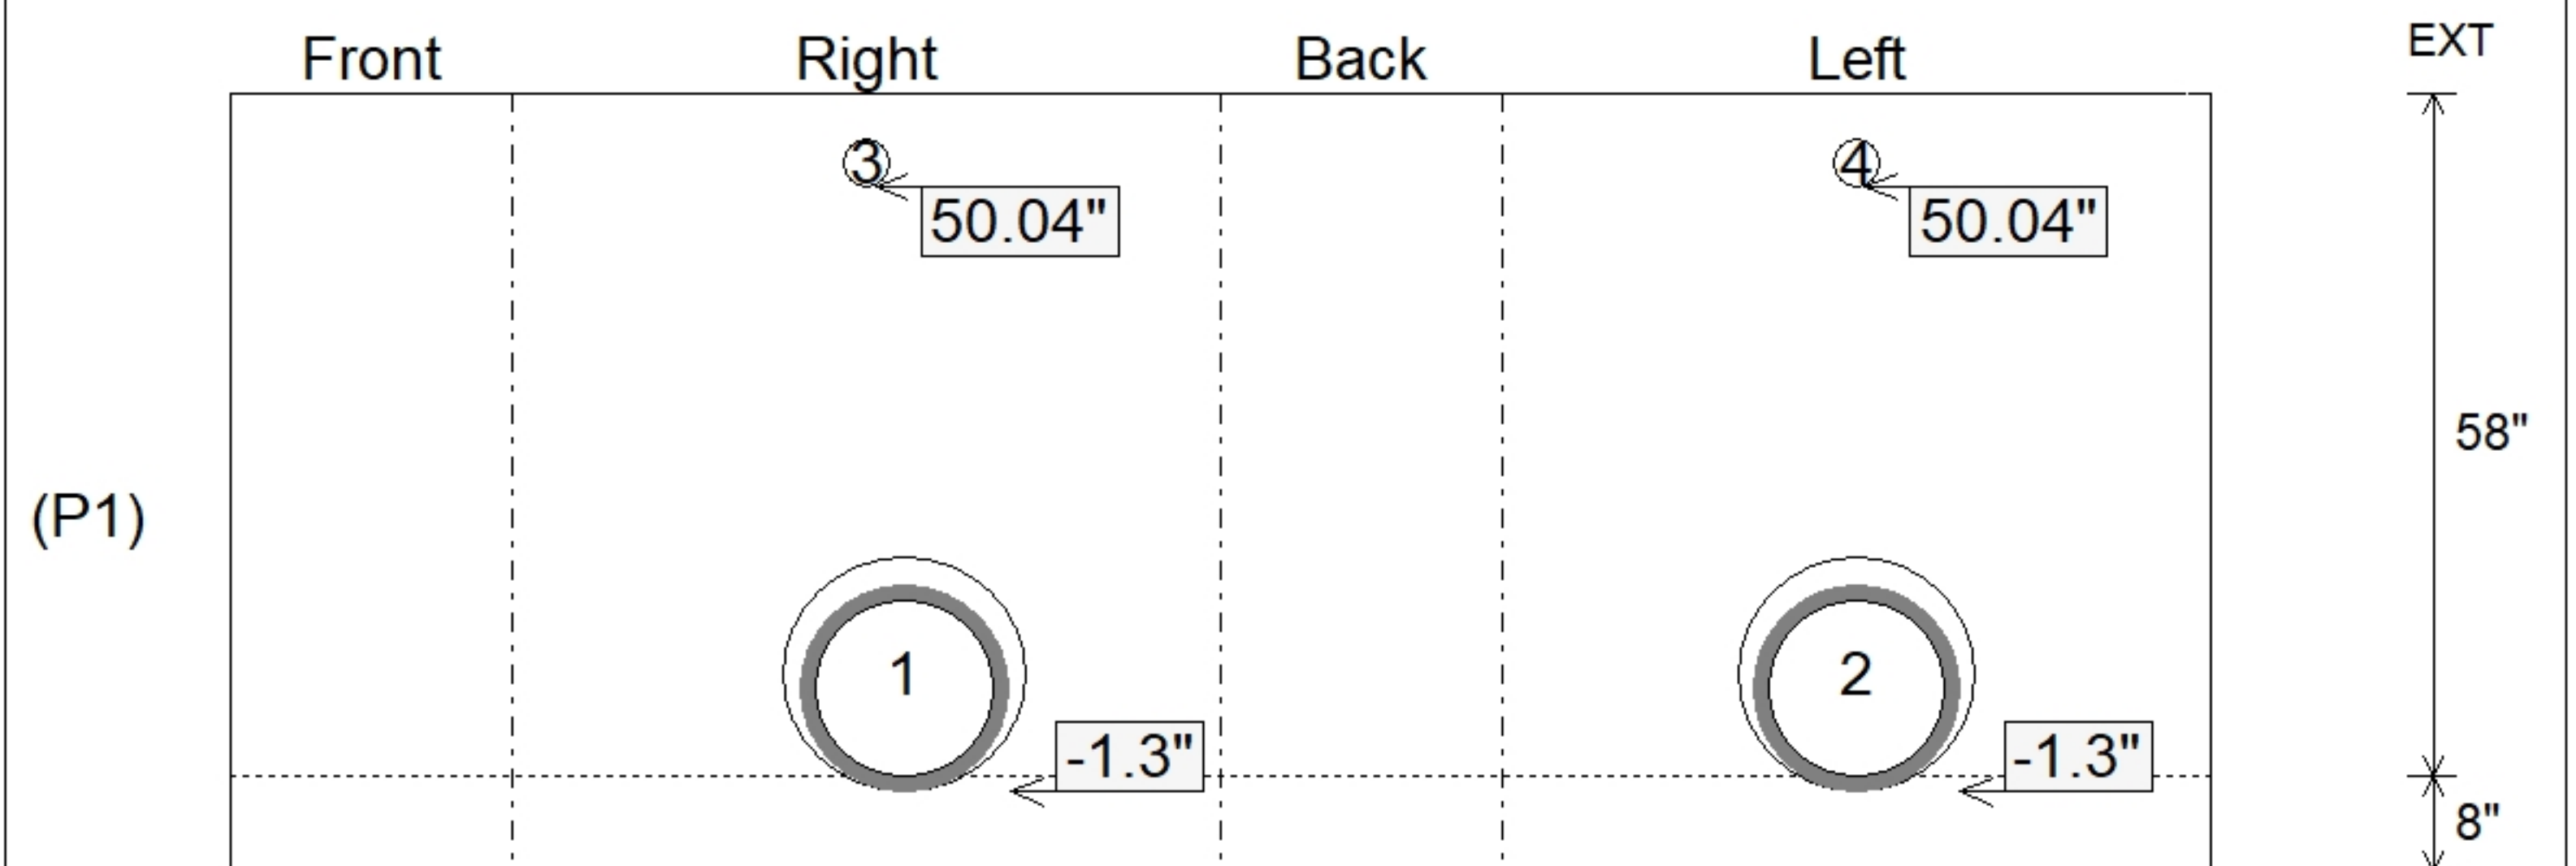

SUBMITTAL
APPROVED BY:
