

Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam



Size: 32" x 32"

Rim to Invert: 6.86'

Floor Height: 8"


Slack: 0.32"

- FLOOR (As .31) #5 BARS AT 12: C.C.E.W.

1) Hole - 20


0 lb

Structure Total: 9784 lb

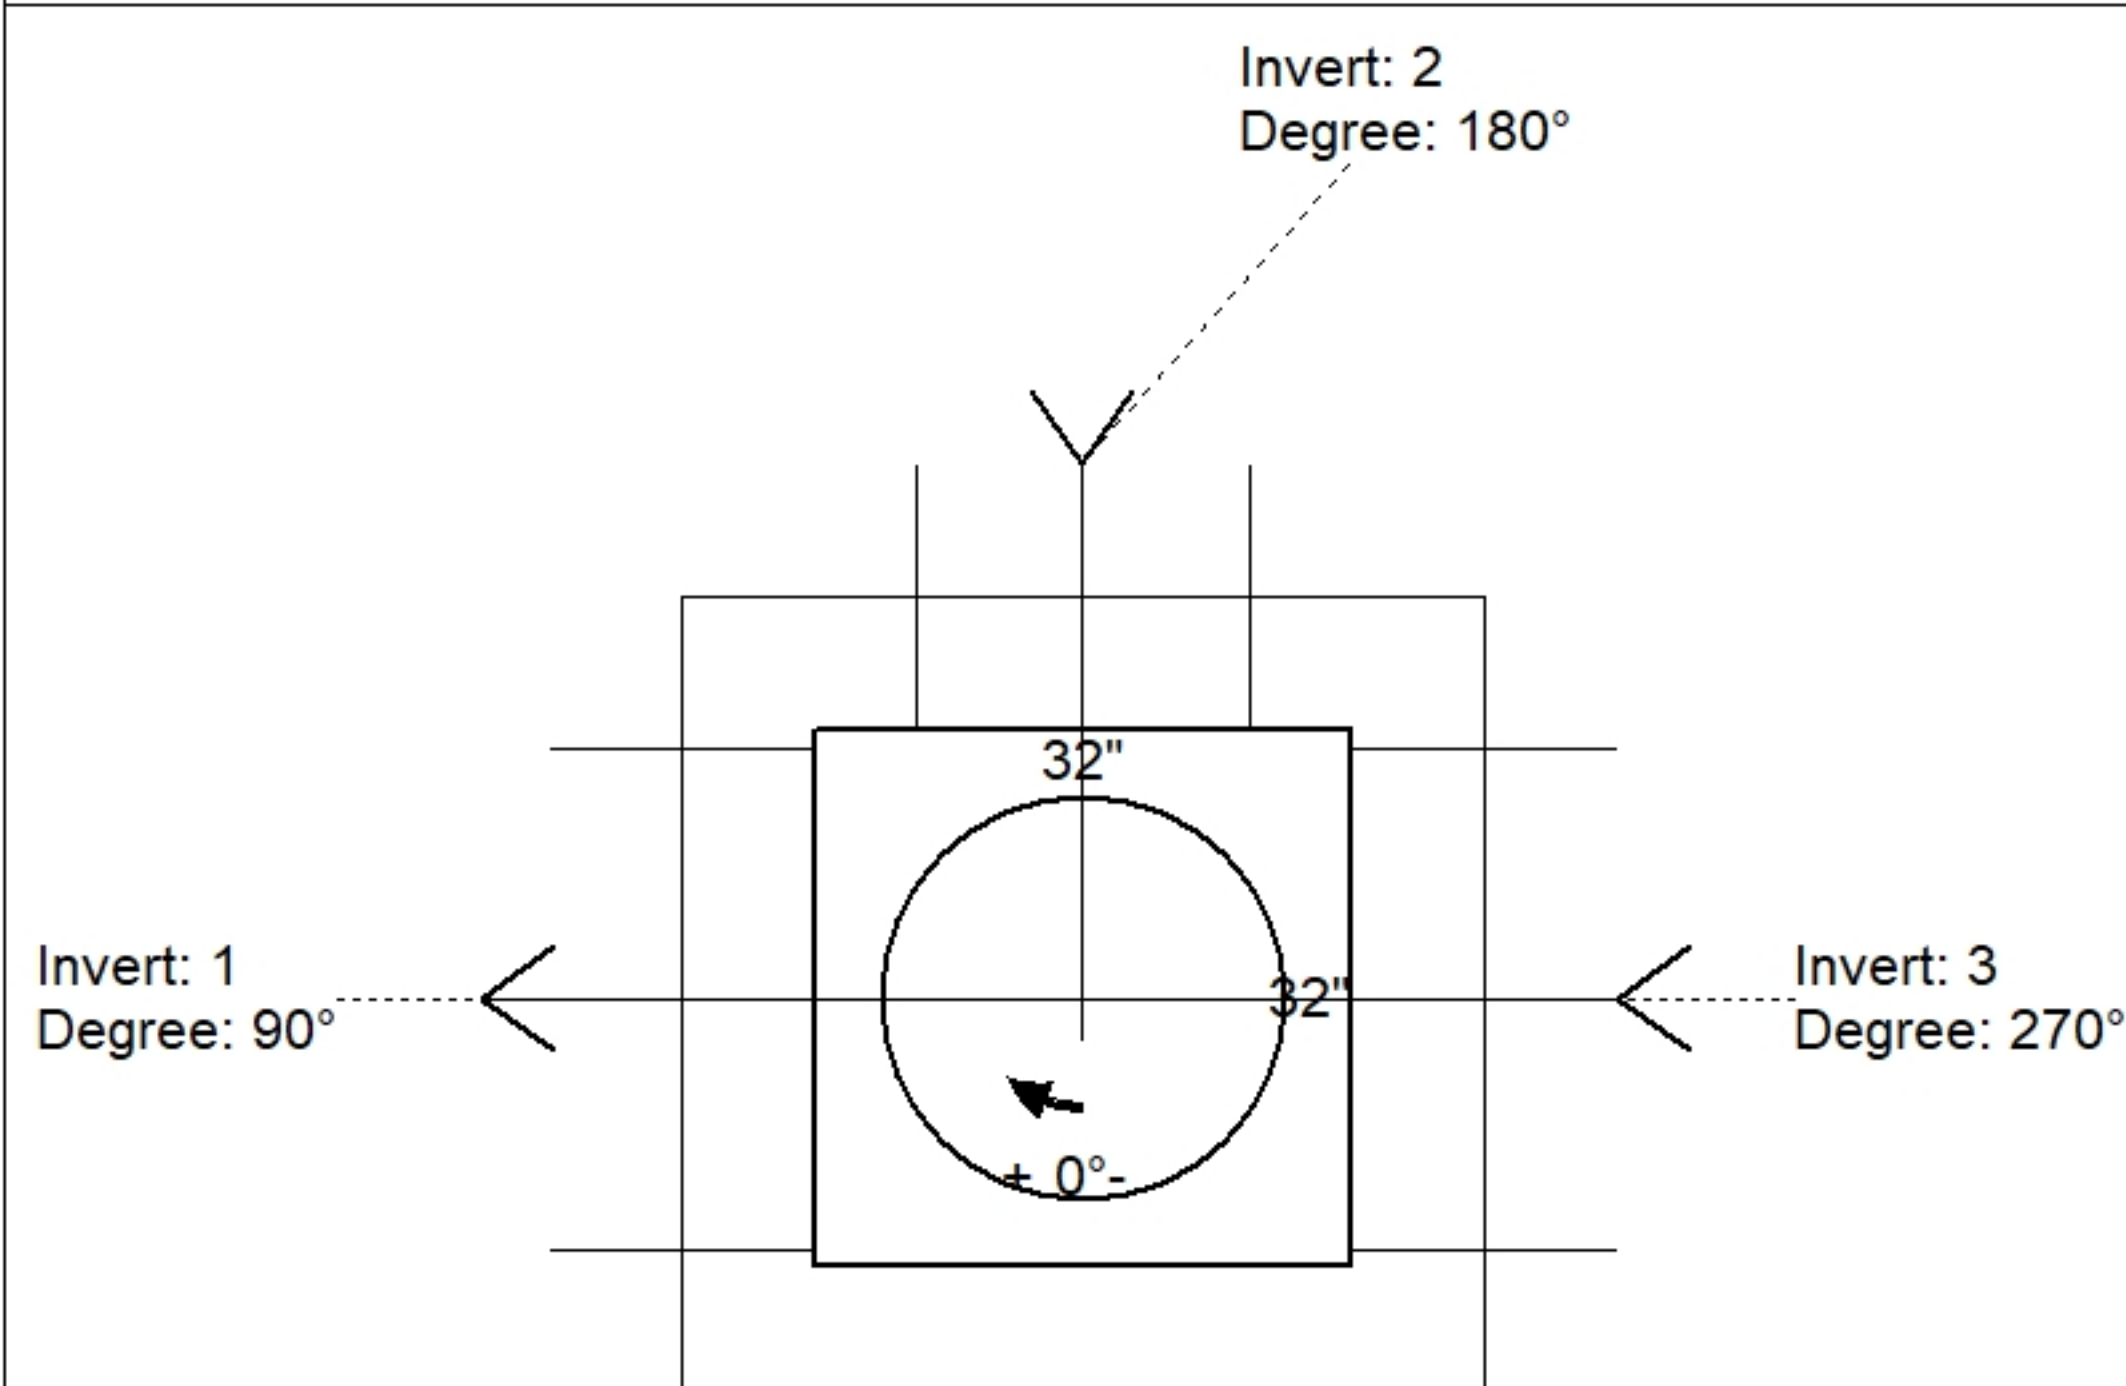

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	527.3'							
Reducer								
Invert 1	520.44'	90°	24" HDPE	27.8"	30"	Hole 30	-1.9"	P1
Invert 2	521.19'	180°	15" HDPE	17.6"	20"	Hole 20	7.7"	P1
Invert 3	520.44'	270°	24" HDPE	27.8"	30"	Hole 30	-1.9"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

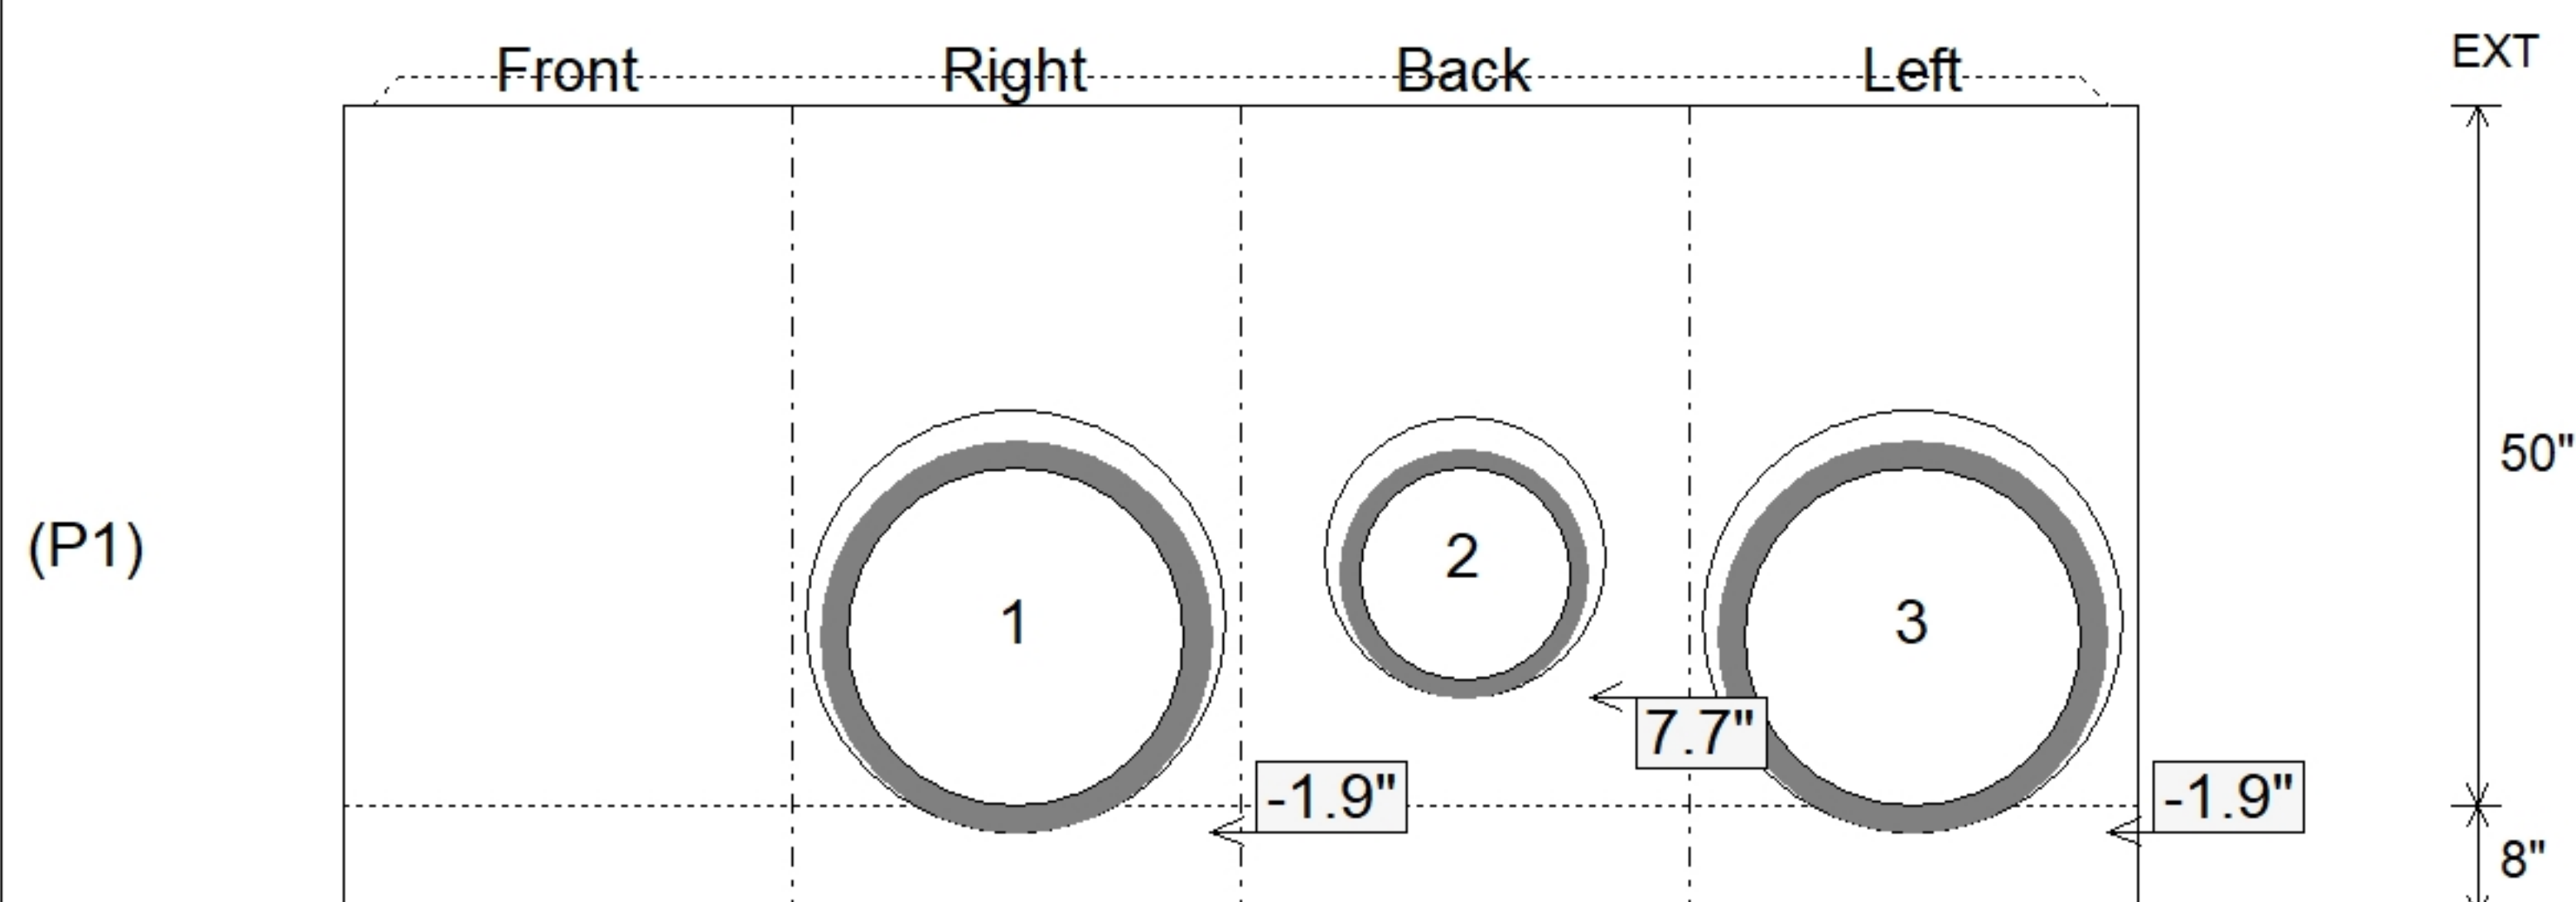

SUBMITTAL
APPROVED BY:
