

Contractor: Scotty's Contracting & Stone, LLC

TECH: J. Horsley

Plant: Beaver Dam



Size: 24" x 60"

Rim to Invert: 3.46'

Floor Height: 8"

Slack: 2.52"



REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. (DBL MAT).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

2) Hole - 4


0 lb

Structure Total: 6599 lb

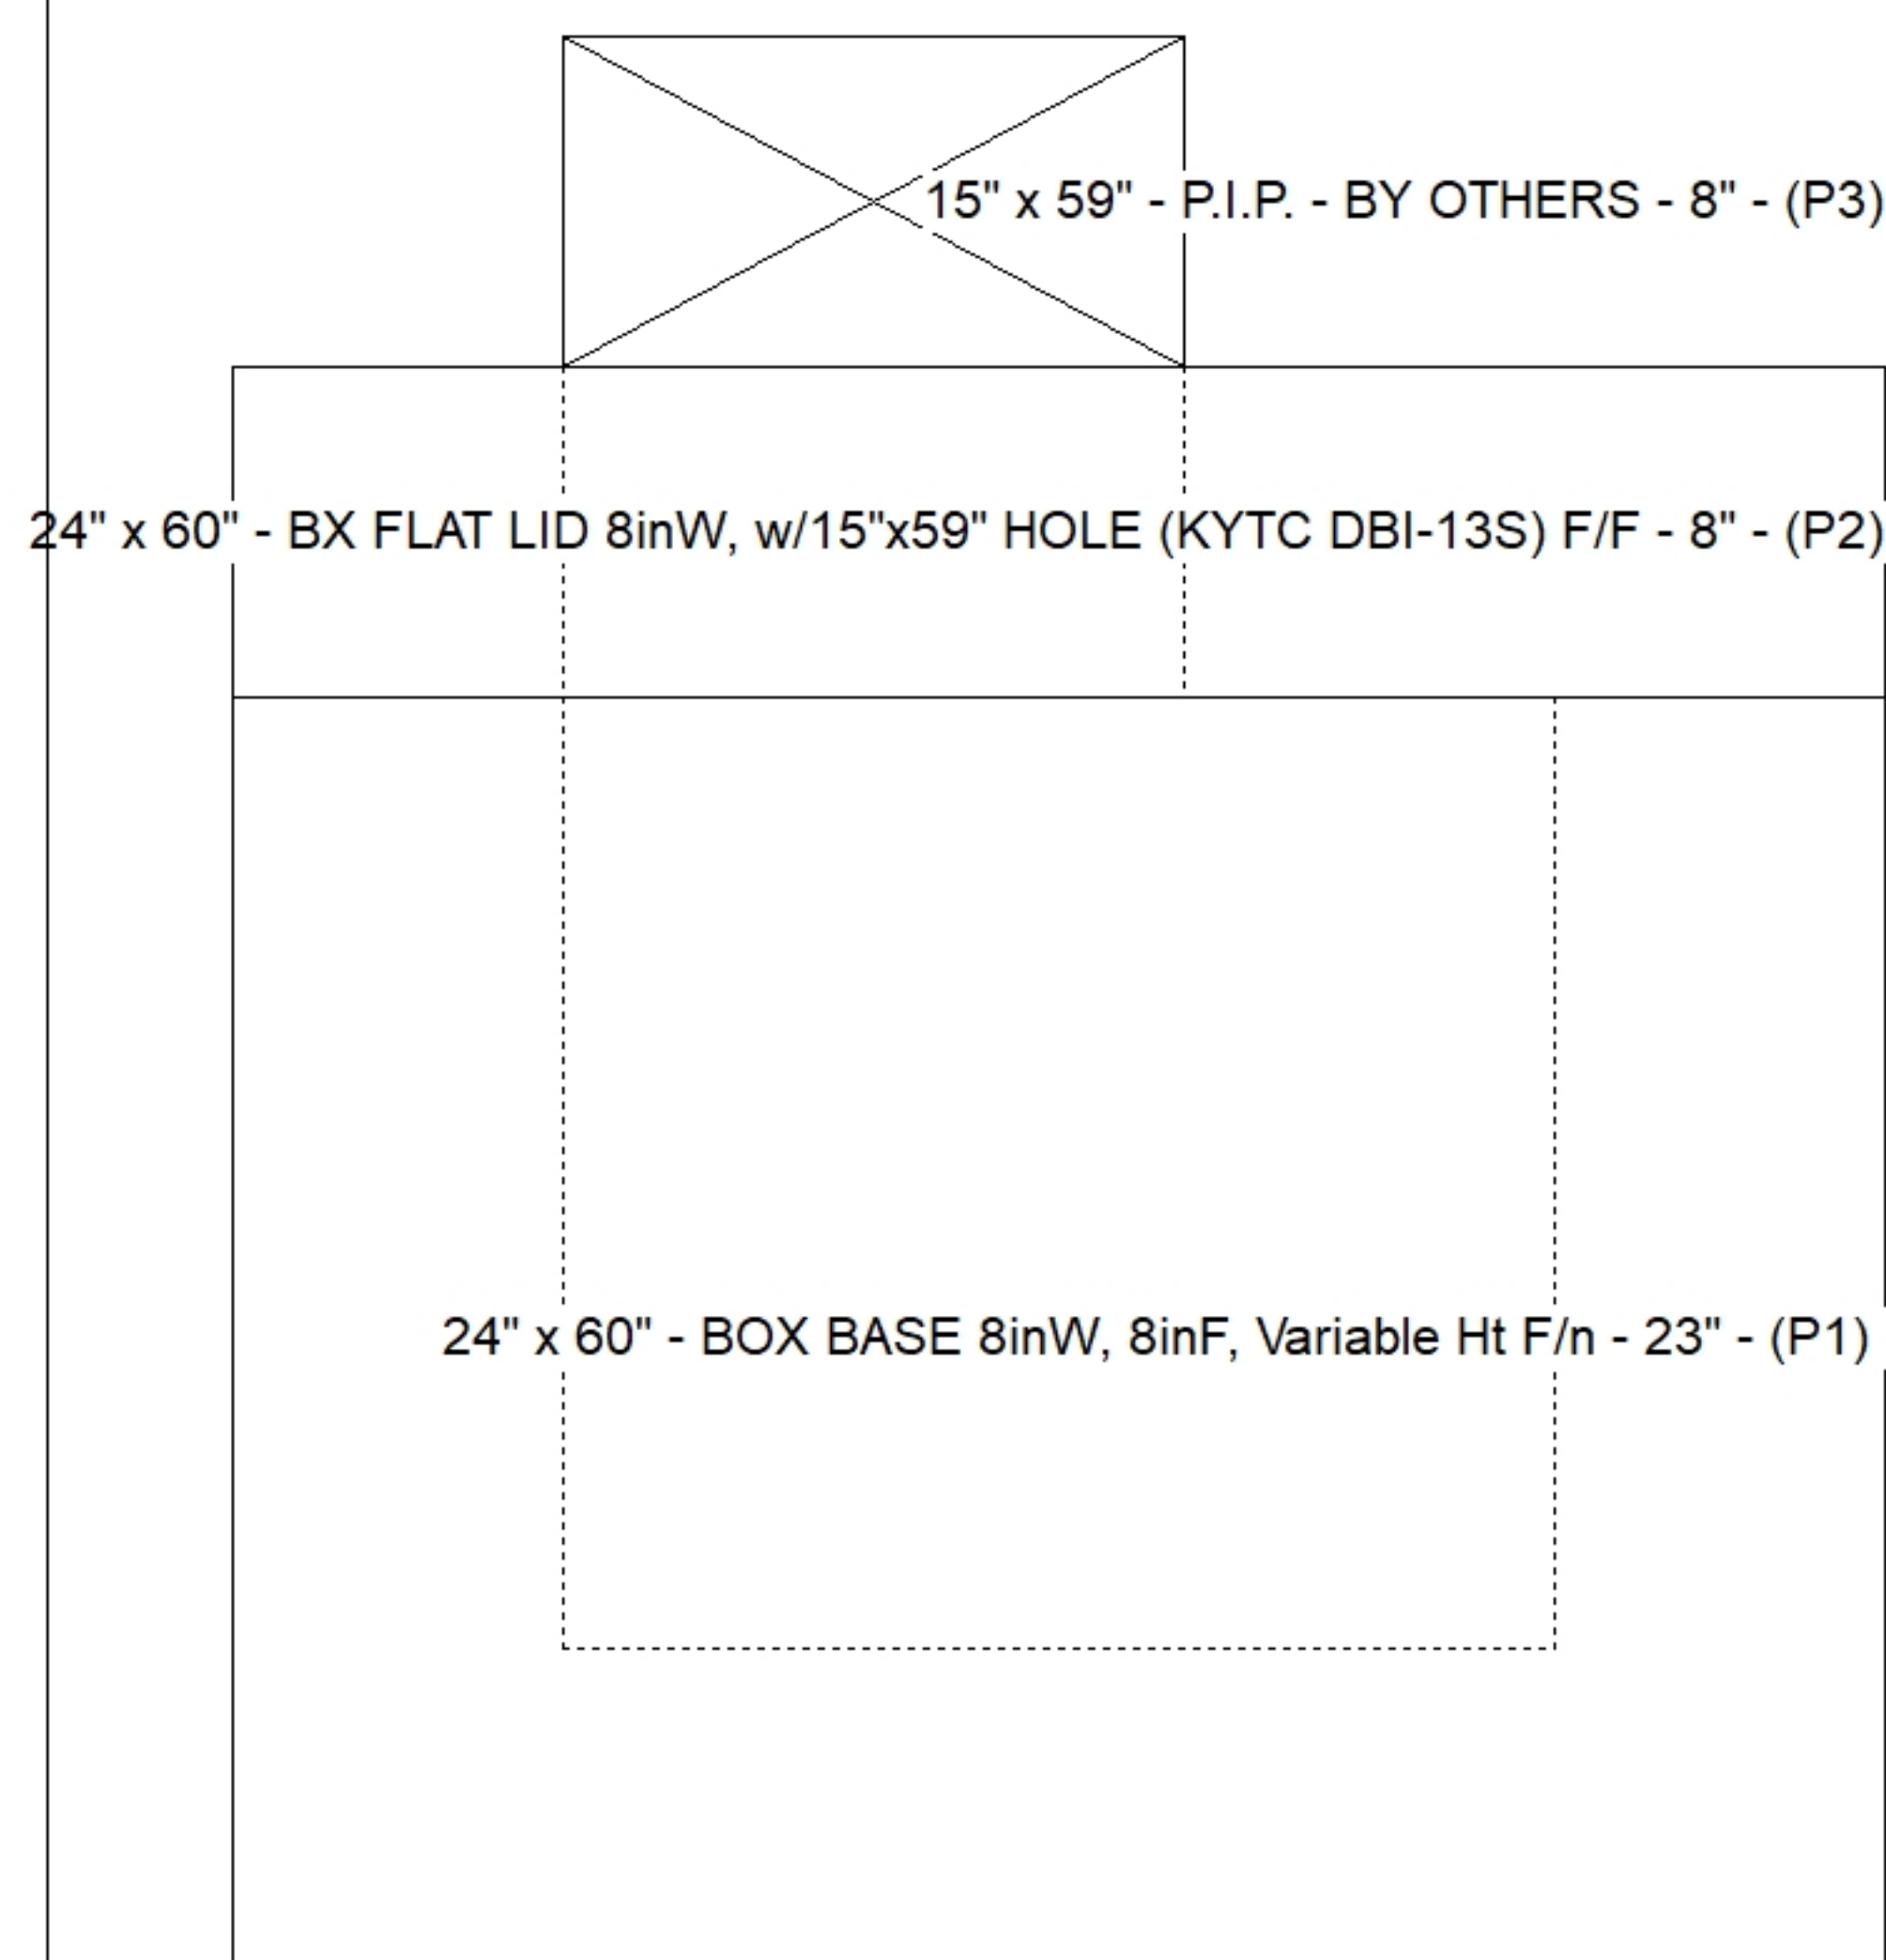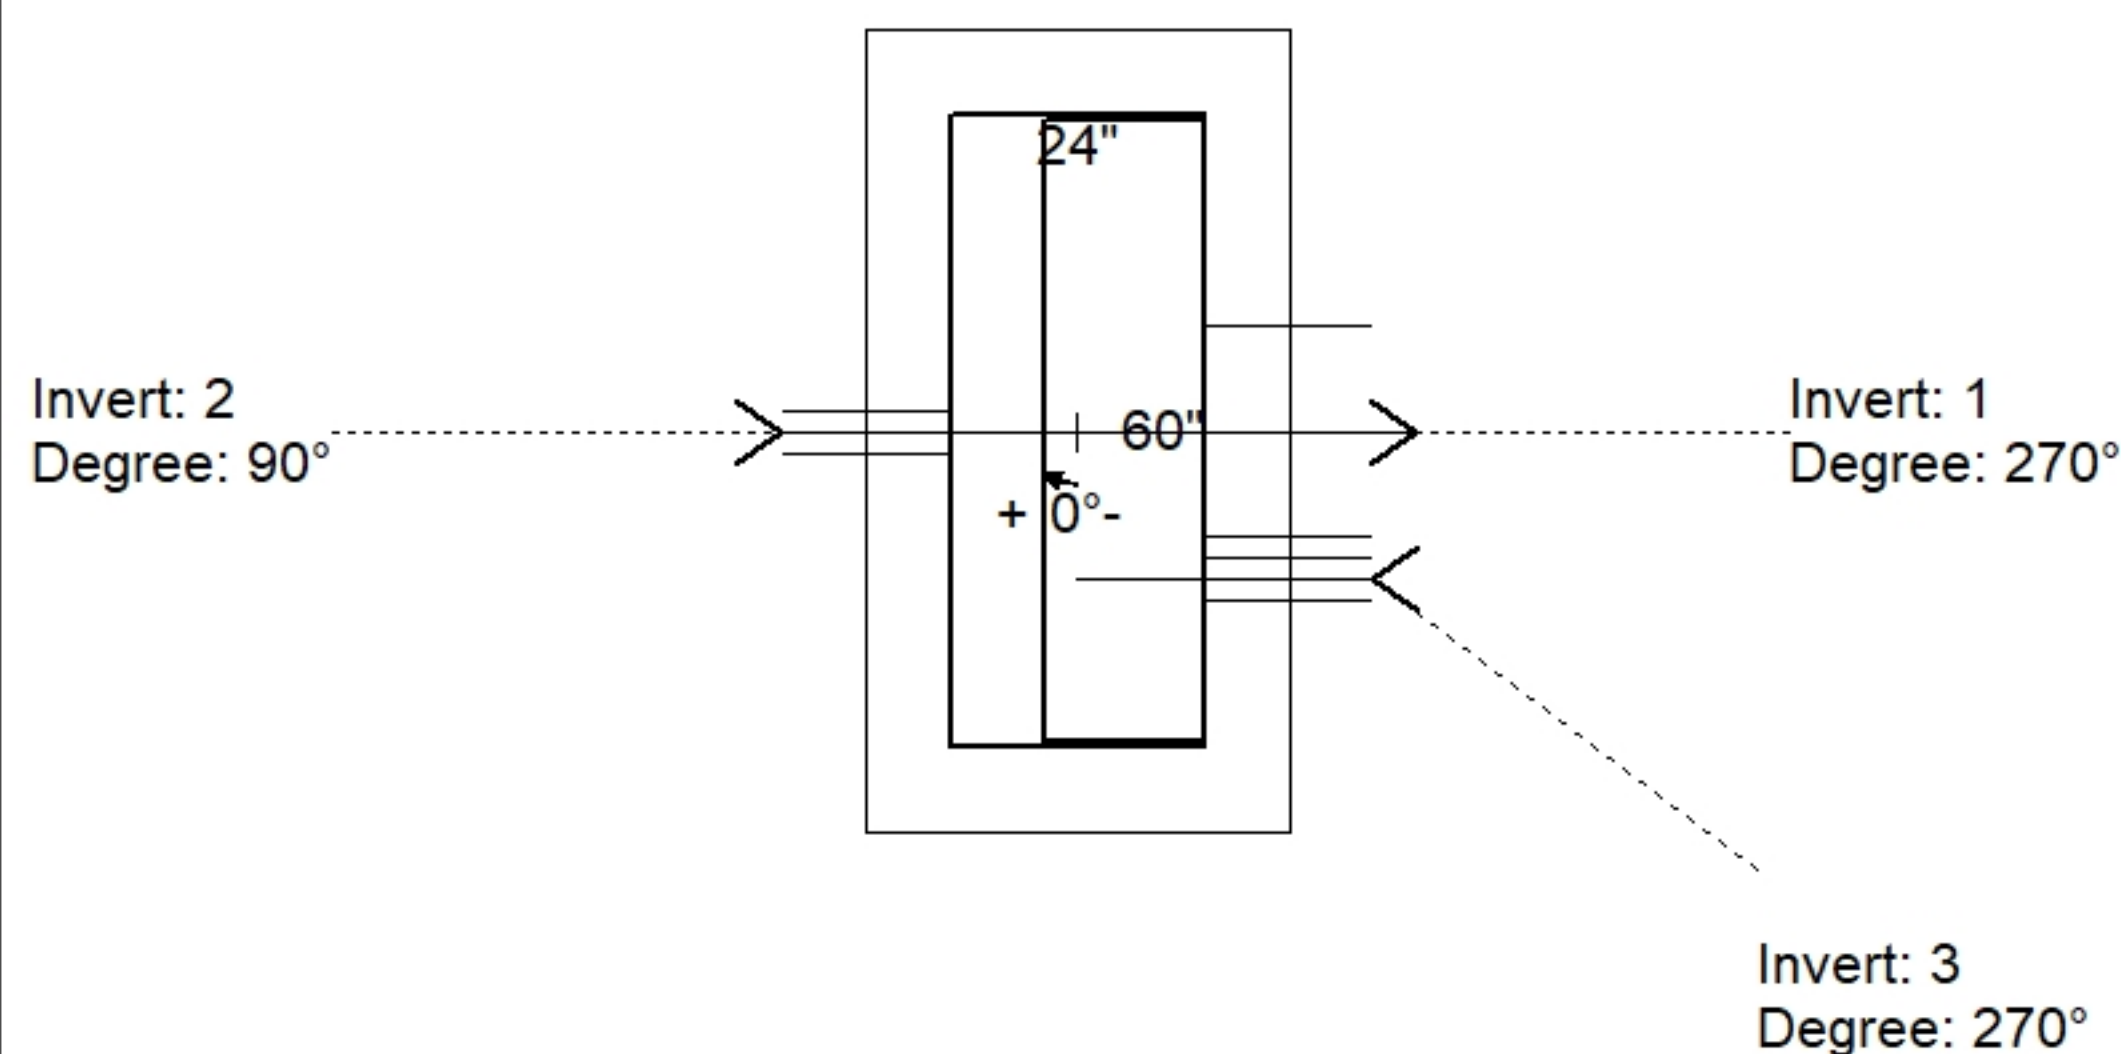

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	524.88'							
Reducer								
Invert 1	521.42'	270°	15" HDPE	17.6"	20"	Hole 20	-1.3"	P1
Invert 2	522.66'	90°	4" WEEP HOLE	4"	4"	Hole 4	14.88"	P1
Invert 3	522.66'	270°	4" WEEP HOLE	4"	4"	Hole 4	14.88"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

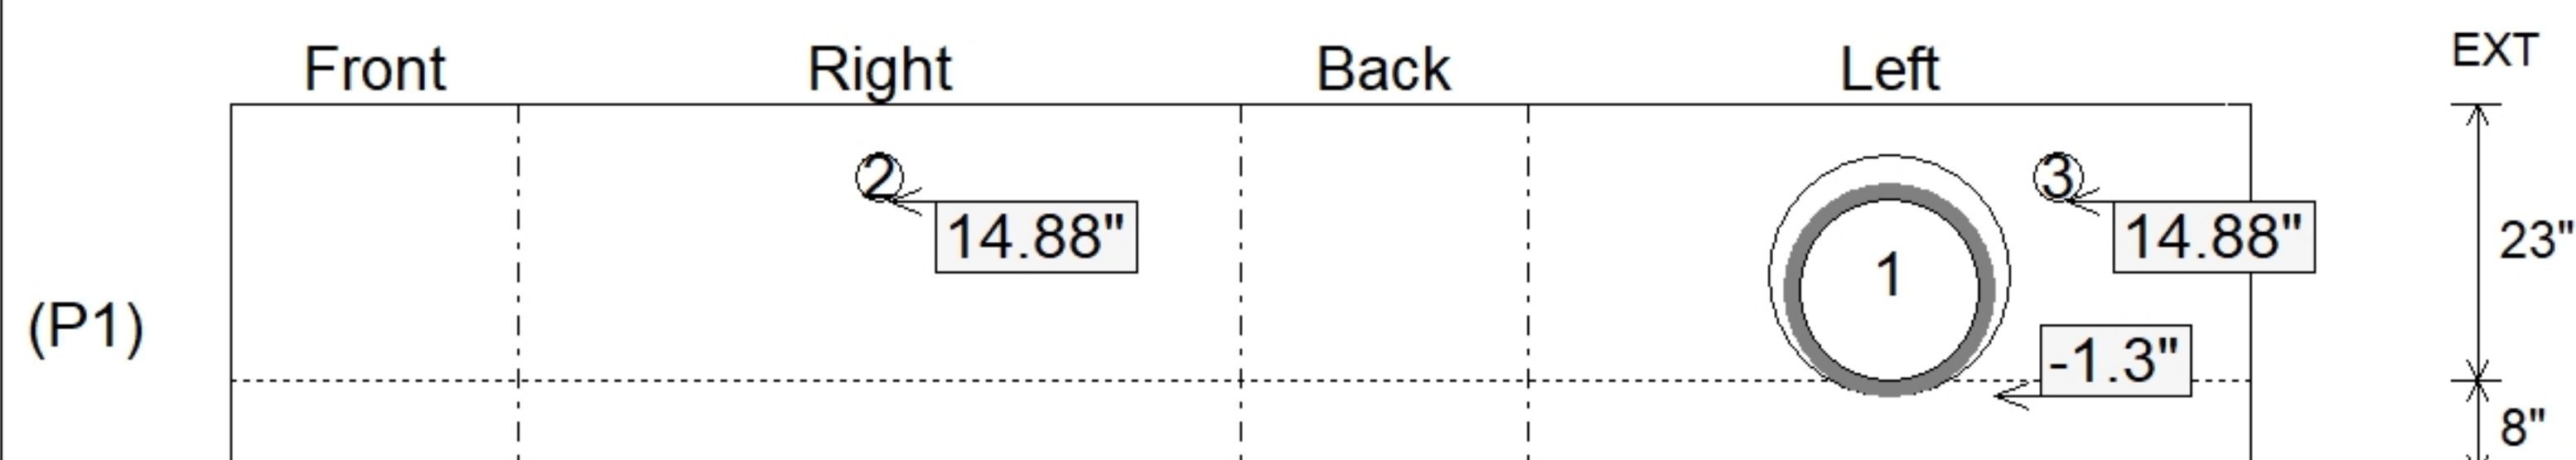

SUBMITTAL
APPROVED BY:
