

**Contractor: Scotty's Contracting & Stone, LLC**

Plant: Beaver Dam



Size: 24" x 30"

Rim to Invert: 4.23'

Floor Height: 8"


Slack: 0.01"

REINFORCING PER ASTM A615 (GRADE 60).  
- WALLS (As .31) #5 BARS AT 12" C.C.E.W..  
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

1) Hole - 20


0 lb

Structure Total: 5855 lb

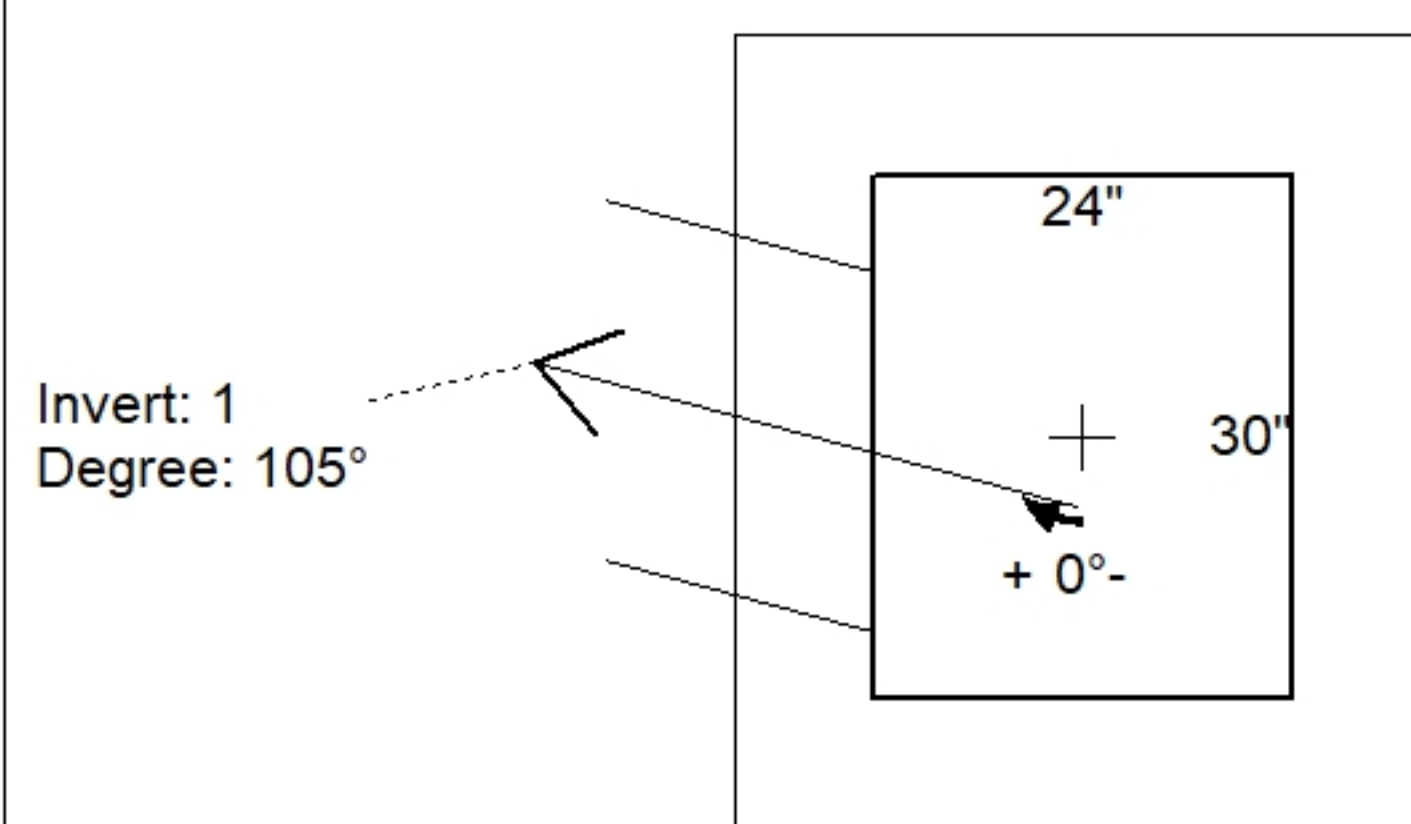

| Position | Elev    | Angle | Pipe     | Pipe OD | Hole | Connector | Up (') | Ref |
|----------|---------|-------|----------|---------|------|-----------|--------|-----|
| Rim      | 526.6'  |       |          |         |      |           |        |     |
| Reducer  |         |       |          |         |      |           |        |     |
| Invert 1 | 522.37' | 105°  | 15" HDPE | 17.6"   | 20"  | Hole 20   | -1.3"  | P1  |
| Invert 2 |         |       |          |         |      |           |        |     |
| Invert 3 |         |       |          |         |      |           |        |     |
| Invert 4 |         |       |          |         |      |           |        |     |
| Invert 5 |         |       |          |         |      |           |        |     |
| Invert 6 |         |       |          |         |      |           |        |     |
| Invert 7 |         |       |          |         |      |           |        |     |
| Invert 8 |         |       |          |         |      |           |        |     |

### Default - Interior Dimensions

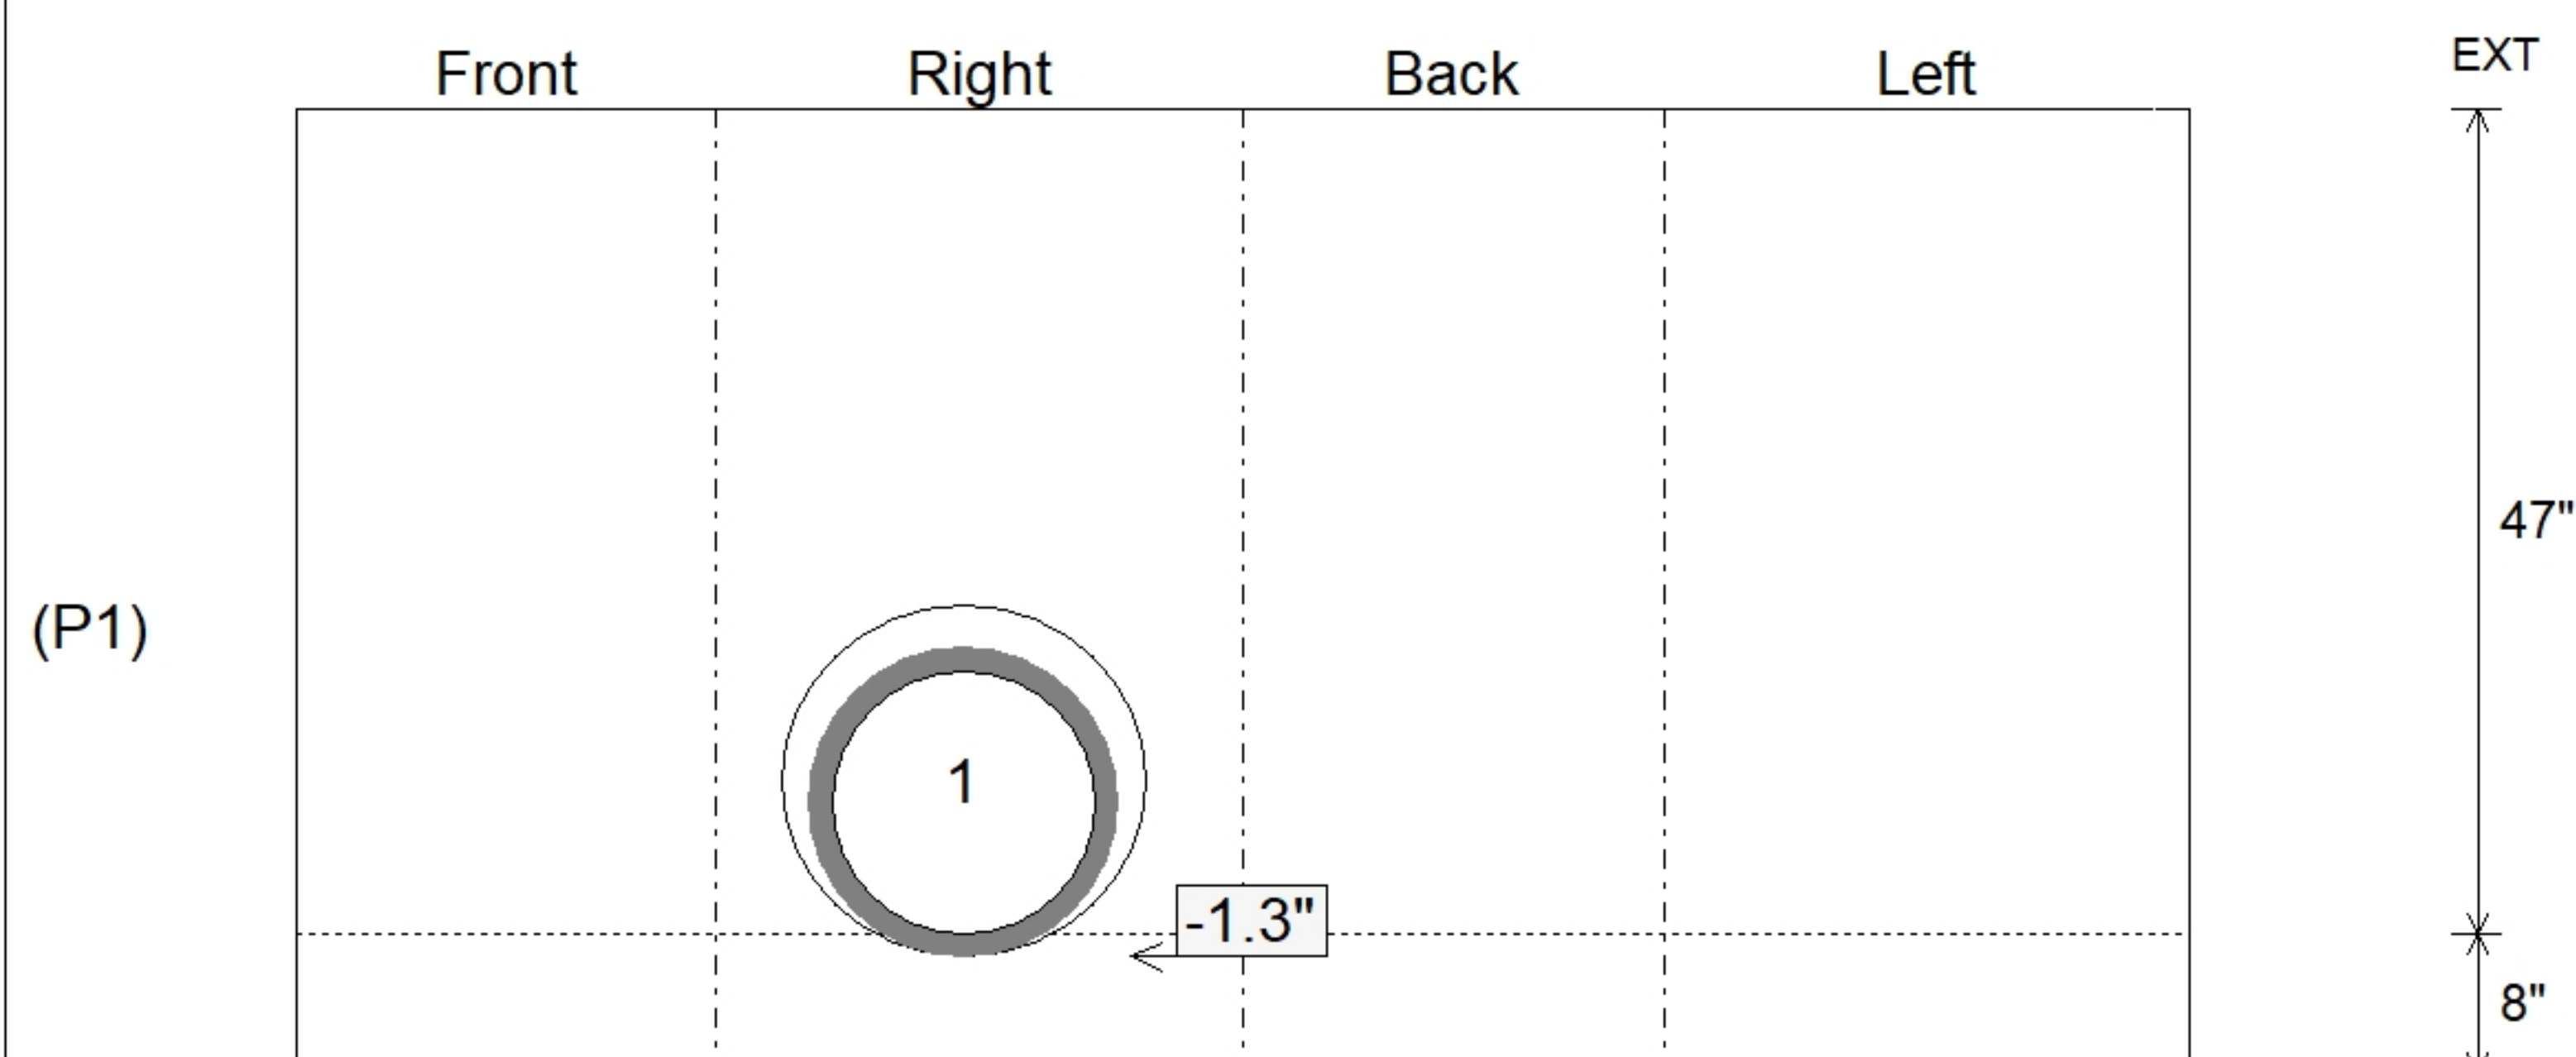

SUBMITTAL  
APPROVED BY:
