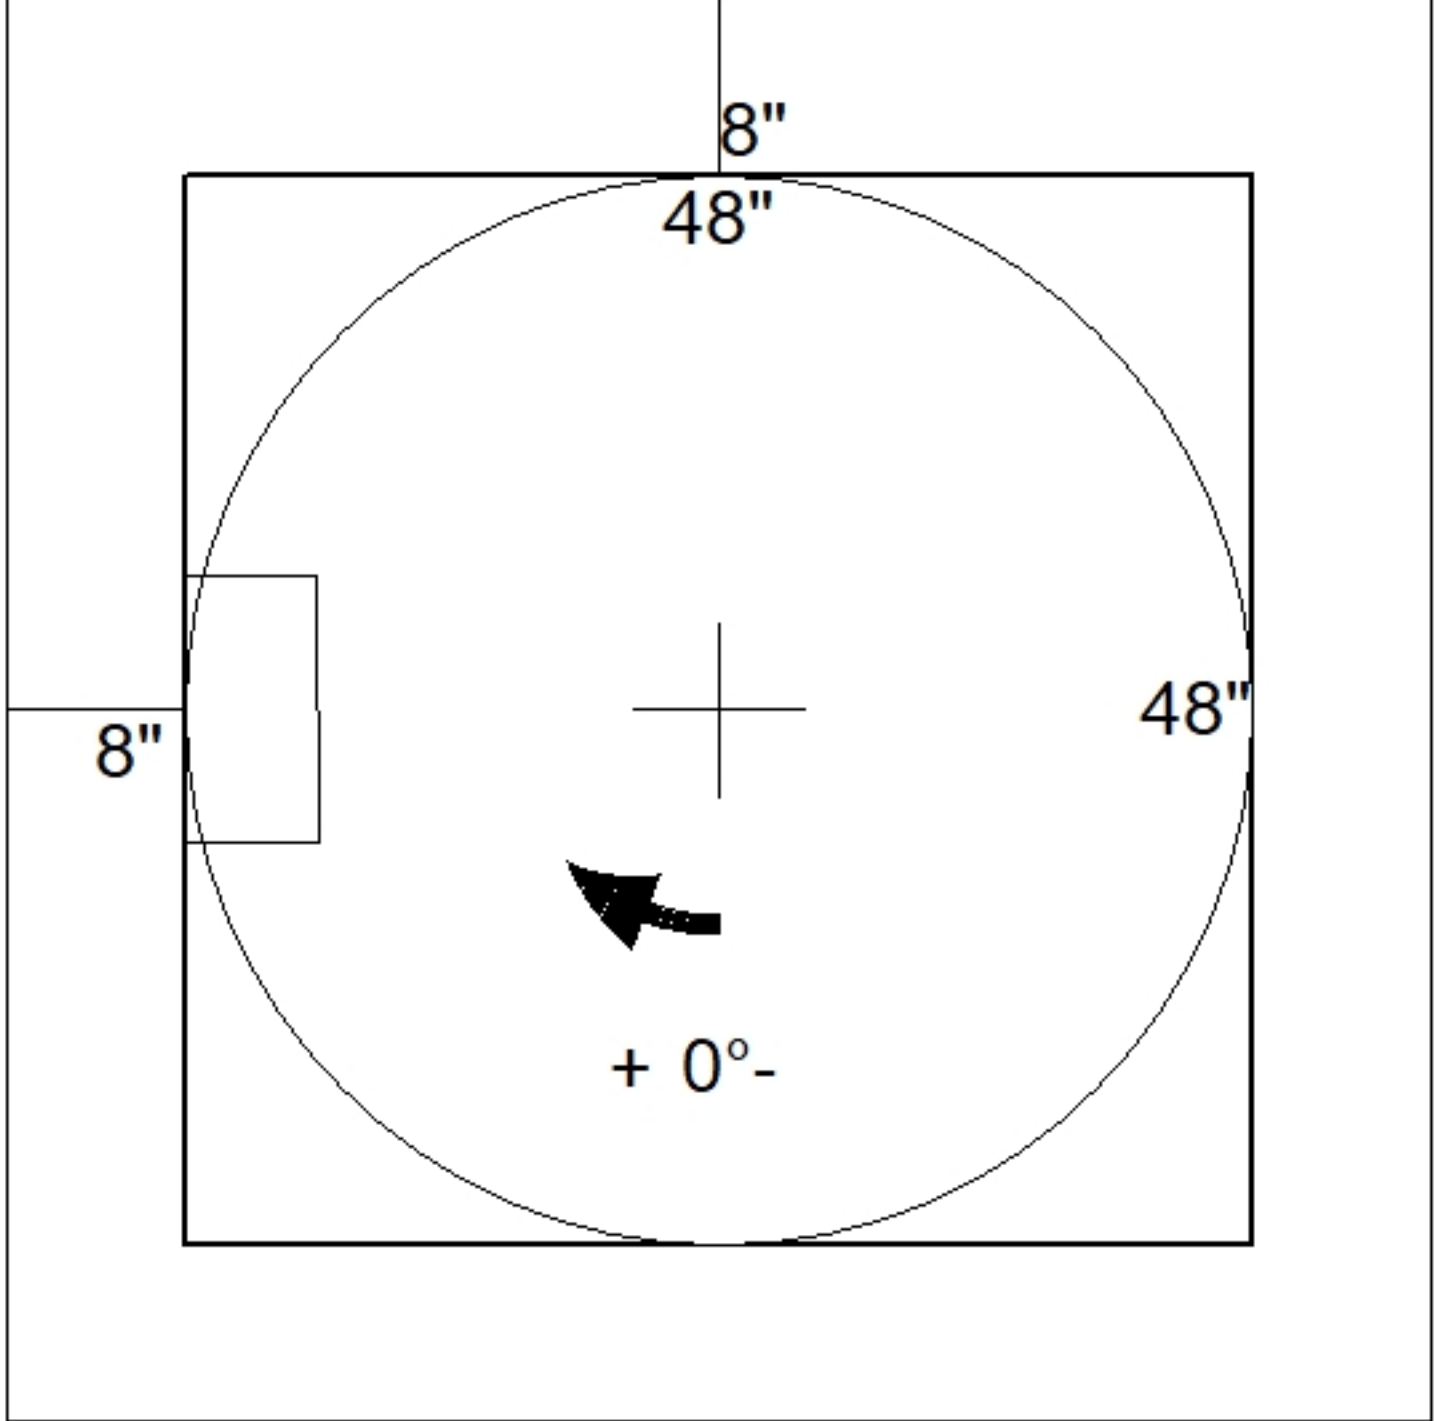
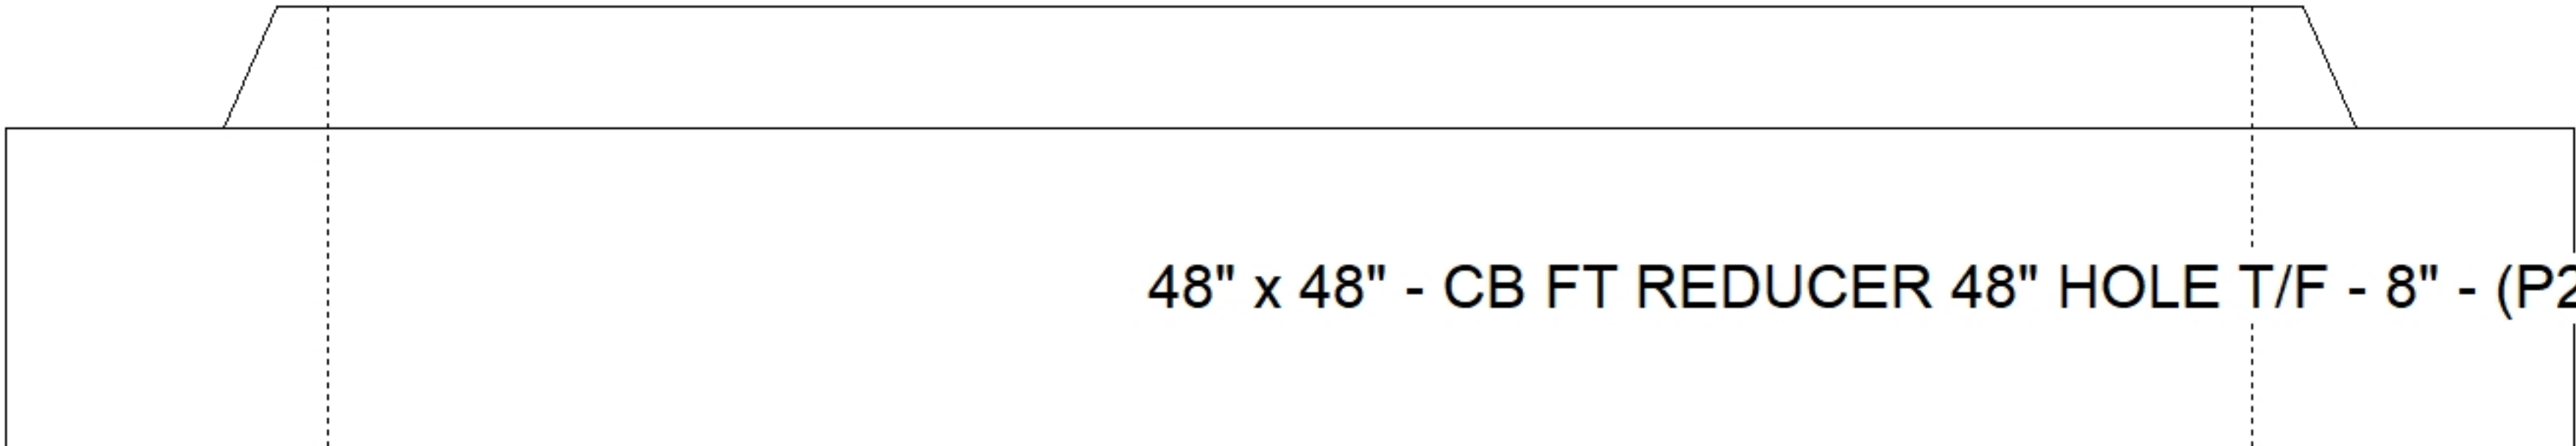


Job Name: 24-4208 - KYTC Christian Co. Call 100 (ID 241018) Job Location: Hopkinsville, KY Contractor: Scotty's Contracting & Stone, LLC		Plant: Beaver Dam 8/3/2026 3:41:25 PM	Tech: J. Horsley PC: C. Goff		
Structure ID: MH277 (439+85 RT)					
P2 BX048048-08TS48		CB FT REDUCER 48" HOLE T/F			
P4) 24" - CASTING HEIGHT - 8" P3) 48" - ECC CONE w/ 24" HOLE F/G - 36" P2) 48" x 48" - CB FT REDUCER 48" HOLE T/F - 8" P1) 48" x 48" - BX BASE w/FLANGE 08W/12F/08EF F/n - 60" 1) CASTING - HOE KY-510 F/C (KY TY.2) 1) 48" x 48" - Conseal CS-102 1.00" 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 44 1) Hole - 20		0 lb 3000 lb 1535 lb 13214 lb 510 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 18259 lb Structure Total:	Structure Notes: . ** KYTC STATE PROJECT** 1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE KY-510 F/C) 4. SECONDARY POUR REQ'D FOR EXTENDED FLANGE (8"WD x 12" THICK). . REINFORCING PER ASTM A615 (GRADE 60). - TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT). - WALLS #5's AT 6" C.C.E.W. - FLOOR #5's AT 12" C.C.E.W..		
					
					
Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 8"	Weight (Net): 1535 lb Volume (Net): 0.39cu.yd	
