

Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam



Size: 48" x 48"

Rim to Invert: 7.9'

Floor Height: 12"


Slack: 0.8"

- FLOOR #5's AT 12" C.C.E.W..


8) MH Step ML-10-TDS-NCR - 10"

0 lb


Structure Total: 15818 lb

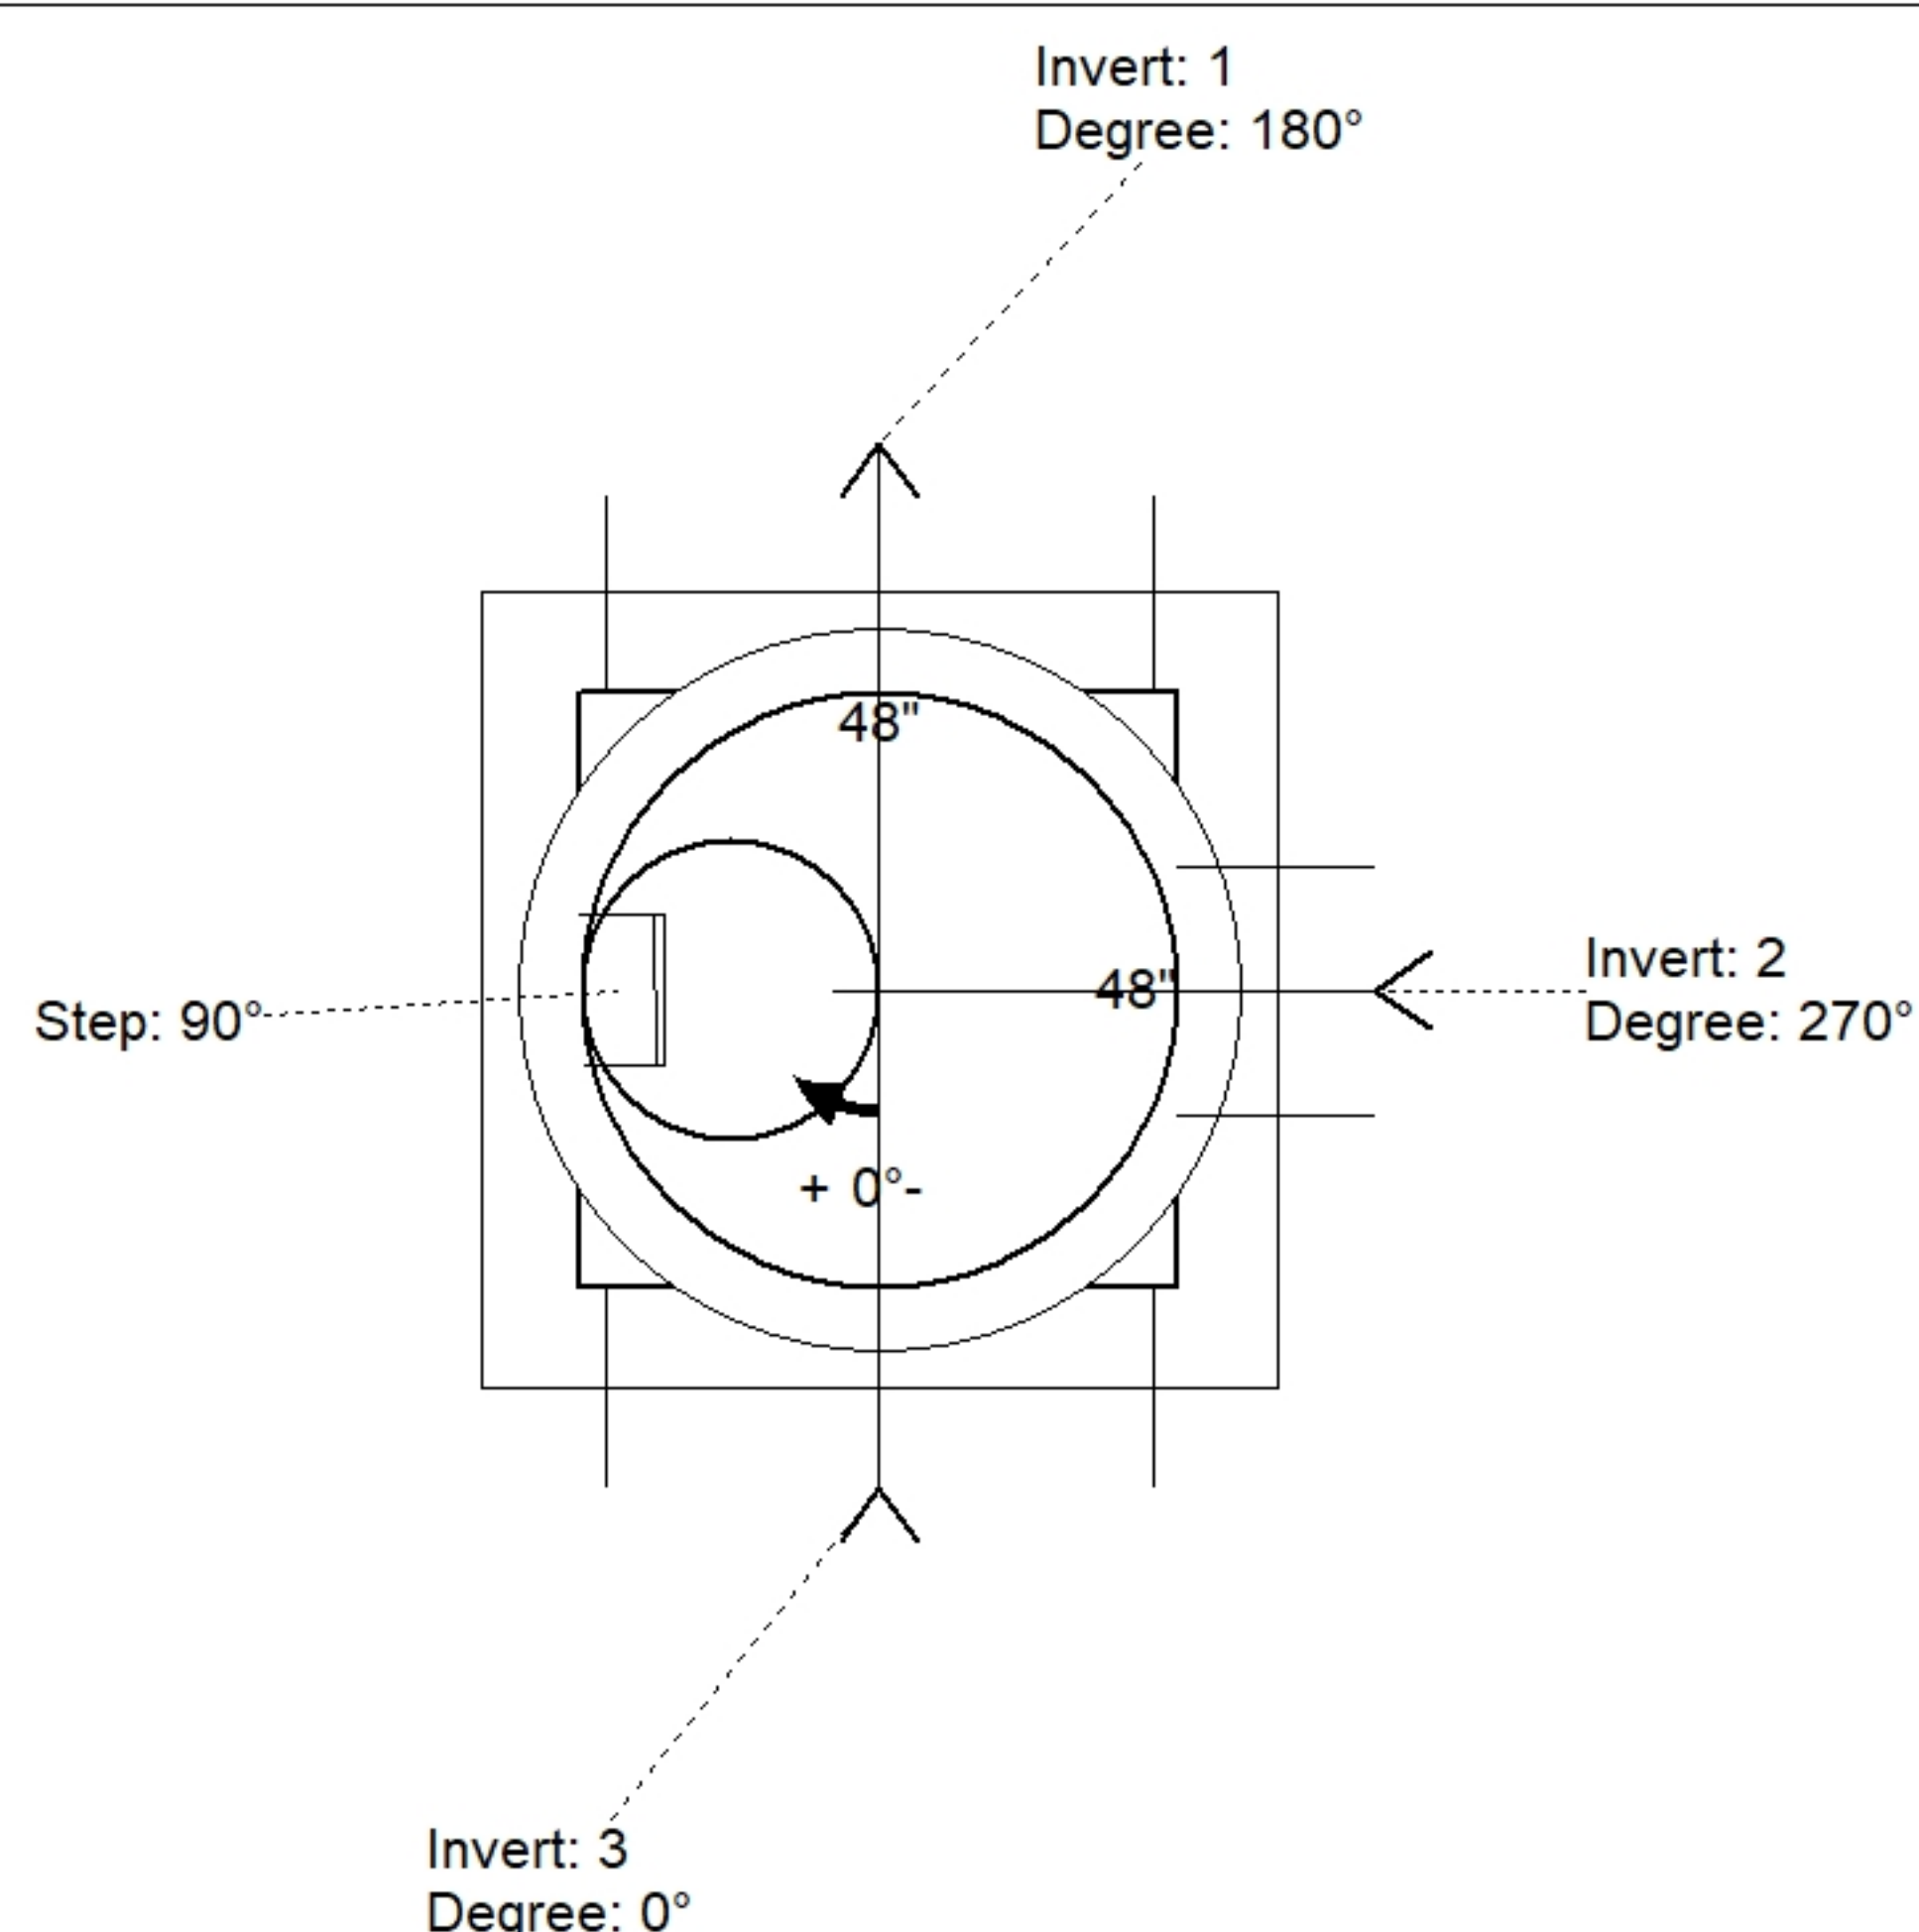

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	537'							
Reducer	533.6'							
Invert 1	529.1'	180°	36" HDPE	41.7"	44"	Hole 44	-2.85"	P1
Invert 2	530.85'	270°	15" HDPE	17.6"	20"	Hole 20	19.7"	P1
Invert 3	529.1'	0°	36" HDPE	41.7"	44"	Hole 44	-2.85"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

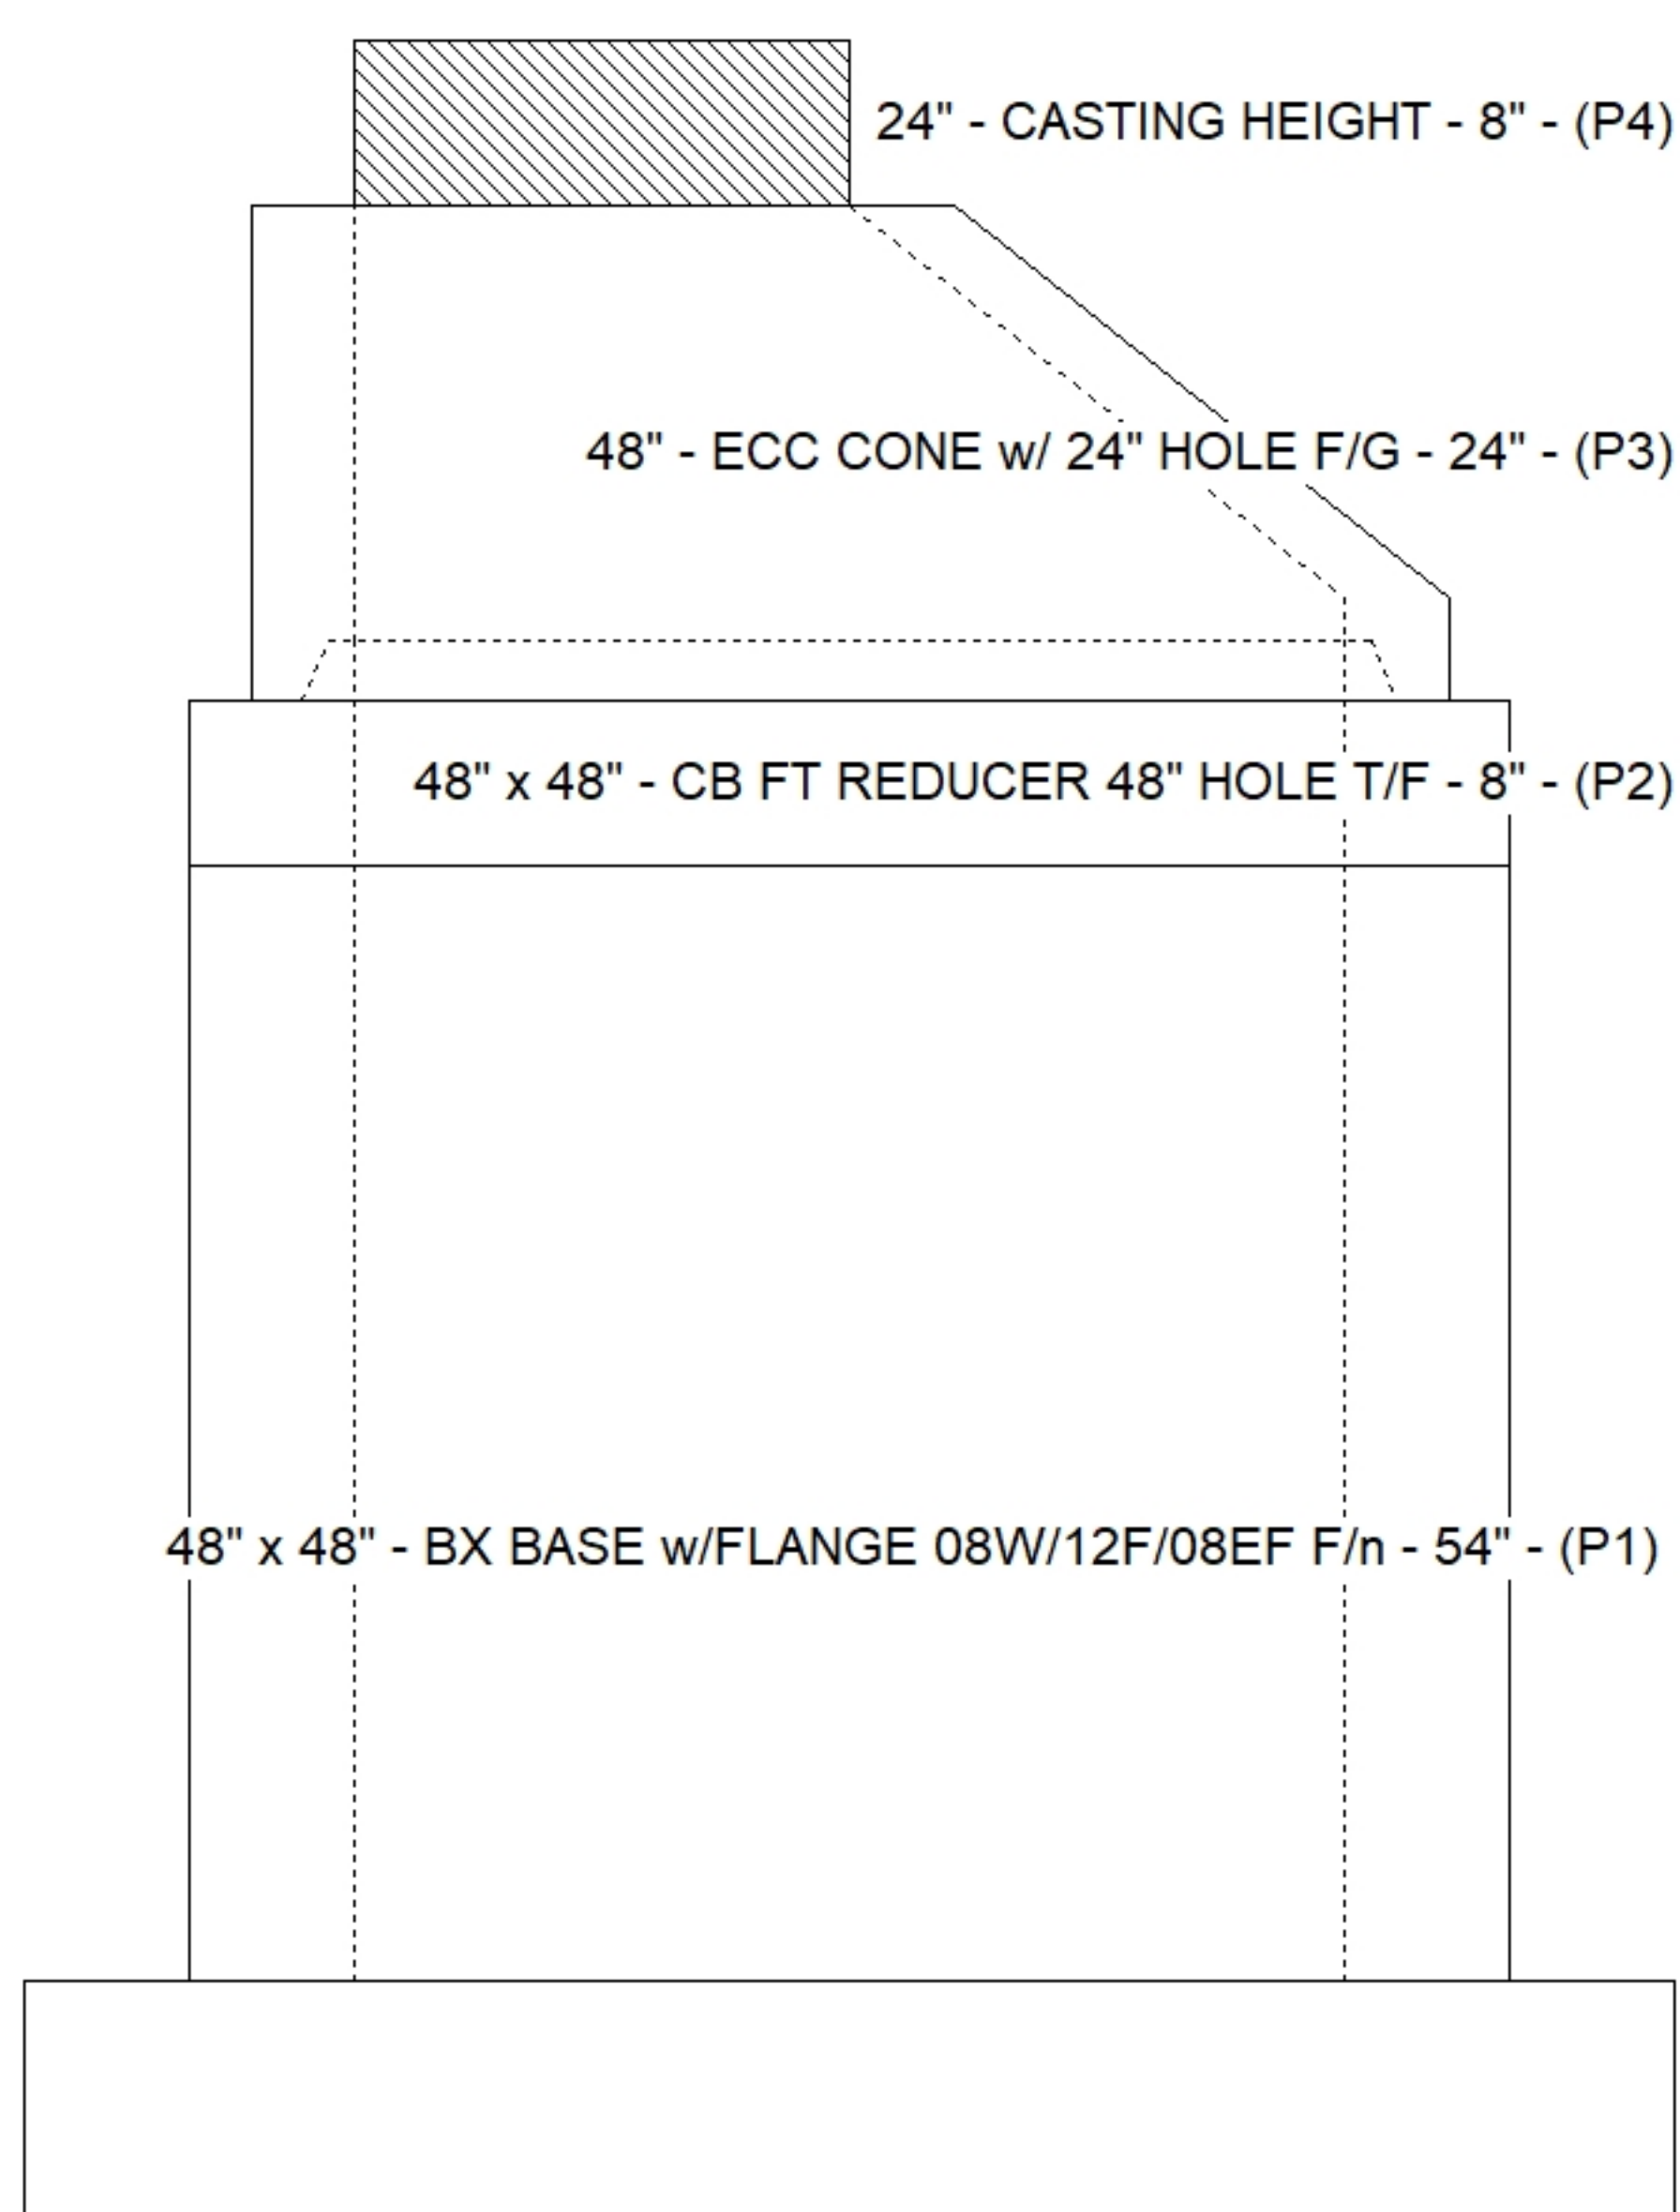

Default - Interior Dimensions

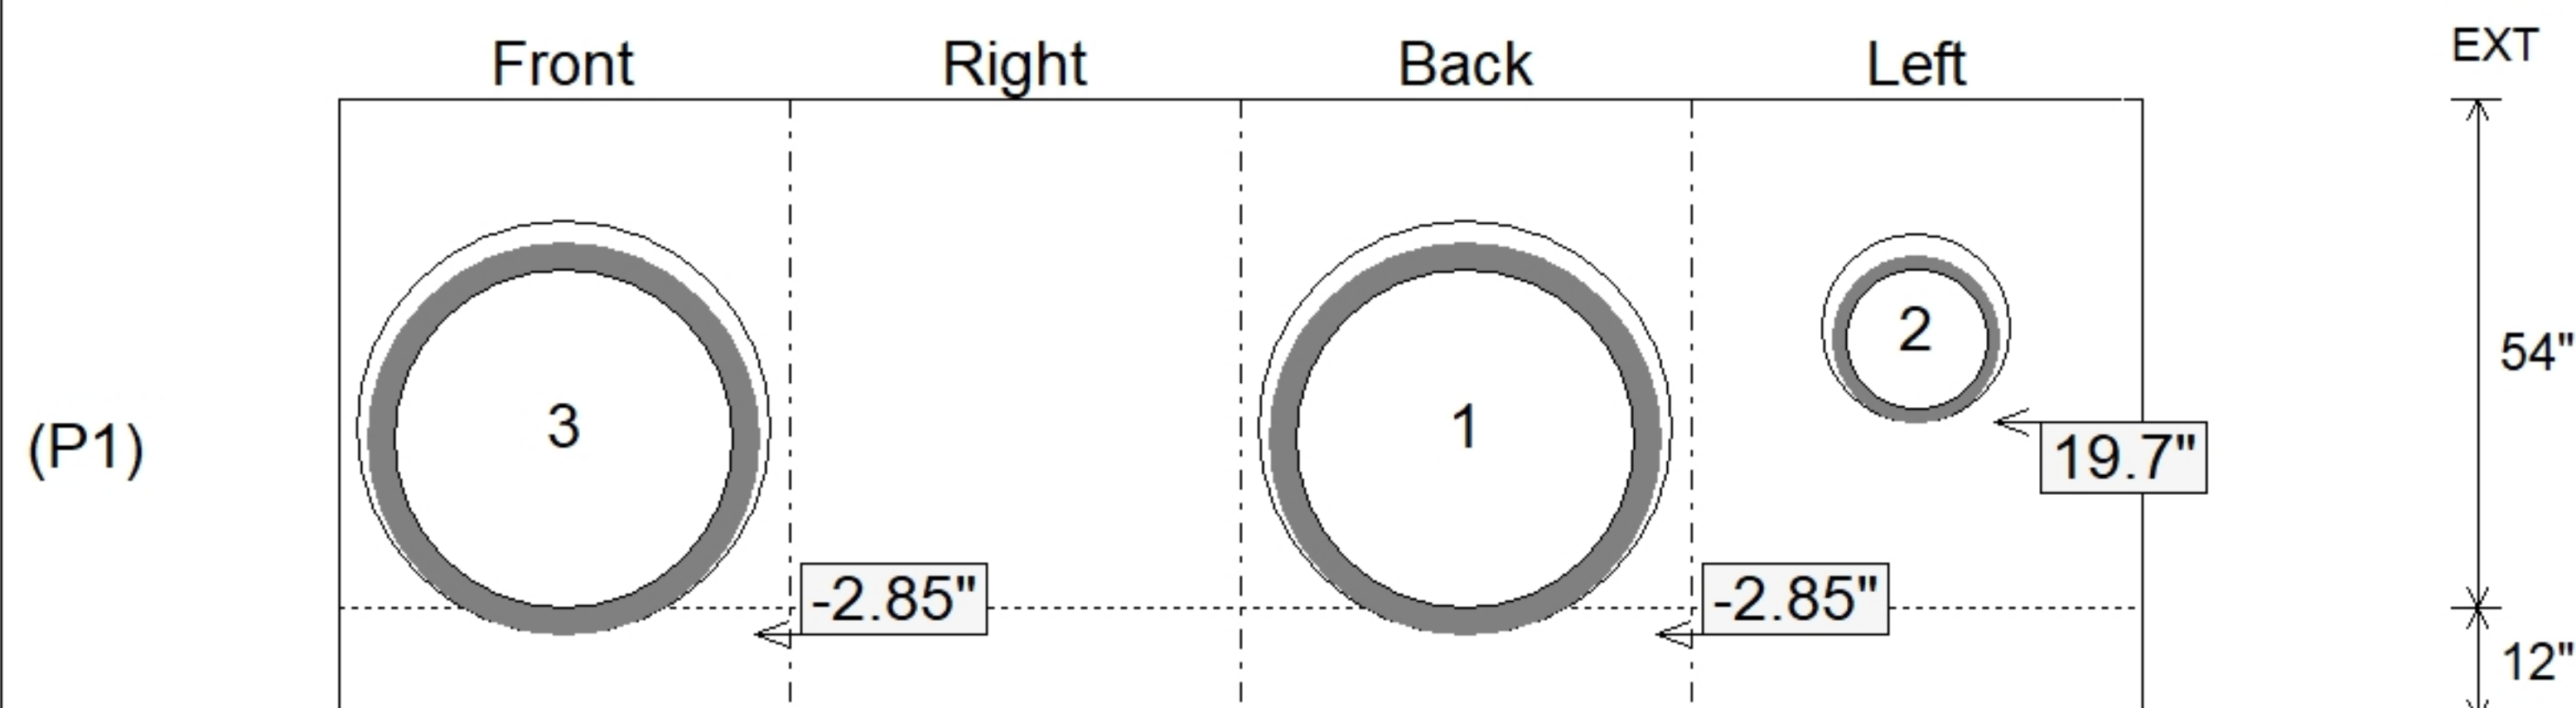

SUBMITTAL
APPROVED BY:
