


Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam



Slack: 0.12"

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌋)	Ref
Rim	527.79'							
Reducer								
Invert 1	520.78'	180°	42" HDPE	47.7"	52"	Hole 52	-3.15"	P1
Invert 2	523.03'	270°	15" HDPE	17.6"	20"	Hole 20	25.7"	P1
Invert 3	520.78'	0°	42" HDPE	47.7"	52"	Hole 52	-3.15"	P1
Invert 4	525.985'	0°	7" x 9" I-Beam Notch	7" x 9"	7" x 9"	I-Beam Notch 7"x9"x5"	58.96"	P1
Invert 5	525.985'	180°	7" x 9" I-Beam Notch	7" x 9"	7" x 9"	I-Beam Notch 7"x9"x5"	58.96"	P1
Invert 6								
Invert 7								
Invert 8								

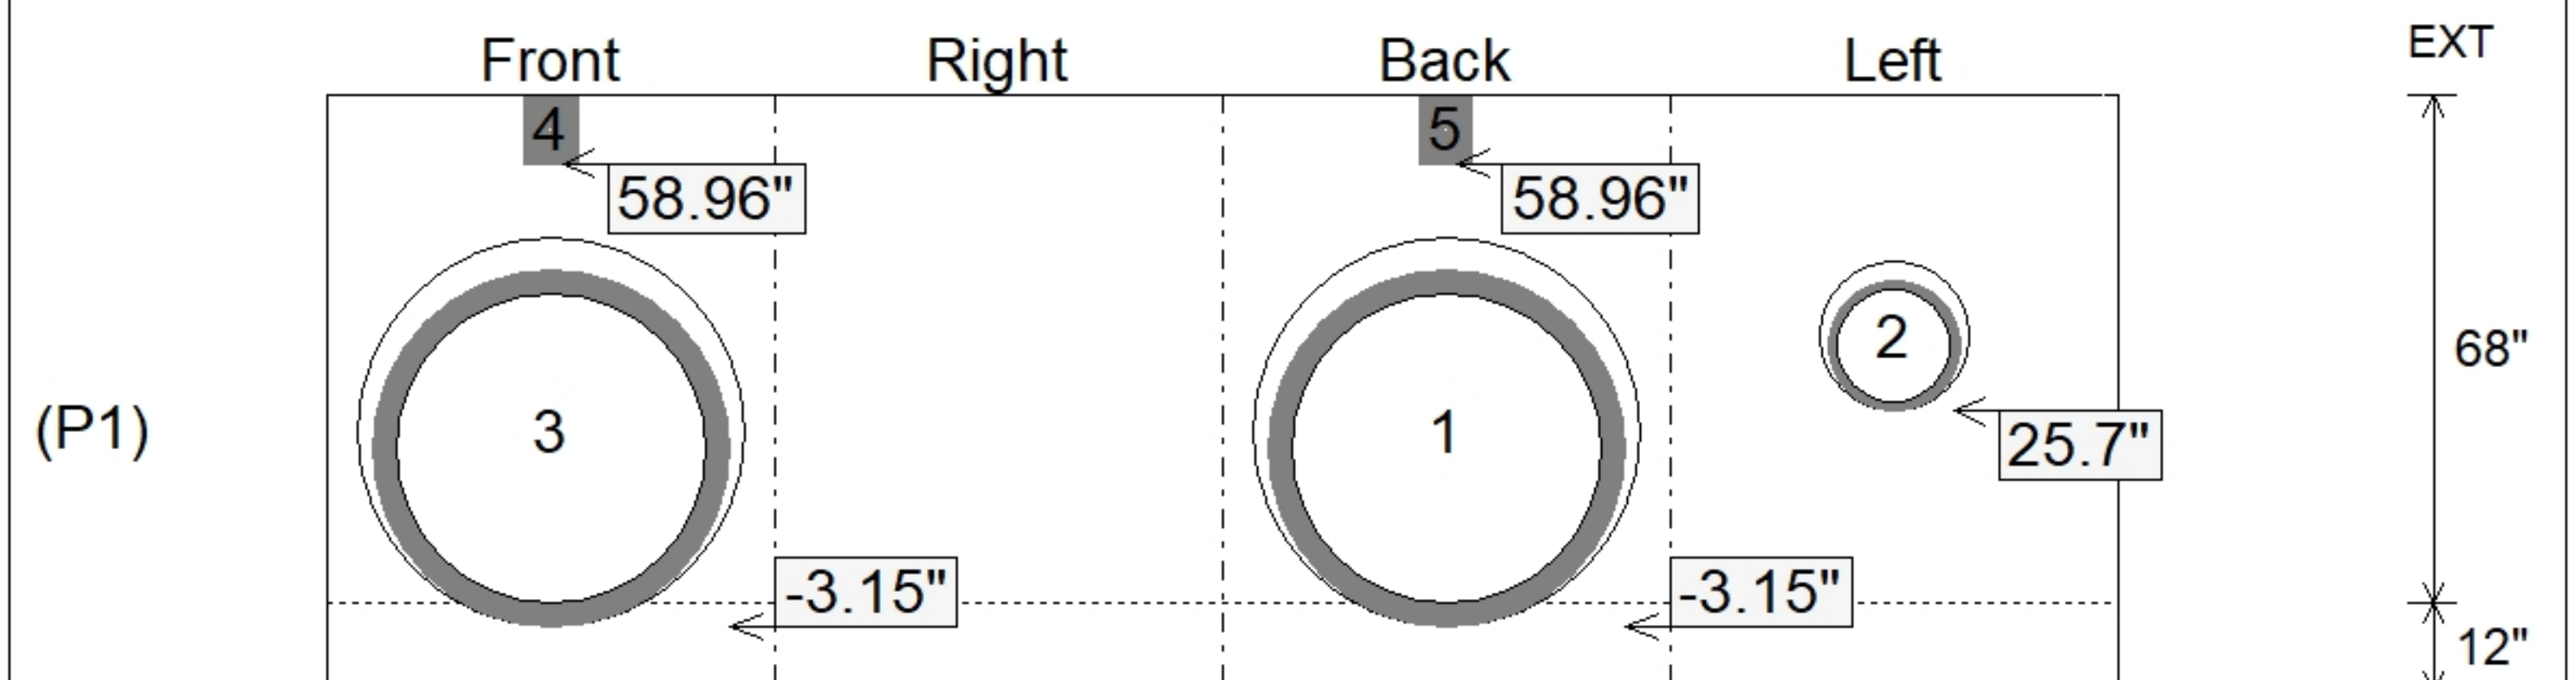

SUBMITTAL
APPROVED BY:
