


Contractor: Scotty's Contracting & Stone, LLC

Plant: Beaver Dam



Slack: 0.96"

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	527.06'							
Reducer								
Invert 1	518.98'	270°	48" HDPE	53.5"	56"	Hole 56	-2.95"	P1
Invert 2	519.48'	90°	42" HDPE	47.7"	50"	Hole 50	2.85"	P1
Invert 3	521.48'	160°	18" RCP B WALL	23"	26"	Hole 26	27.5"	P1
Invert 4	525.185'	90°	7" x 9" I-Beam Notch	7" x 9"	7" x 9"	I-Beam Notch 7"x9"x5"	70.96"	P1
Invert 5	525.185'	270°	7" x 9" I-Beam Notch	7" x 9"	7" x 9"	I-Beam Notch 7"x9"x5"	70.96"	P1
Invert 6								
Invert 7								
Invert 8								

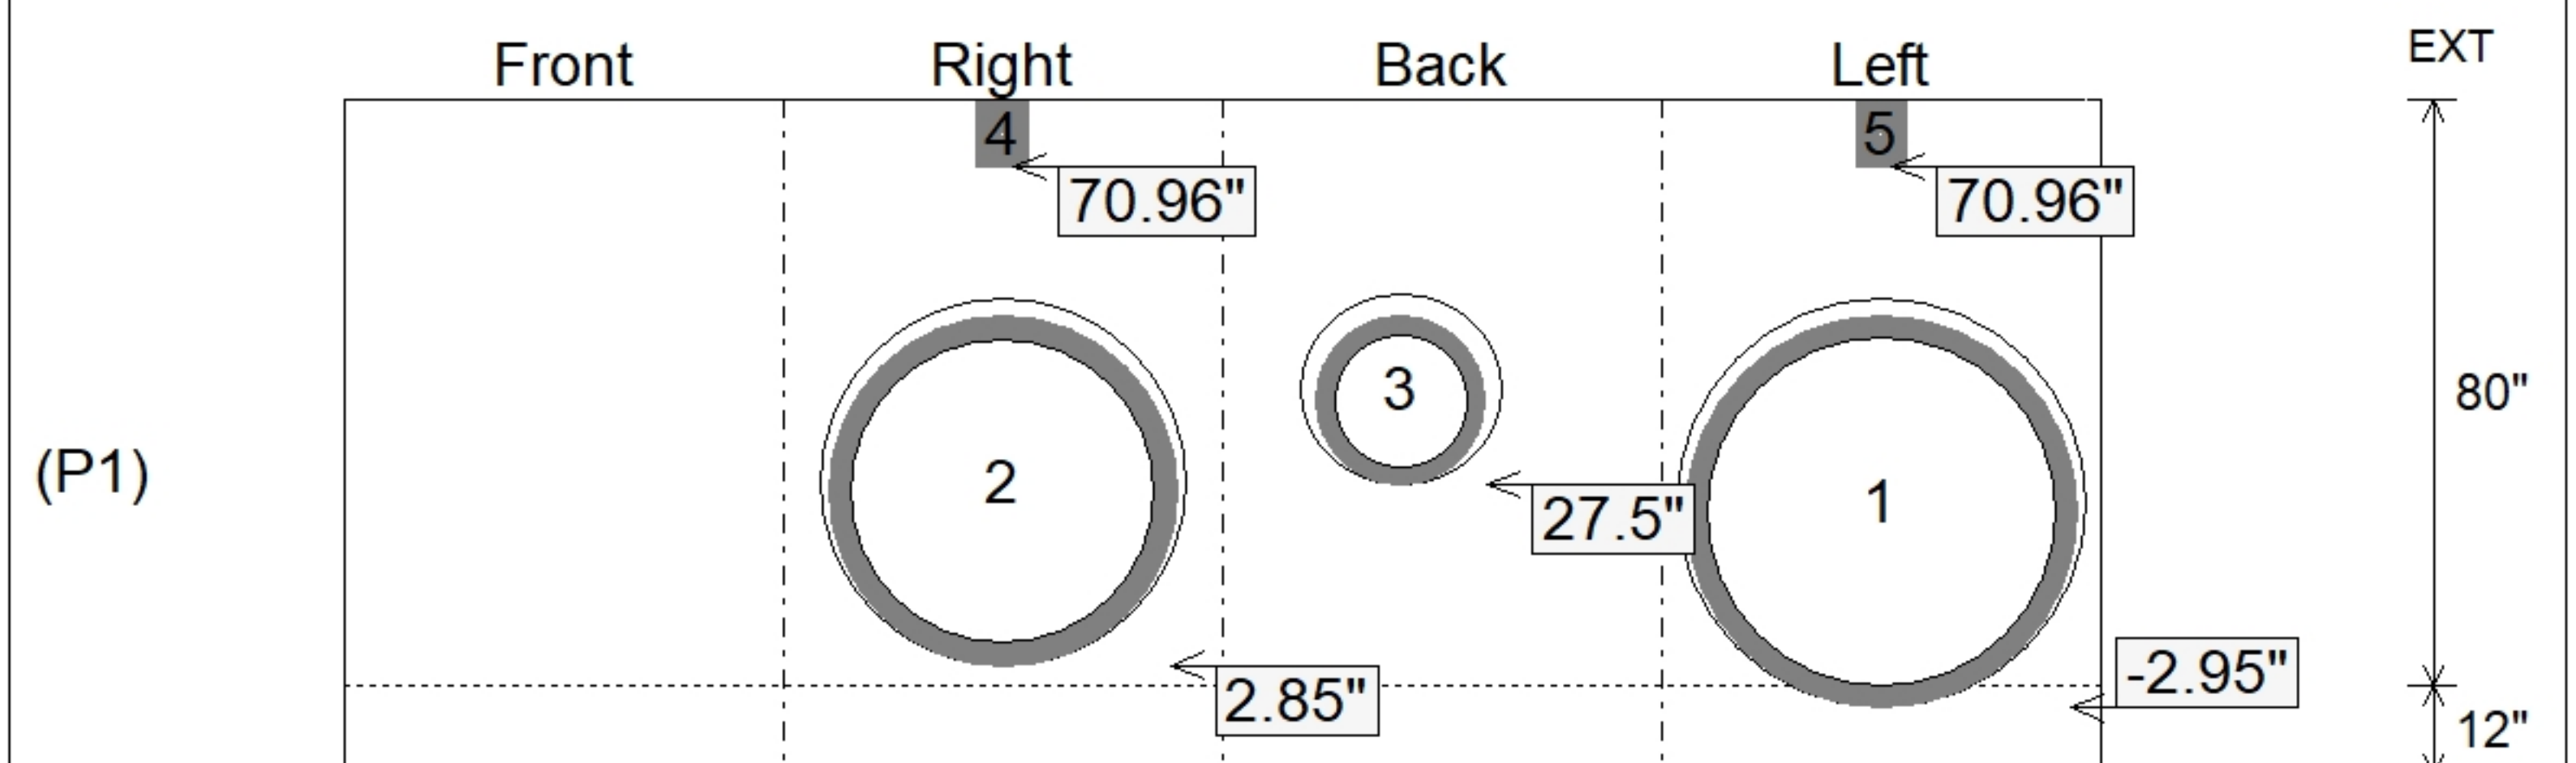

SUBMITTAL
APPROVED BY:
