

Job Name: 25-1172 - Midland Farms
Job Location: Somerset, KY 45203
Contractor: Weddle Enterprises, Inc

PC: C. Goff
 TECH: J. Horsley - F
 Plant: 100



Structure ID: **ARV 2**
 Spec: Sanitary
 Type: Air Release MH
 Size: 48"

Rim: 4'
 Invert: 0'
 Rim to Invert: 4'

Sump: 0"
 Floor (Top): 0'
 Floor Height: 0"


Floor (Bot): 0'
 Overall Height: 4'
 Slack: 0"

- Structure Notes:**
- PER ASTM C-478 SPECIFICATIONS
 - CONCRETE: 4,000 PSI AT 28 DAYS
 - REINFORCEMENT:
 - FLAT LID: #4 BAR @ 10" C.C. E.W. (GRADE 60)
 - DOGHOUSE RISER: PER ASTM A615
 - NO STEPS
 - CASTING SUPPLIED BY OTHERS (7" FRAME & SOLID COVER)



STRUCTURE SUMMARY:

P3) 24" - CASTING HEIGHT - 7"	0 lb
P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12"	1561 lb
P1) 48" - MH DH RISER Custom Ht T/F - 29"	2026 lb
1) JOINT WRAP - 0.065"x6"x50" CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) Hole - 0	0 lb

Structure Total:	3587 lb



Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	4'							
Reducer								
Invert 1			NO OPENINGS					
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

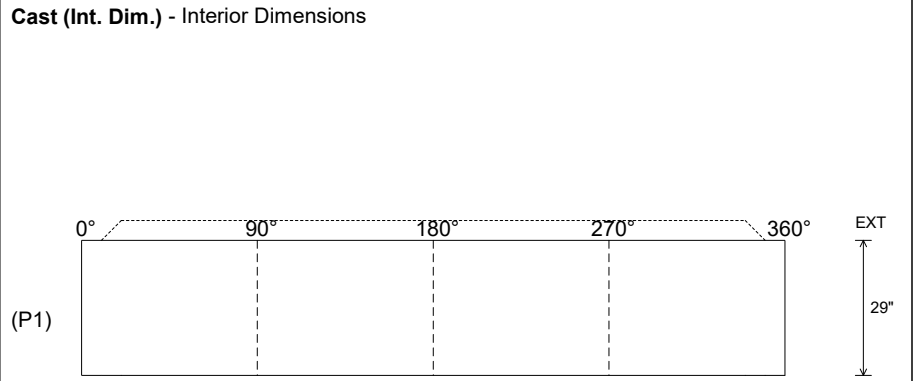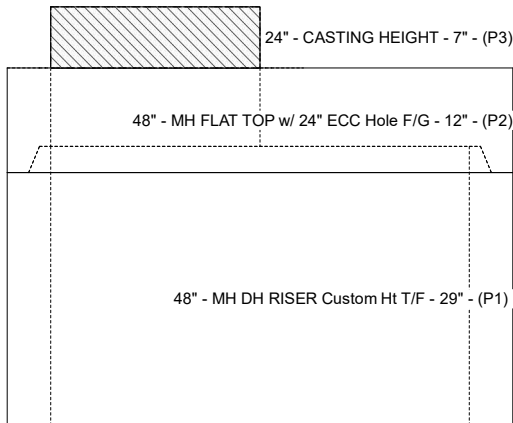

Submittal Drawing
 12/16/2025 1:23:44 PM

SUBMITTAL
 APPROVED BY:
