

Job Name: 25-1401 Irwin Landing Ph. 1
Job Location: Murfreesboro, TN
Contractor: Bear Construction LLC

PC: Erica Bradley
TECH: S. Felletter
Plant: Beaver Dam



Structure ID: R16

Spec: Storm

Type: STM.MH

Size: 48"

Rim: 579.25'

Invert: 570.37'

Rim to Invert: 8.88'

Sump: 2.5"

Floor (Top): 570.162'

Floor Height: 6"

Floor (Bot): 569.662'

Overall Height: 9.417'

Slack: 2.06"

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (JBS-3104 SINGLE SET).

REINFORCING PER ASTM A615 (GRADE 60).


- TOP SLAB (As .62) #5 BARS AT 8" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:

- P4) 28" x 28" - CASTING HEIGHT - 5"
P3) 48" - MH FLAT TOP w/28"x28" Hole F/G - 12"
P2) 48" - MH RISER T/G - 48"
P1) 48" - MH BASE T/n - 42"
1) 48" - STORM INVERT CHANNEL - 1/4 HEIGHT
1) CASTING - JBS 3104-V SINGLE SET
2) 48" - Con Seal CS-102 1.00"
1) 28" x 28" - Con Seal CS-102 1.00"
3) Hole - 28"
7) MH Step ML-10-TDS-NCR - 10"


0 lb
1368 lb
3120 lb
3798 lb
1075 lb
250 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 9611 lb

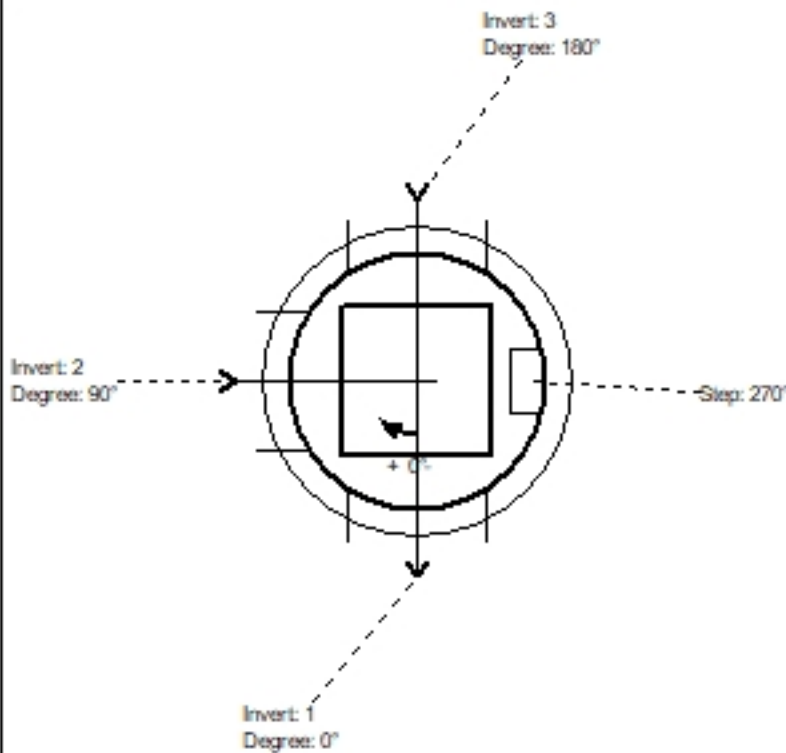

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	579.25'							
Reducer								
Invert 1	570.37'	0°	18" RCP B WALL	23"	28"	Hole 28	0"	P1
Invert 2	575.22'	90°	18" RCP B WALL	23"	28"	Hole 28	11.95"	P2
Invert 3	570.37'	180°	18" RCP B WALL	23"	28"	Hole 28	0"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

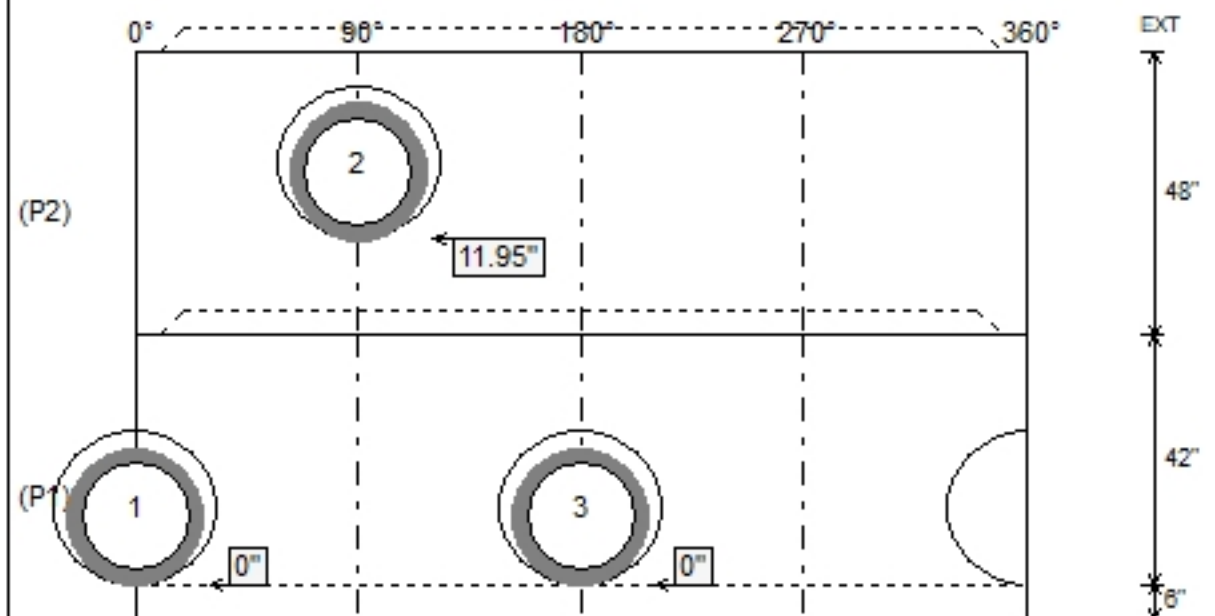

Submittal Drawing
6/10/2026 3:15:29 PM

SUBMITTAL
APPROVED BY:
