

Job Name: 25-1684P13 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.

7/21/2026 12:37:18 PM

Tech: N. Richards

PC: J. Jarvis



Structure ID: 78+91 JB-A

P2 BX3636_08LD08

CB FLAT TOP 8"W SOLID

P2) 36" x 36" - CB FLAT TOP 8"W SOLID - 8"

P1) 36" x 36" - BOX BASE 8inW, 8inF - 36"

1) 36" x 36" - Conseal CS-102 1.00"

1) Hole - 34

1) Hole - 28

1815 lb

5046 lb

0 lb

0 lb

0 lb

Structure Total: 6861 lb

Structure Notes:

-KYTC STATE PROJECT 251007


-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)

-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).

-KYTC CERTIFICATIONS REQUIRED.

3 EA. CONAC .8 TON $8\frac{1}{16}$ "
(6MM) WIRE ROPE ANCHORS
REQUIRED—MINIMUM.


KYTC STATE PROJECT

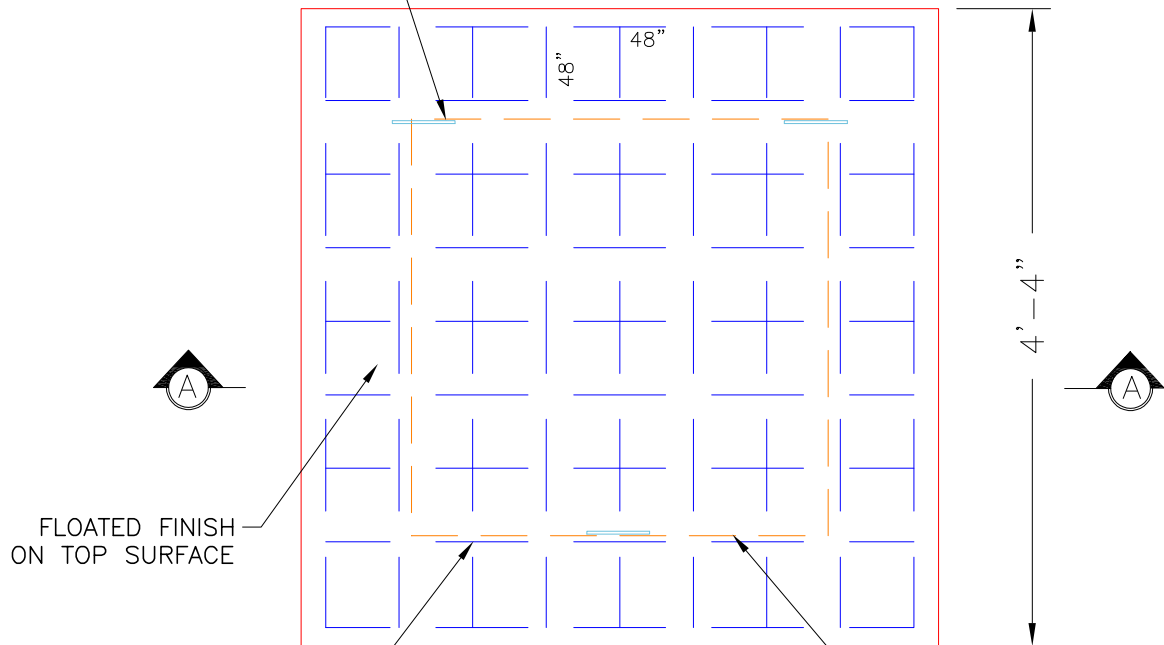

#4 BAR @ 6"
C/C E.W. (TYP.)

PLAN VIEW

$\frac{3}{4}$ " DEEP X 9" WIDE
RECESS REQUIRED

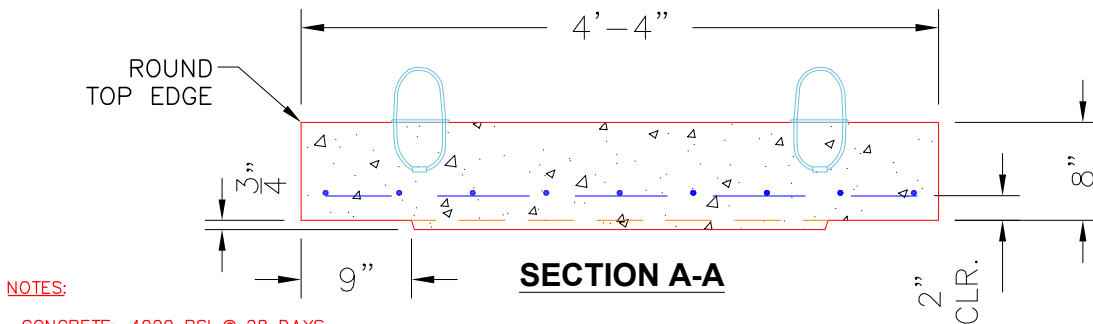

NOTES:

- CONCRETE: 4000 PSI @ 28 DAYS.
- MANUFACTURE TO KYTC SPECIFICATIONS.
- REINFORCING: #5 BAR @ 6" C/C E.W.—GRADE 60.
(BOTTOM LAYER ONLY)
- 3 EA. CONAC WIRE LOOP LIFTERS REQUIRED.

#4 BAR CUT LIST

18 EA. @ 48"

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1815 lb
Volume (Net): 0.46cu.yd
