

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/4/2026 11:28:57 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 15+86 MOD MH TYPE C

P2 BX084132-10TS48

CB FT REDUCER 48" HOLE

- P5) 24" - CASTING HEIGHT - 4"
P4) 24" - GRADE RING - 3"
P3) 48" - ECC CONE w/ 24" HOLE - 42"
P2) 84" x 132" - CB FT REDUCER 48" HOLE - 10"
P1) 84" x 132" - BX BASE w/FLANGE 08W/12F/08EF - 84"
1) 48" - SGL 1"x14.5' Butyl
1) Hole - 52
2) Hole - 40
1) SQ. Hole - 68"x68"
4) Vert. Notch - 7"x9"x5"

Structure Total:


0 lb
202 lb
3200 lb
10901 lb
36186 lb
0 lb
0 lb
0 lb
0 lb
0 lb

50489 lb

Structure Notes:

- KYTC STATE PROJECT 251007
- KYTC CERTIFICATIONS REQUIRED.
- 1. PER KYTC MANHOLE TYPE C / ASTM C913 SPEC'S.
- 2. CONCRETE = 4,000 PSI AT 28 DAYS.
- 3. NO INVERT CHANNEL
- 4. CASTING PROVIDED BY OTHERS.
- 5. REINFORCING PER ASTM A615 (GRADE 60).
 - TRANS. SLAB #5's AT 6" C.C.E.W (DBL MAT).
 - WALLS #5's AT 6" C.C.E.W.
 - FLOOR #5's AT 12" C.C.E.W..
- 6. PRODUCTION TO PLACE 4X POCKETS FOR I-BEAMS (I-BEAM PROVIDED BY OTHERS)

KYTC STATE PROJECT

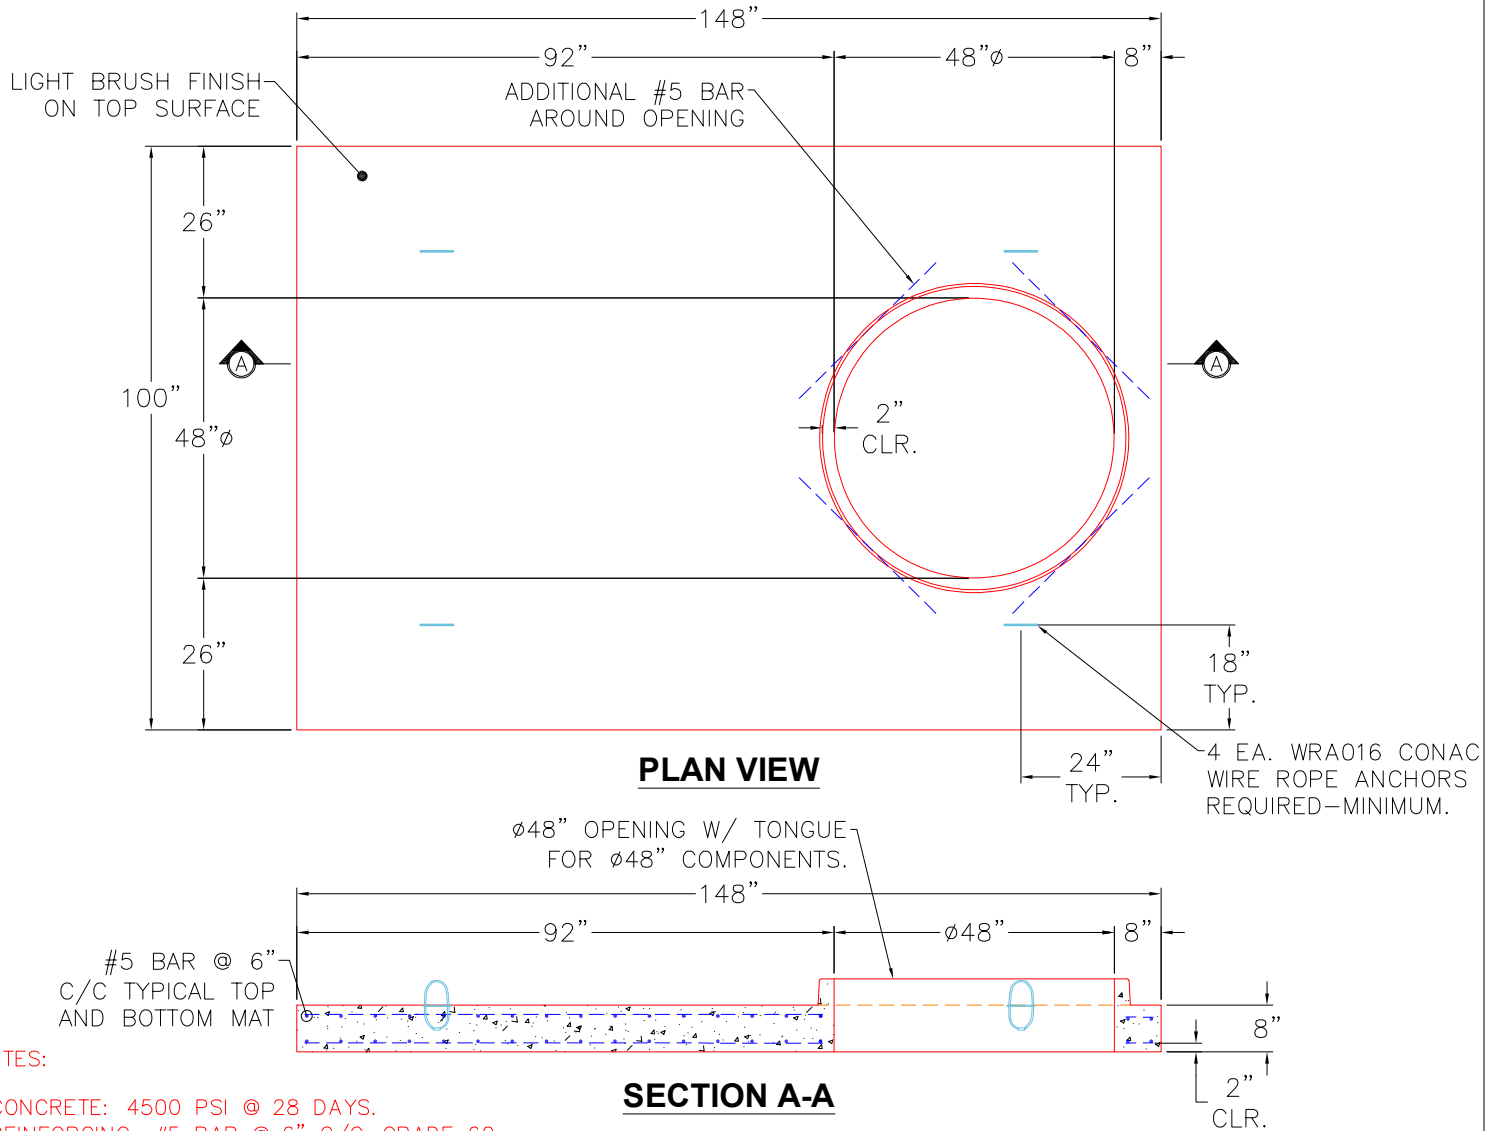

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- REINFORCING: #5 BAR @ 6" C/C-GRADE 60.
(TOP & BOTTOM LAYERS).
- KYTC CERTIFICATIONS REQUIRED.
- 4 EA. CONAC WIRE LOOP LIFTERS REQUIRED.

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 10"

Weight (Net): 10901 lb
Volume (Net): 2.78cu.yd
