

Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, KY
8/6/2026 12:00:43 PM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 22+18 CBBI-MOD B1




P2 CMBBIT9-B1LH

CB MED BAR BOX INLET 9B1 LH

- P3) 24" x 120" - CASTING (cast in) - 3"
P2) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 29"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 22



0 lb Structure Notes:
4000 lb -KYTC STATE PROJECT 251007
4100 lb -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
0 lb -CASTING FRAMES & GRATES BY OTHERS.
0 lb -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
Structure Total: 8100 lb -KYTC CERTIFICATIONS REQUIRED.

REINFORCING CUT LIST				
BAR	QTY.	MATERIAL	LENGTH	TOTAL WEIGHT
Ⓐ	3	#5 BAR	34"	9 LBS.
Ⓑ	2	#5 BAR	48"	8 LBS.
Ⓒ	3	#5 BAR	132"	34 LBS.
Ⓓ	7	#5 "L" BAR	30"	44 LBS.
Ⓔ	8	#5 "U" BAR	42"	30 LBS.
Ⓕ	5	#5 BAR	100"	44 LBS.
Ⓖ	8	#5 BAR	12"	8 LBS.

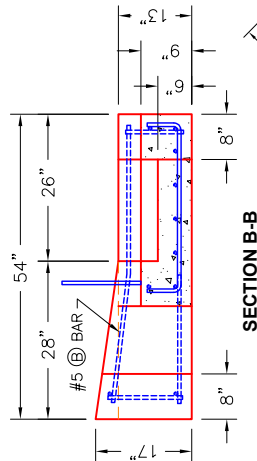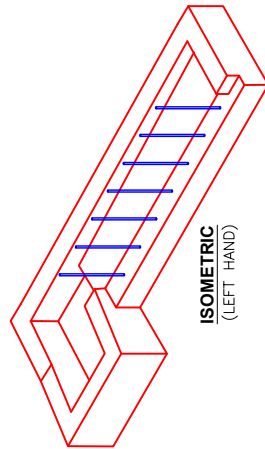

KYTC STATE PRODUCT

THIS DRAWING IS INTENDED TO BE PRINTED IN COLOR.
LATEST REVISION 9-15-25

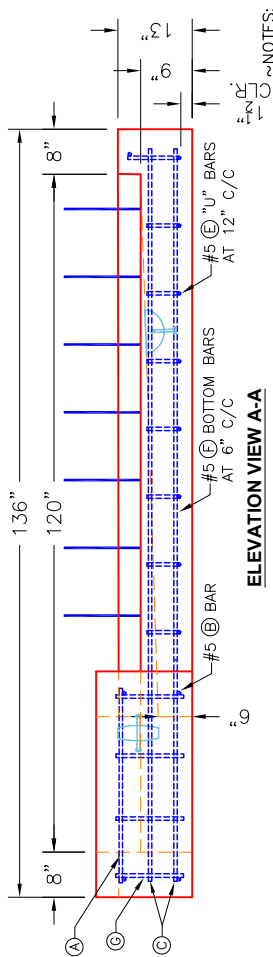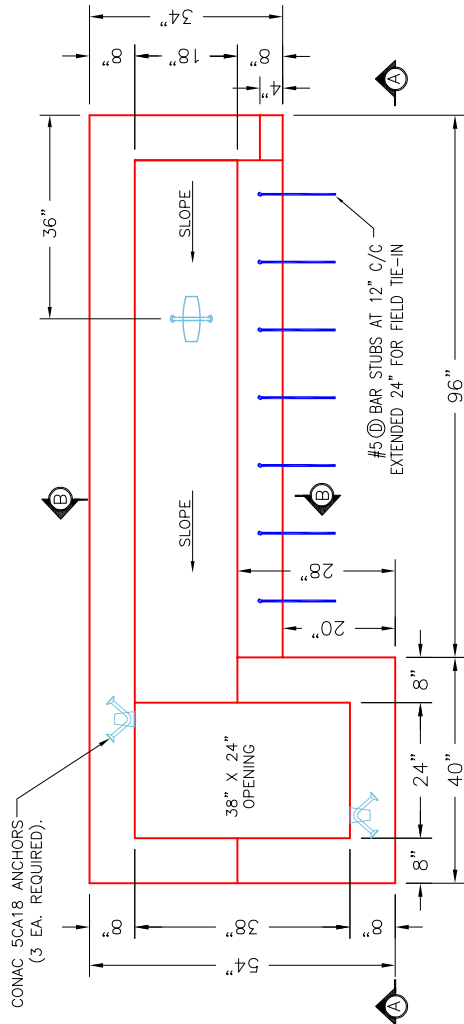

1. CONCRETE: 4,500 PSI KYTC APPROVED.
2. REINFORCING: #5 BAR @ 12\"/>

PRODUCTION WORK ORDER		DESCRIPTION: KYTC MBI B1 TYPE 9 10' TOP PHASE (LEFT HAND)	
QUALITY CONTROL CHECKLIST		CUSTOMER: CLEARY CONSTRUCTION INC.	
☐ ALL DIMENSIONS CORRECT.		PROJECT: JEFFERSON CO. (251007)	
☐ LIFTERS INSTALLED.		STRUCTURE ID.: 22+18 MBI B1 (SEC. P3)	
☐ CASTING AT CORRECT LOCATION.		SALES ORDER NO.: 25-1684	
☐ REINFORCING CORRECT.		DRAWING: N. RICHARDS	
☐ LIGHT BRUSH FINISH ACCEPTABLE.		DATE: 11/19/25	
☐ KYTC STANDARD THROAT CORRECT.		SCALE: NTS	
☐ ALL PATCHWORK ACCEPTABLE.		PG. 1 of 1	



THIS DRAWING IS THE PROPERTY OF INFRASTRUCTURE PRECAST, INC. ANY USE OR DUPLICATION OF THIS DRAWING WITHOUT PRIOR AUTHORIZATION IS STRICTLY PROHIBITED.

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 17"	Weight (Net): 4000 lb Volume (Net): 0cu.yd
----------------------------------	--------------------------------	--------------------	-------------------	---
