


Job Name: 25-1684P14 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					Plant: Beaver Dam, KY 8/4/2026 11:26:56 AM		Tech: J. Coppage PC: T. Ryan				
Structure ID: 4010+98 LT CBBI-MOD B1											
P1		BX3636-08BAVF		BOX BASE 8inW, 8inF, Variable Ht							
P3) 24" x 120" - CB MED BAR BOX INLET 9B1 RH - 17" P2) 36" x 36" - CB FT REDUCER 24"X36" HOLE-FT - 8" P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 38" 1) 36" x 36" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 28 2) Hole - 22						4000 lb 1235 lb 5381 lb 0 lb 0 lb 0 lb ----- Structure Total: 10616 lb		Structure Notes: -KYTC STATE PROJECT 251007 -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.) -CASTING FRAMES & GRATES BY OTHERS. -CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST). -KYTC CERTIFICATIONS REQUIRED.			
Rim: 582.92'		Rim to Invert: 5.65'		Slack: 4.8"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	577.27'	0°	26"	24" CMP	25"	Hole 28	28"	28"	-2"	0"	
Invert 2	577.27'	180°	26"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 3	577.27'	270°	26"	18" CMP	19"	Hole 22	22"	22"	-2"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

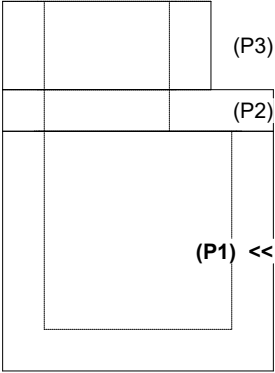


(P3)

(P2)

(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

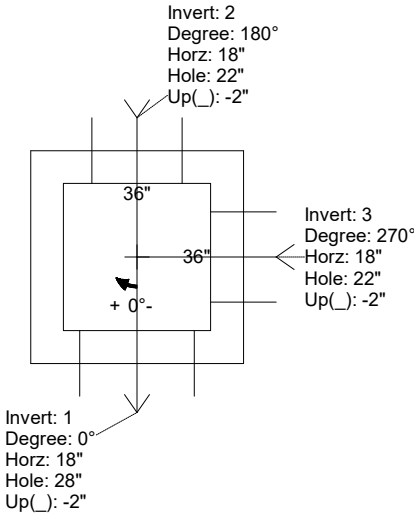


Invert: 2
Degree: 180°
Horz: 18"
Hole: 22"
Up(): -2"

Invert: 3
Degree: 270°
Horz: 18"
Hole: 22"
Up(): -2"

Invert: 1
Degree: 0°
Horz: 18"
Hole: 28"
Up(): -2"

UPSIDE-DOWN VIEW (int. dimensions)

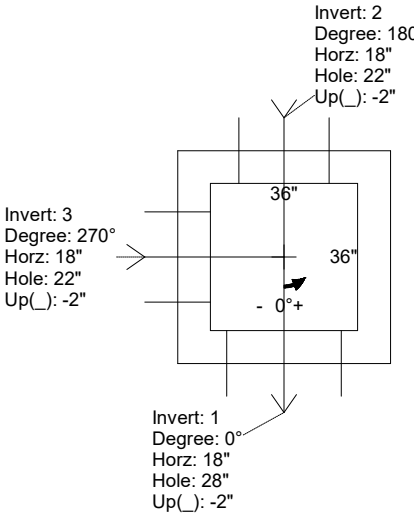


Invert: 2
Degree: 180°
Horz: 18"
Hole: 22"
Up(): -2"

Invert: 3
Degree: 270°
Horz: 18"
Hole: 22"
Up(): -2"

Invert: 1
Degree: 0°
Horz: 18"
Hole: 28"
Up(): -2"

INSIDE WALL DIMENSIONS

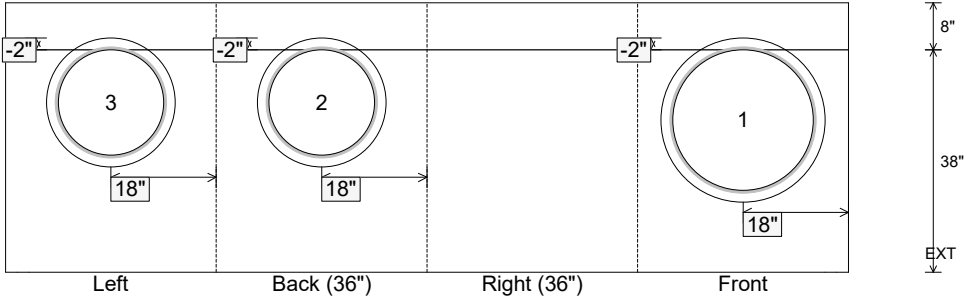

(P1)

Left Back (36") Right (36") Front

EXT

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 38" Height (Ext): 46"	Weight (Net): 5381 lb Volume (Net): 1.37cu.yd
----------------------------------	-------------------------------	--	--	--
