

**Structure ID: 4013+85 LT CBBI-MOD B1**

P2 CMBBIT9-B1RH






CB MED BAR BOX INLET 9B1 RH

- P3) 24" x 120" - CASTING (cast in) - 3"
P2) 24" x 120" - CB MED BAR BOX INLET 9B1 RH - 17"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 26"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 22
1) Hole - 18

0 lb Structure Notes: .
4000 lb -KYTC STATE PROJECT 251007
3368 lb -REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
0 lb -CASTING FRAMES & GRATES BY OTHERS.
0 lb -KS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
0 lb -CYT CERTIFICATIONS REQUIRED.

Structure Total: 7368 lb

REINFORCING CUT LIST					
BAR	QTY.	MATERIAL	LENGTH	SHAPE	TOTAL WEIGHT
(A)	3	#5 BAR	34"	STR.	9 LBS.
(B)	2	#5 BAR	48"	STR.	8 LBS.
(C)	3	#5 BAR	132"	STR.	34 LBS.
(D)	7	#5 1" BAR	30"	BENT	44 LBS.
(E)	8	#5 1/2" BAR	42"	BENT	30 LBS.
(F)	5	#5 BAR	100"	STR.	44 LBS.
(G)	8	#5 BAR	12"	STR.	8 LBS.

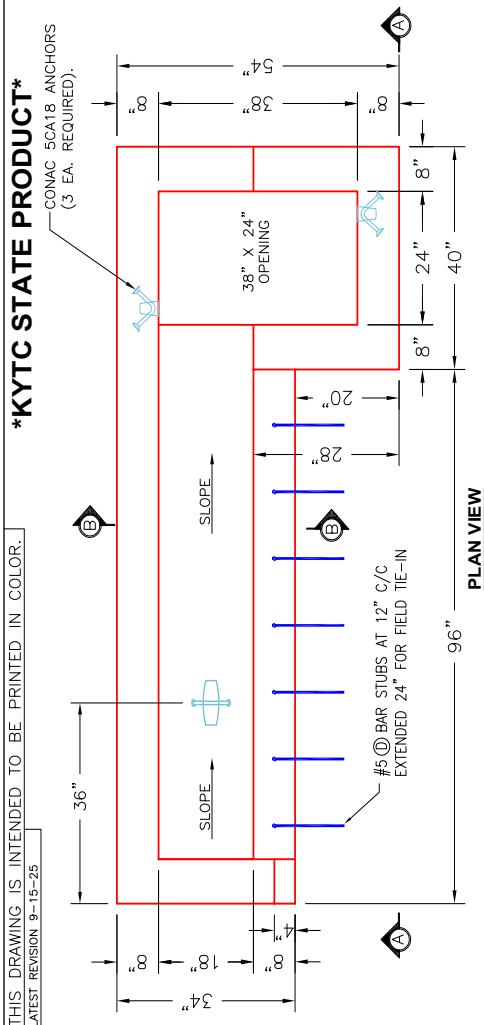

1. CONCRETE: 4,500 PSI MYTC APPROVED.
2. REINFORCING BARS: #4 (GRADE 60)
3. REINFORCING BARS TO BE TACK WELDED OR TIED.
4. LIFTING ANCHOR POCKETS TO BE GROUED OR TIED.
5. REINFORCING BARS TO BE GROUED OR TIED.
6. RDB-230 OR RDB-231-11, RDB-240-02 AND THE STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION.
7. REINFORCING BARS TO BE WELDED AS RIGHT HAND & LEFT HAND & SAG.
8. "P" DESIGNATES REBAR STUDS ON BOTH SIDES AND "S" DESIGNATES REBAR STUDS ON ONE SIDE AND "2" DESIGNATES REBAR STUDS ON BOTH SIDES AS SHOWN.

PRODUCTION WORK ORDER		PRODUCT I.D.: CMBBIT9-B1RH	DESCRIPTION: KYTC MBI B1 TYPE 9 10' TOP PHASE (RIGHT HAND)
	QUALITY CONTROL CHECKLIST	PRODUCT VIEW: RIGHT SIDE UP	CUSTOMER: CLEARY CONSTRUCTION INC.
	☐ ALL DIMENSIONS CORRECT.	PLANT: BEAVER DAM, KY.	PROJECT: JEFFERSON CO. (251007)
	☐ LIFTERS INSTALLED.	WEIGHT: 4,325 LBS.	STRUCTURE ID: 4013+85 LT MBI B1 (SEC. P2)
	☐ CASTING AT CORRECT LOCATION.	TOP SECTION JOINT: N/A	SALES ORDER NO.: 25-1684
	☐ REINFORCING CORRECT.	BOTTOM SECTION JOINT: SHIP-LAP GROOVE	PC: J. JARVIS DRAWING: N. RICHARDS
	☐ LIGHT BRUSH FINISH ACCEPTABLE.	QC CHECK INITIALS:	DATE: 11/19/25 SCALE: NTS PG. 1 of 1
	☐ KYTC STANDARD THROAT CORRECT.		
	☐ ALL PATCHWORK ACCEPTABLE.		

THIS DRAWING IS THE PROPERTY OF INFRASTRUCTURE PRECAST, INC. ANY USE OR DUPLICATION OF THIS DRAWING WITHOUT PRIOR AUTHORIZATION IS STRICTLY PROHIBITED.

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 17"

Weight (Net): 4000 lb
Volume (Net): 0cu.yd
