

Contractor: Cleary Construction, Inc.

PC:	T. Ryan
TECH:	J. Coppage
Plant: Beaver Dam, KY	




Slack: 4.4"


- KYTC STATE PROJECT 251007
- REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
- CASTING FRAMES & GRATES BY OTHERS.
- CS-102 BUTYL REQUIRED (SUPPLIED BY ICST).
- KYTC CERTIFICATIONS REQUIRED.

P4) 24" x 120" - CASTING (cast in) - 3"	0 lb
P3) 24" x 120" - CB MED BAR BOX INLET 9B1 LH - 17"	4000 lb
P2) 36" x 48" - CB FT REDUCER 24"X36" HOLE-FT - 8"	1654 lb
P1) 36" x 48" - BOX BASE 8inW, 8inF, Variable Ht - 51"	7327 lb
1) 36" x 48" - Conseal CS-102 1.00"	0 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
1) Hole - 40	0 lb
1) Hole - 48	0 lb


Structure Total: 12981 lb

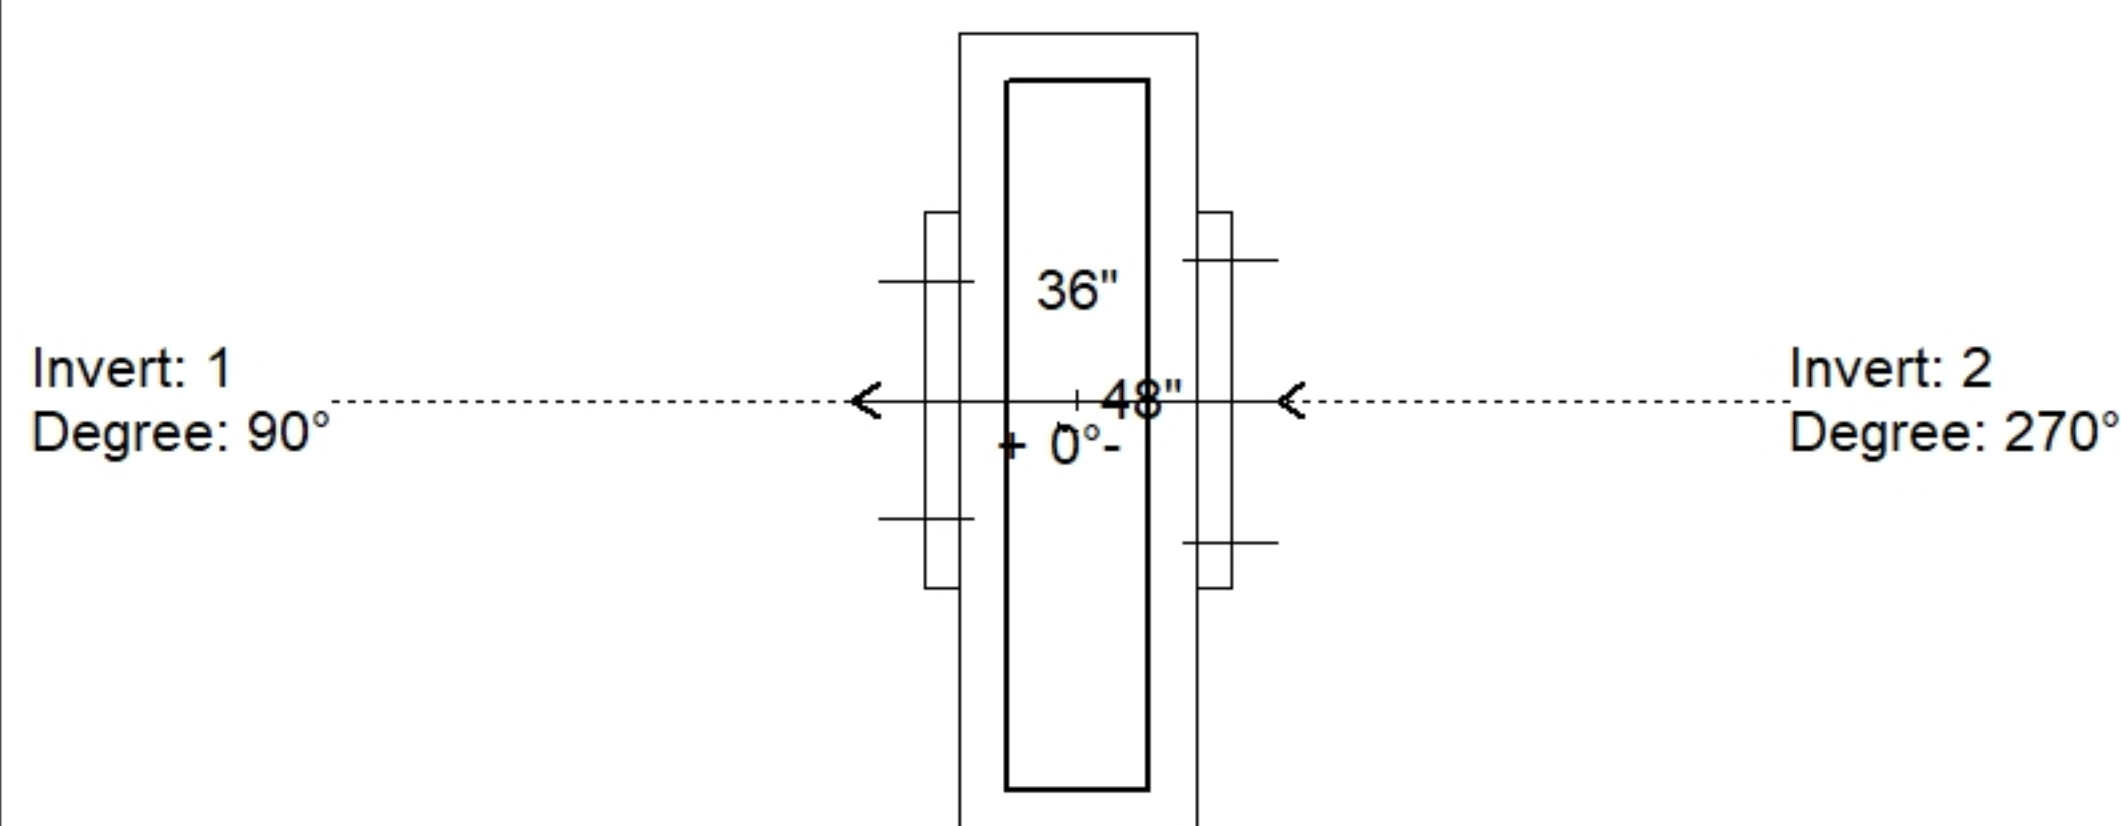

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	580.21'							
Reducer	577.76'							
Invert 1	573.51'	90°	36" CMP	37"	40"	Hole 40	-2"	P1
Invert 2	573.67'	270°	36" RCP B WALL	44"	48"	Hole 48	-4.08"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

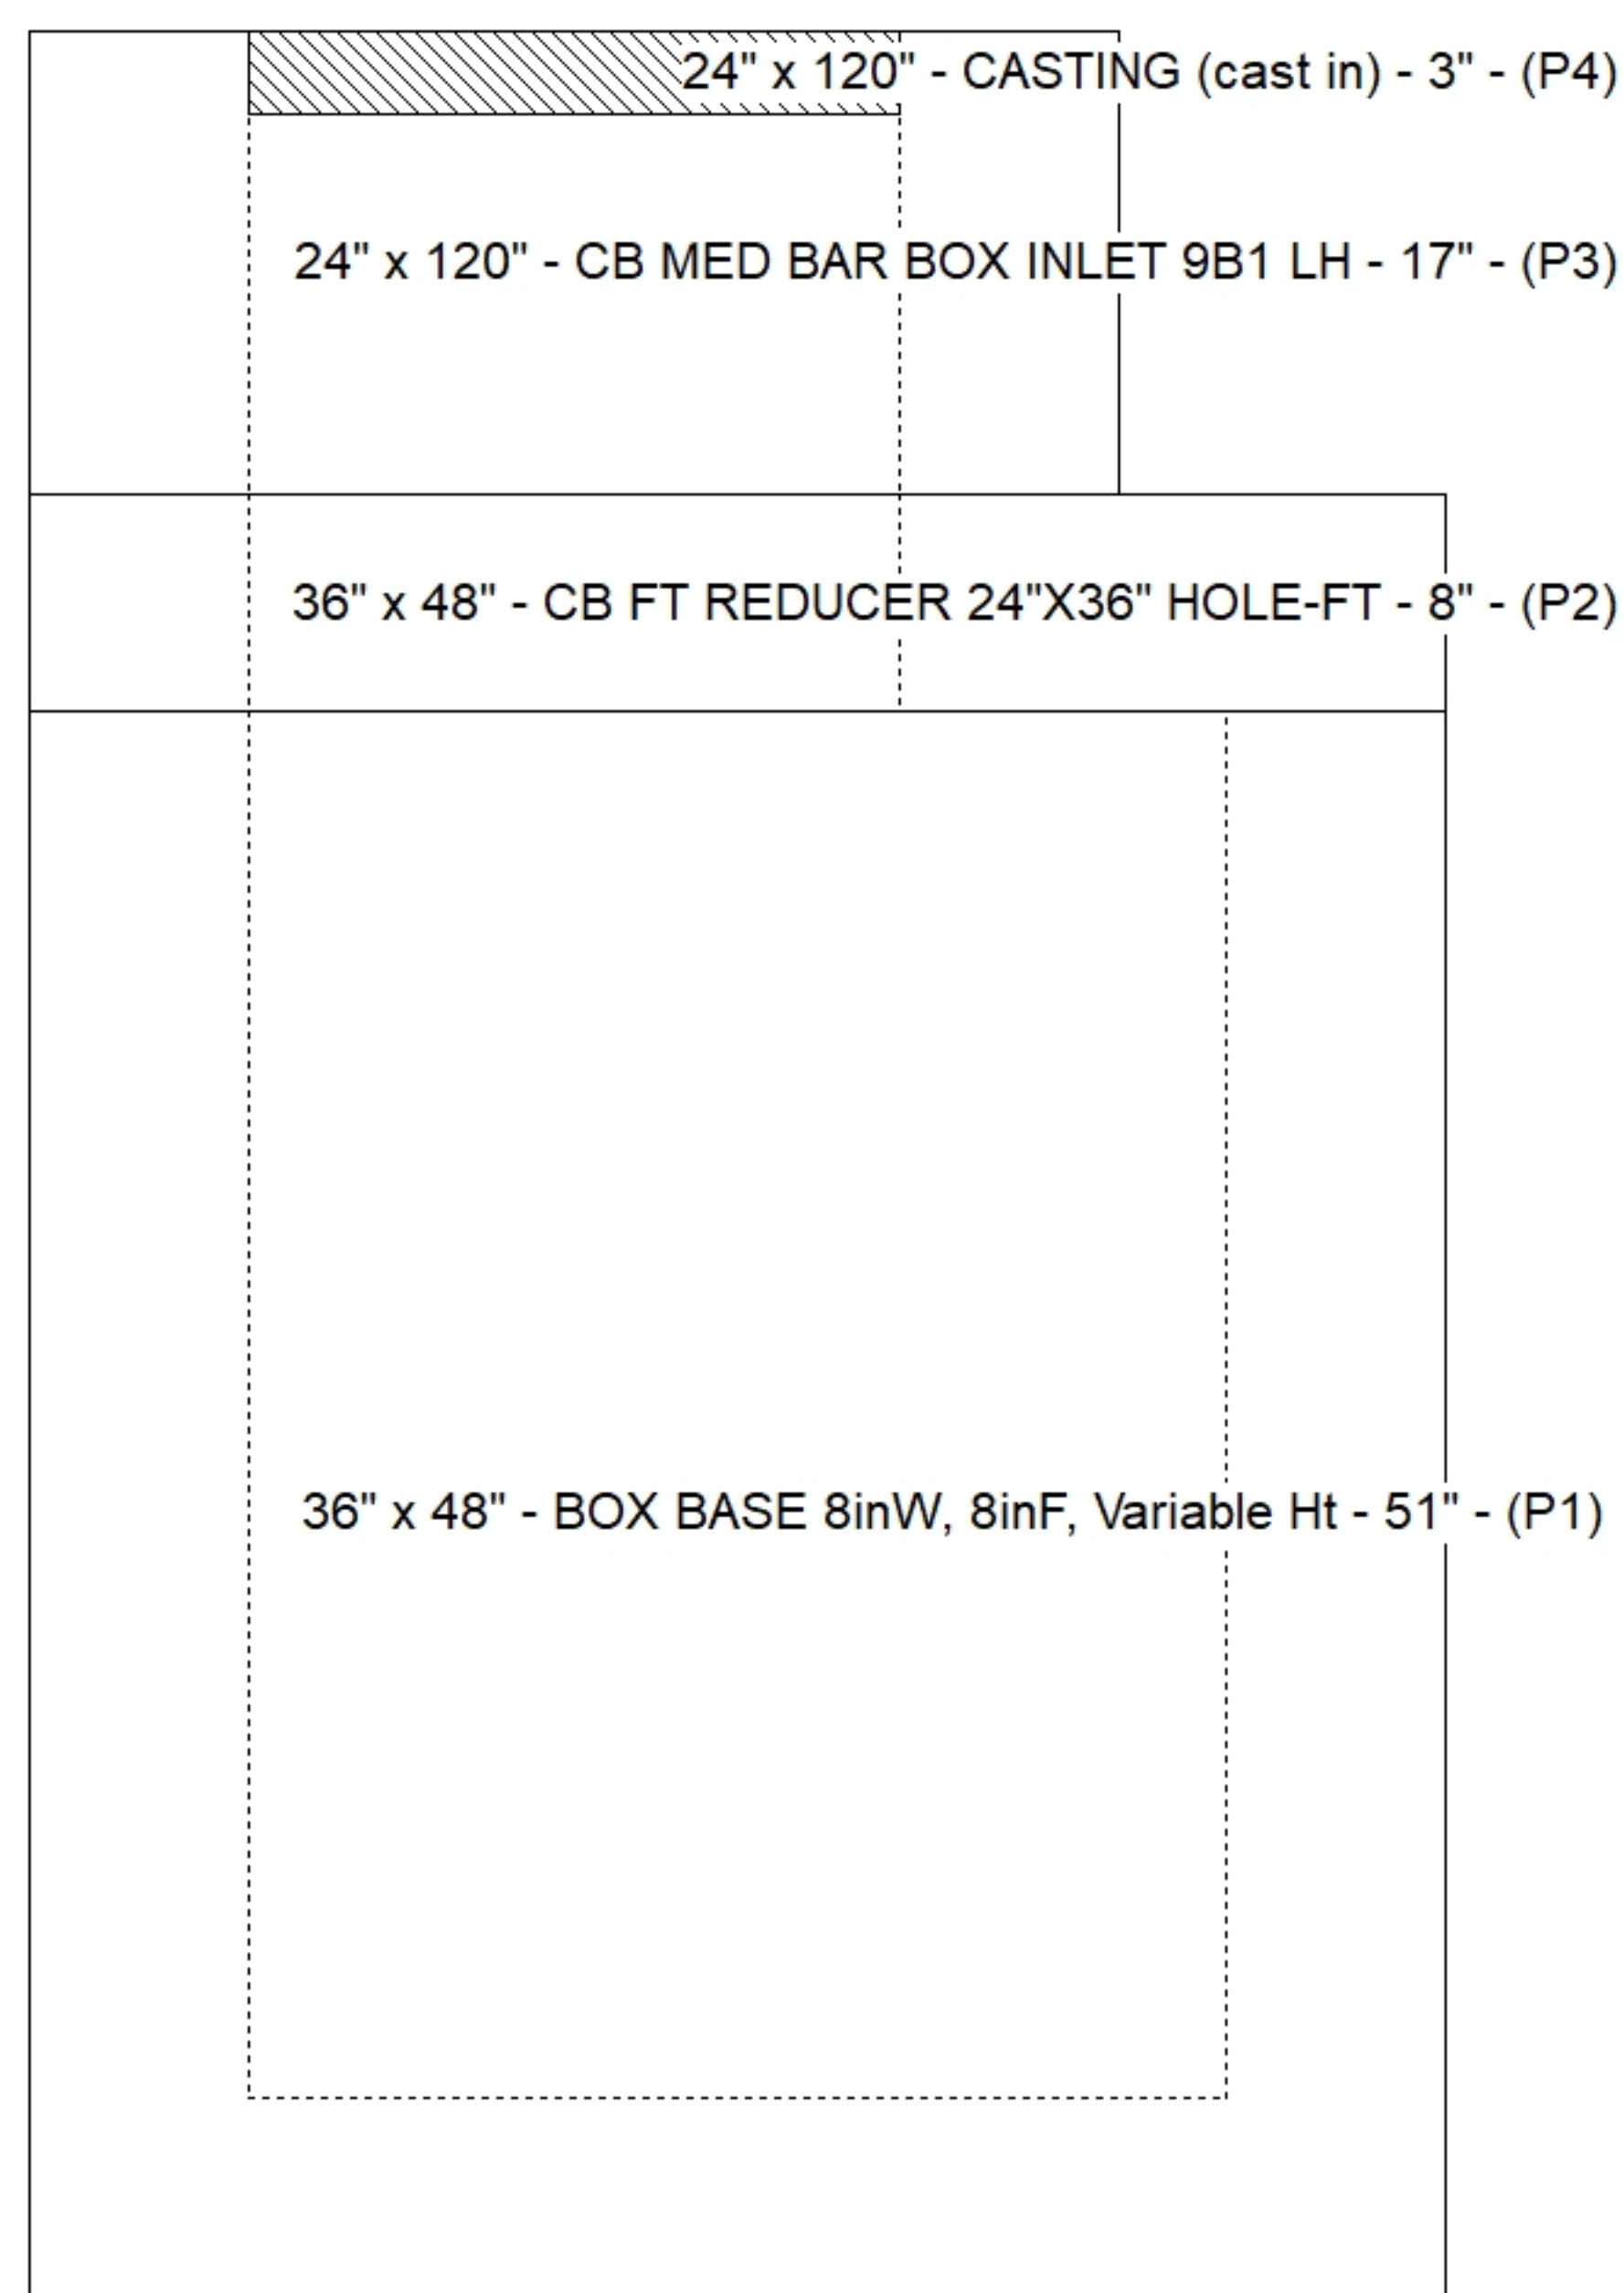

Default - Interior Dimensions

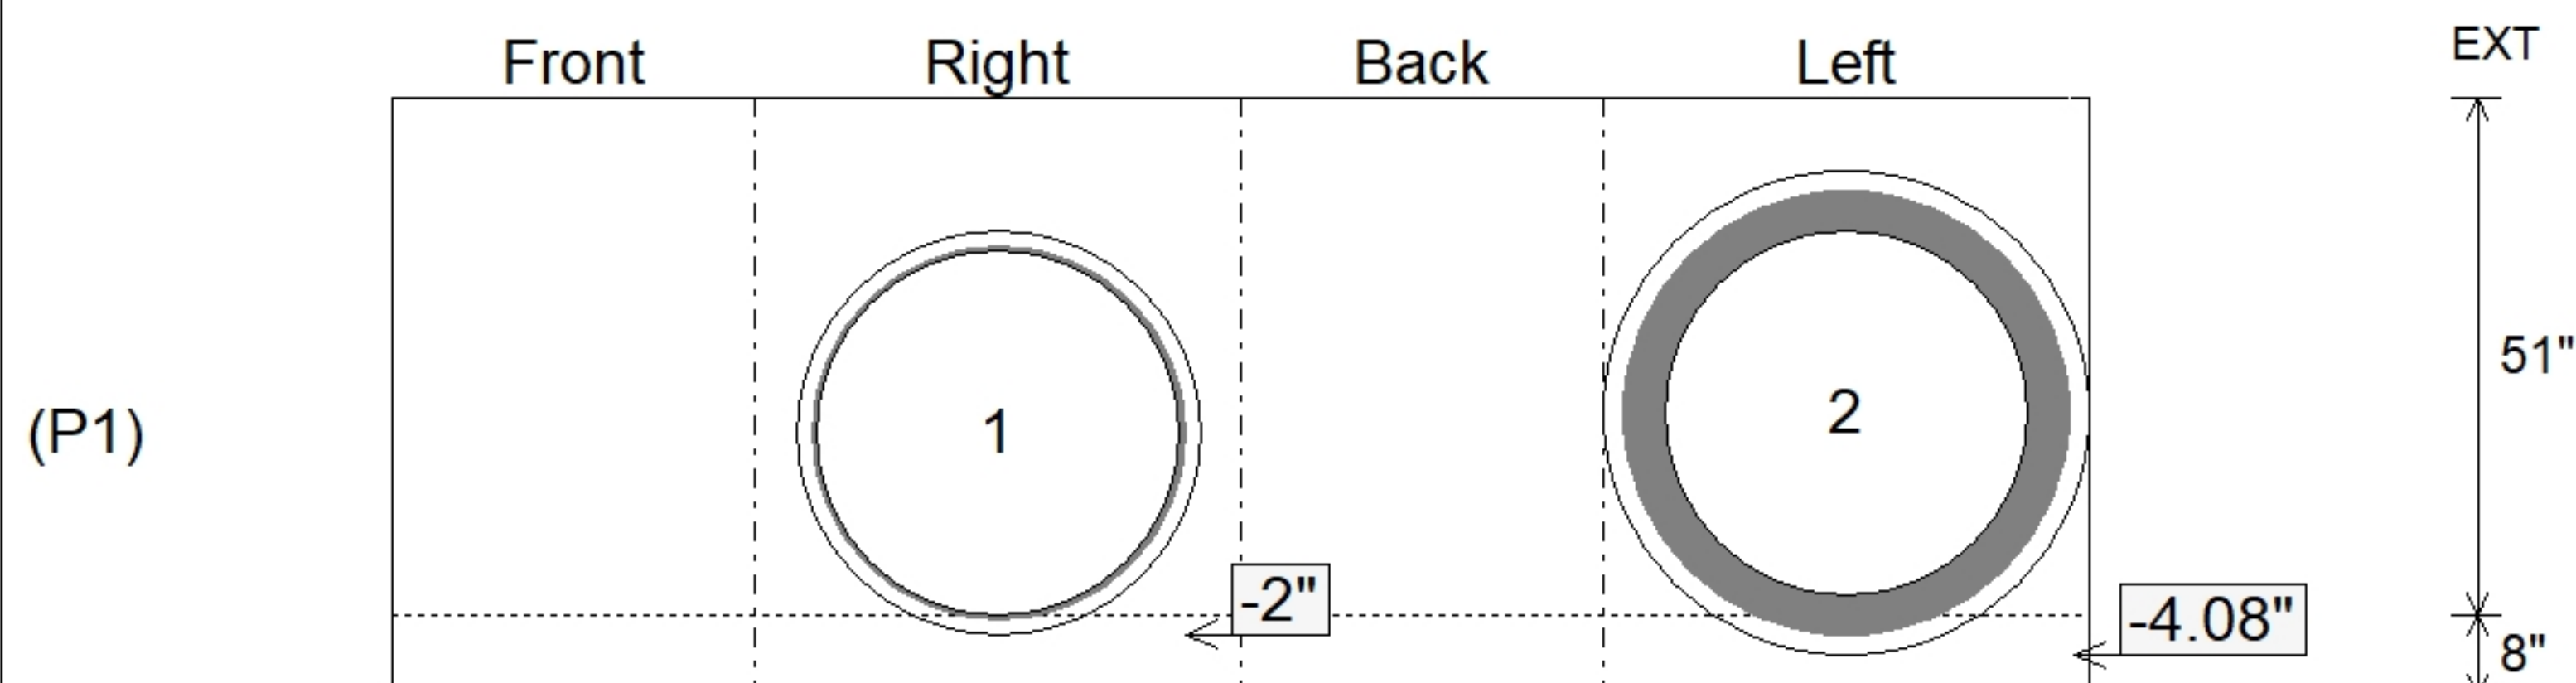

Submittal Drawing
8/10/2026 11:02:42 AM

SUBMITTAL
APPROVED BY:
