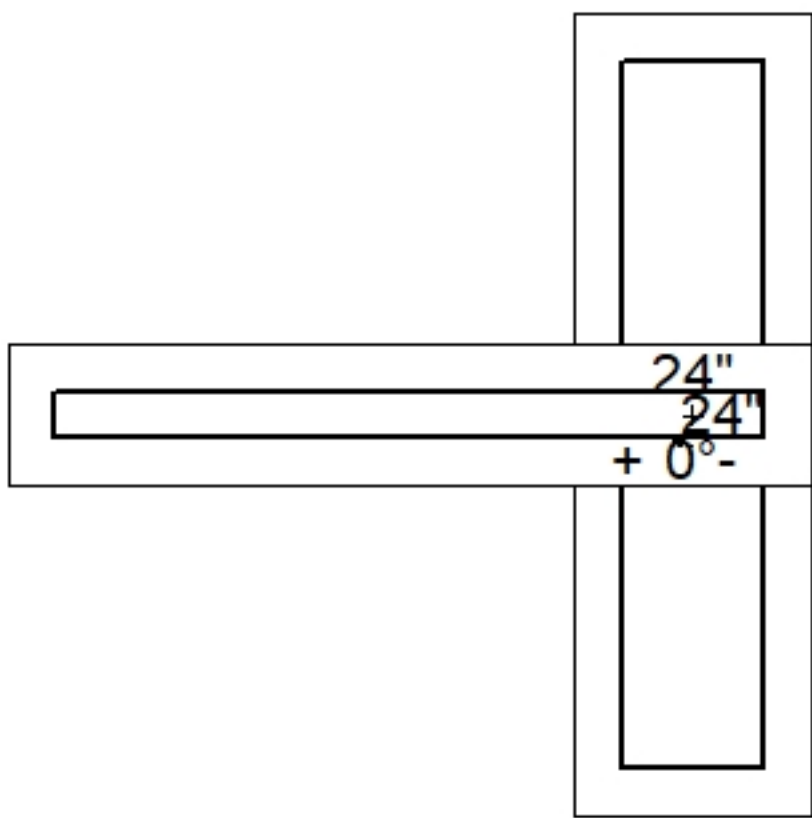
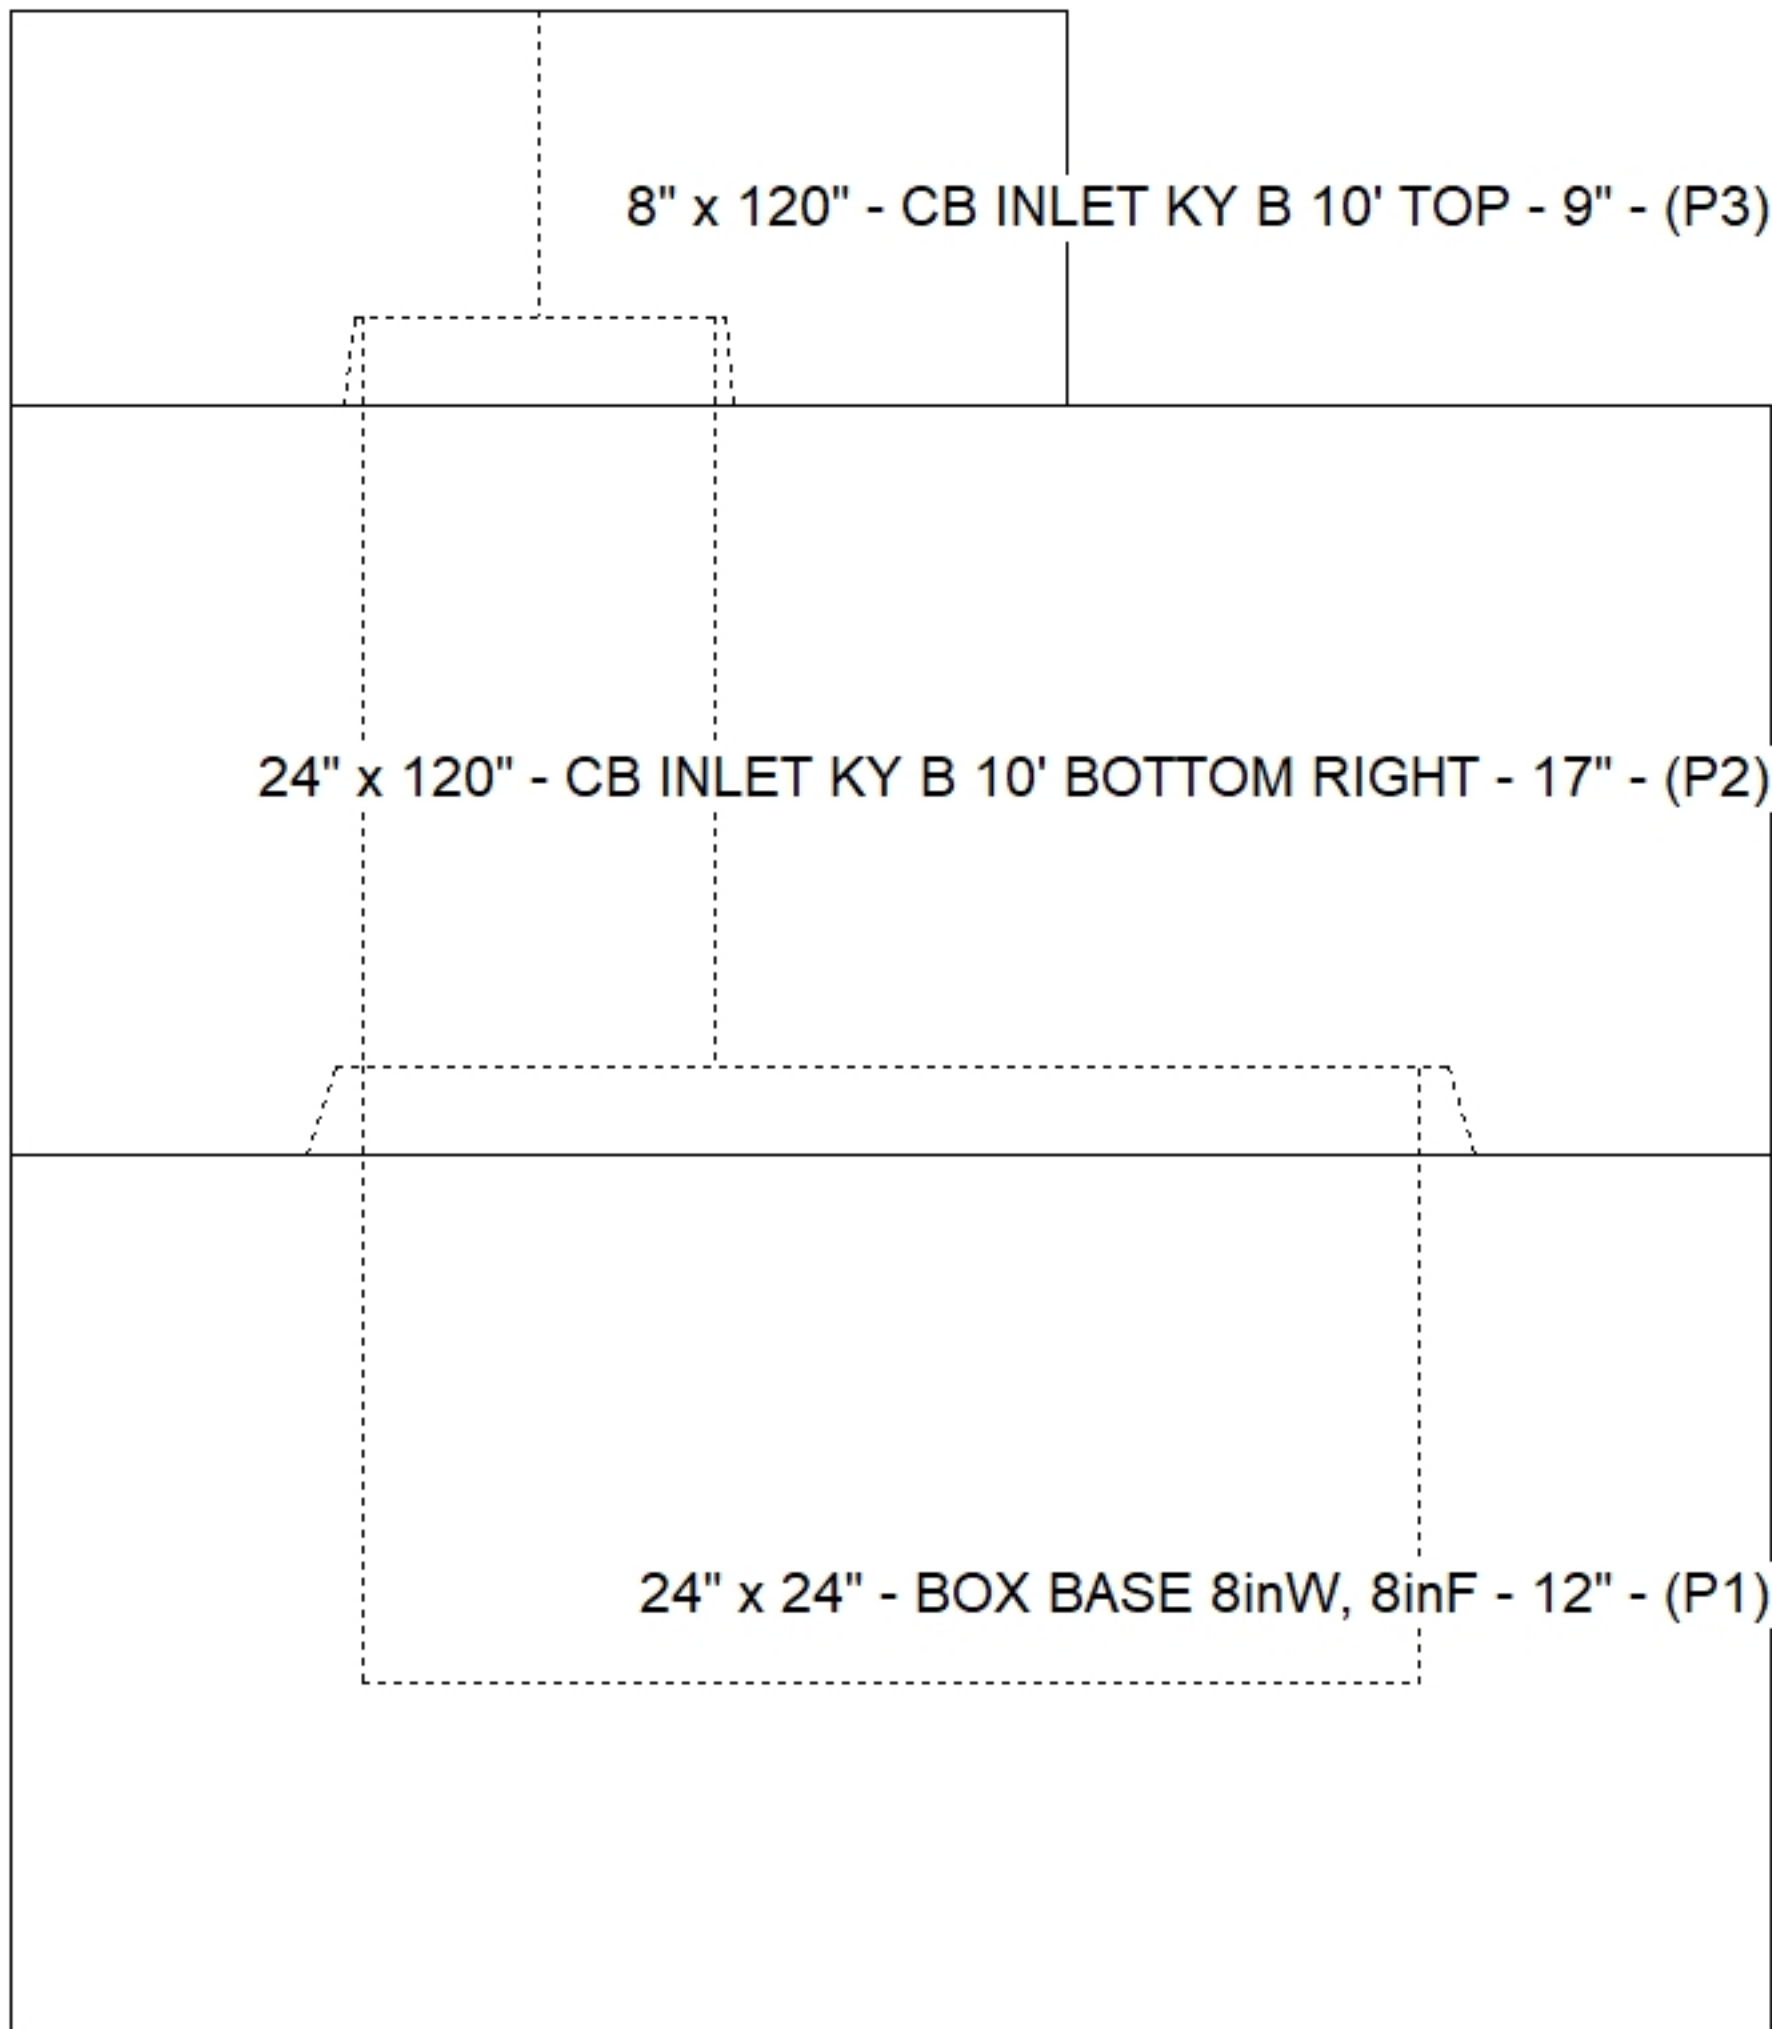
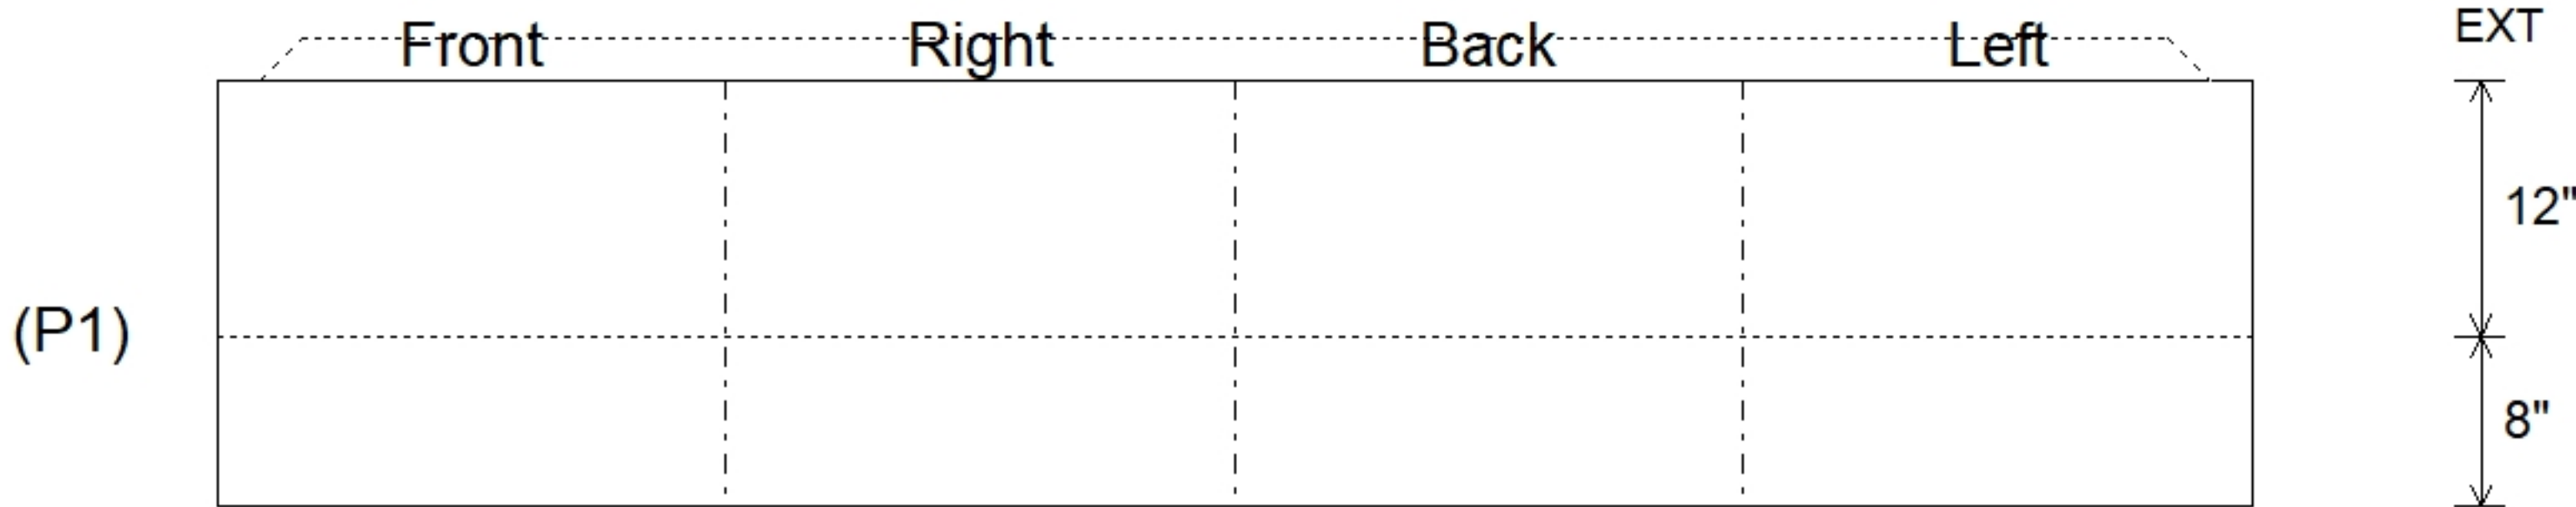


Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007) Job Location: I-264 Louisville, Ky. Contractor: Cleary Construction, Inc.					PC: T. Ryan TECH: J. Coppage Plant: Beaver Dam, Ky.																																																																																																						
Structure ID: 12+53 RT CBIB INLET 47 Spec: KYTC Type: CBI TYPE B (10') private Size: 24" x 24" Rim: 584.4' Invert: 584.4' Rim to Invert: 0' Sump: 38" Floor (Top): 581.233' Floor Height: 8" Floor (Bot): 580.567' Overall Height: 3.833' Slack: 0"																																																																																																											
Structure Notes: . ** KYTC STATE PROJECT ** 1. PER KYTC CBI TYPE B / ASTM C913 SPEC'S. 2. CONCRETE = 4,000 PI AT 28 DAYS. 3. NO INVERT CHANNEL. REINFORCING PER ASTM A615 (GRADE 60). - TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				STRUCTURE SUMMARY: P3) 8" x 120" - CB INLET KY B 10' TOP - 9"1660 lb P2) 24" x 120" - CB INLET KY B 10' BOTTOM RIGHT - 17"2650 lb P1) 24" x 24" - BOX BASE 8inW, 8inF - 12"2105 lb 1) 24" x 24" - Conseal CS-102 1.00"0 lb Structure Total: 6415 lb																																																																																																							
				<table><tr><th>Position</th><th>Elev</th><th>Angle</th><th>Pipe</th><th>Pipe OD</th><th>Hole</th><th>Connector</th><th>Up ()</th><th>Ref</th></tr><tr><td>Rim</td><td>584.4'</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Reducer</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 1</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 2</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 3</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 4</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 5</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 6</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 7</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr><tr><td>Invert 8</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></tr></table>					Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref	Rim	584.4'								Reducer									Invert 1									Invert 2									Invert 3									Invert 4									Invert 5									Invert 6									Invert 7									Invert 8								
Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref																																																																																																			
Rim	584.4'																																																																																																										
Reducer																																																																																																											
Invert 1																																																																																																											
Invert 2																																																																																																											
Invert 3																																																																																																											
Invert 4																																																																																																											
Invert 5																																																																																																											
Invert 6																																																																																																											
Invert 7																																																																																																											
Invert 8																																																																																																											
				Default - Interior Dimensions 																																																																																																							
Submittal Drawing 8/18/2026 9:55:11 AM					SUBMITTAL APPROVED BY:																																																																																																						
