

Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
8/17/2026 10:44:55 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 127+07 RT DBI-13G INLET 80

P2 BX024030-08LD08-15X27

CB FLAT TOP 8"W w/15"x27" HOLE


P3) 15" x 27" - P.I.P. - BY OTHERS - 3"
P2) 24" x 30" - CB FLAT TOP 8"W w/15"x27" HOLE - 8"
P1) 24" x 30" - BOX BASE 8inW, 8inF, Variable Ht - 20"
1) 24" x 30" - Conseal CS-102 1.00"
1) Hole - 18
2) Hole - 4

Structure Total:


0 lb
963 lb
2919 lb
0 lb
0 lb
0 lb
3882 lb

Structure Notes:

-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-DBI 13G FRAME & GRATE BY OTHERS.
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-#5 BAR STUBBED OUT OF TOP OF TRANSITION SLAB 6"
AT 12" C/C FOR FIELD POURED CURB & GUTTER.
-KYTC CERTIFICATIONS REQUIRED.

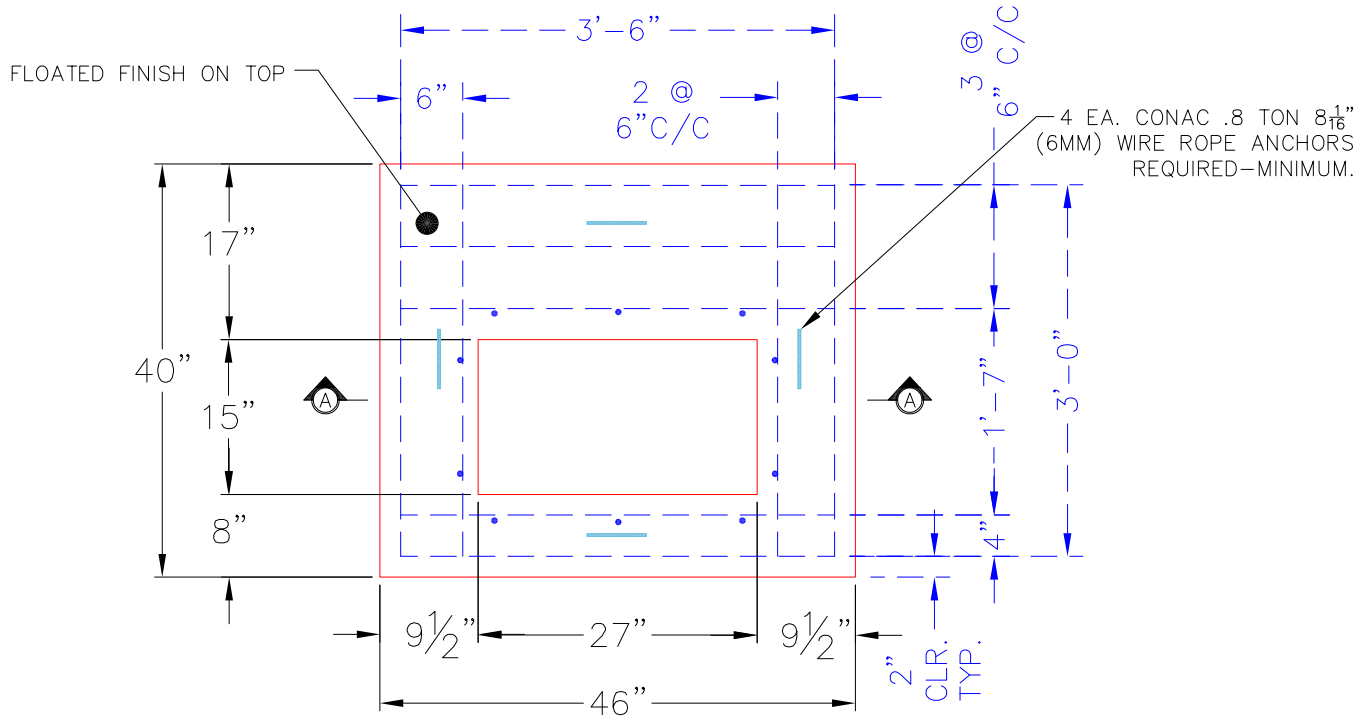

PLAN VIEW

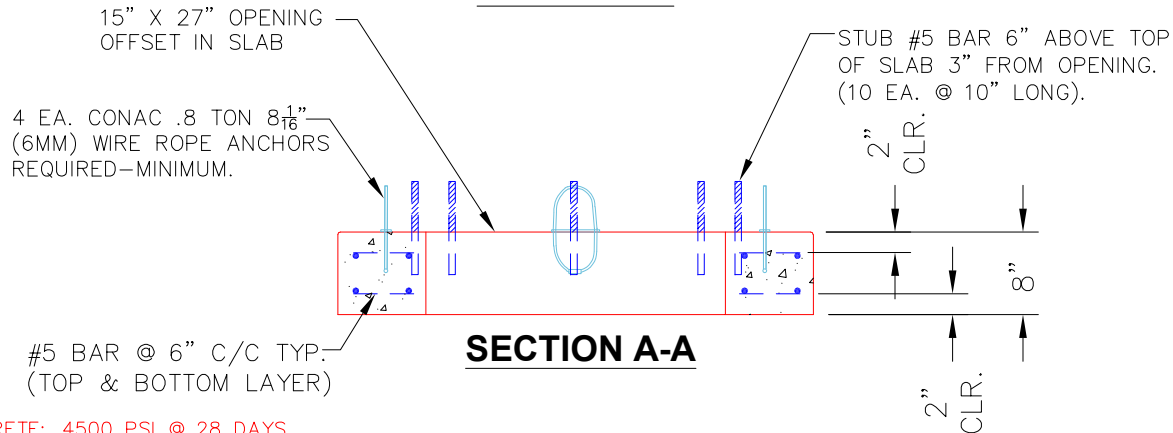

SECTION A-A

NOTES:

-CONCRETE: 4500 PSI @ 28 DAYS.
-MANUFACTURED TO KYTC & ASTM C-913 SPECIFICATIONS.
-REINFORCING: #5 BAR AS SHOWN-GRADE 60. (T&B LAYER)
-4 EA. CONAC WIRE LOOP LIFTS REQUIRED (MIN.)

#5 BAR CUT LIST
10 EA. @ 42" LG.
8 EA. @ 36" LG.

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 963 lb
Volume (Net): 0.25cu.yd
