

Job Name: 25-1684P15 KYTC Jefferson Co. Call 200 (251007)
Job Location: I-264 Louisville, Ky.
Contractor: Cleary Construction, Inc.

Plant: Beaver Dam, Ky.
8/17/2026 10:44:56 AM

Tech: J. Coppage
PC: T. Ryan



Structure ID: 130+84 RT JB-A INLET 74

P2 BX024024-08LD08

CB FLAT TOP 8"W SOLID


- P2) 24" x 24" - CB FLAT TOP 8"W SOLID - 8"
P1) 24" x 24" - BOX BASE 8inW, 8inF - 24"
1) 24" x 24" - Conseal CS-102 1.00"
2) Hole - 18

Structure Total:

1074 lb
2795 lb
0 lb
0 lb

3869 lb

Structure Notes:
-KYTC STATE PROJECT 251007
-REINFORCING: #5 BAR @ 12" C/C E.W. (TYP.)
-CS-102 BUTYL REQUIRED (SUPPLIED BY ICAST).
-KYTC CERTIFICATIONS REQUIRED.

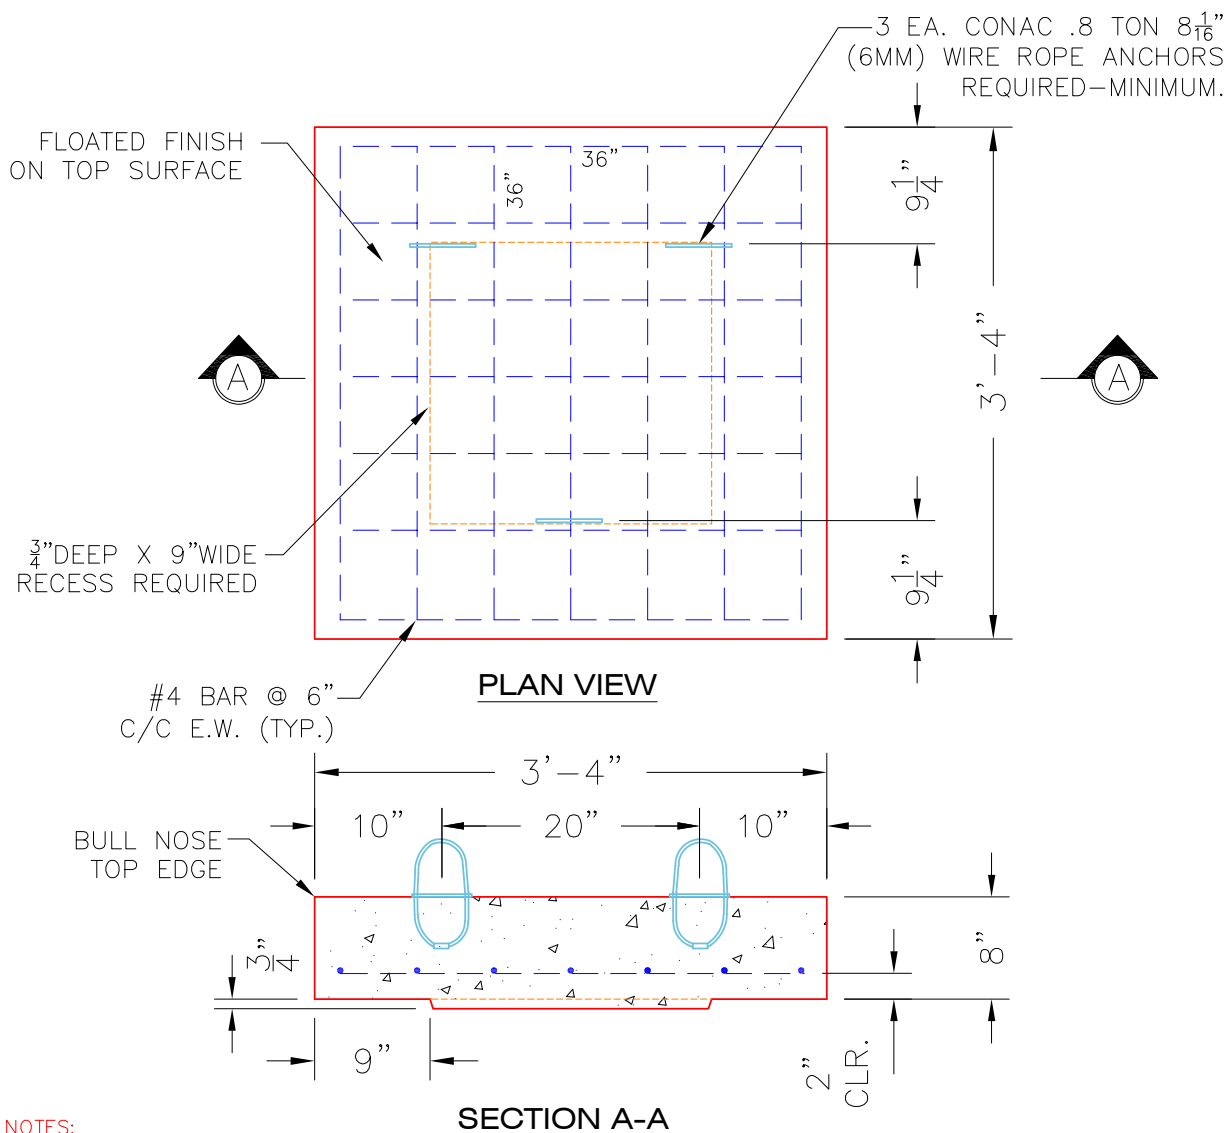

NOTES:

- CONCRETE: 4500 PSI @ 28 DAYS.
- MANUFACTURE TO KYTC SPECIFICATIONS.
- REINFORCING: #4 BAR @ 6" C/C E.W.-GRADE 60.
(BOTTOM LAYER ONLY)
- 3 EA. CONAC WIRE LOOP LIFTERS REQUIRED.
- KYTC CERTIFICATIONS REQUIRED.

[#4 BAR CUT LIST](#)
14 EA. @ 36"

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 1074 lb
Volume (Net): 0.27cu.yd
