

Contractor: Core & Main LP


Plant: 100



Floor (Bot): -0.5'
Overall Height: 6'
Slack: 0"

P3) 24" - CASTING HEIGHT - 4"	0 lb
P2) 60" x 120" - CB FLAT TOP 6"W w/(2) 24" HOLES (Grease Trap) F/F - 8"	6076 lb
P1) 60" x 120" - BOX BASE 6inW, 6inF F/n - 54"	15174 lb
1) 60" x 52" - BAFFLE WALL (GT-1000 GAL.) - 4"	1035 lb
2) CASTING - JBS 1072 F/C GREASE	500 lb
1) 60" x 120" - Conseal CS-102 1.00" (Double)	0 lb
2) PSX - 8QRS-S NYLO	13 lb

Structure Total:	22799 lb

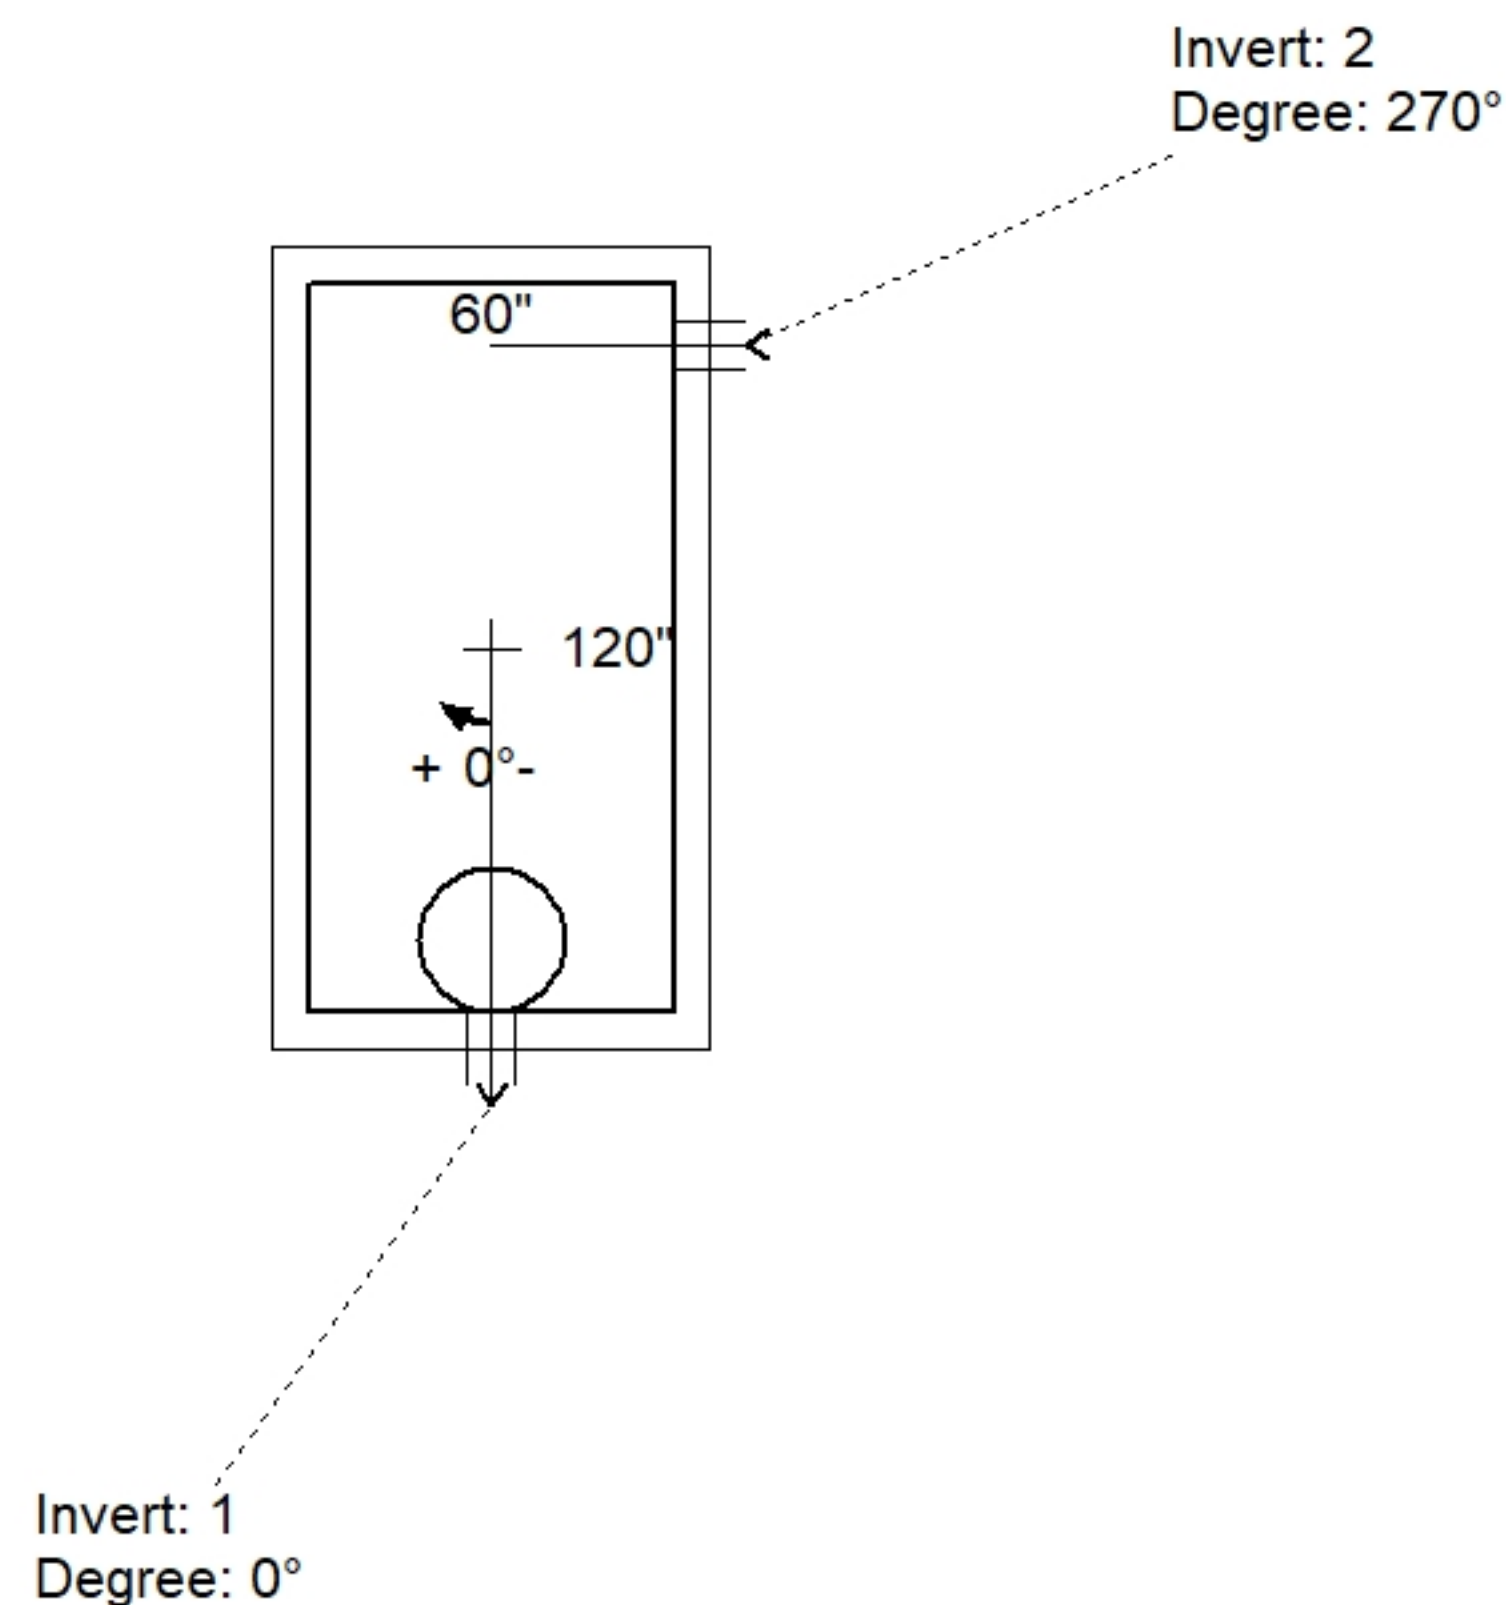


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	5.5'							
Reducer								
Invert 1	2.833'	0°	4" PVC SDR35	4.25"	8"	PSX 8QRS-S NYLO	31.996"	P1
Invert 2	3.083'	270°	4" PVC SDR35	4.25"	8"	PSX 8QRS-S NYLO	34.996"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" - CASTING HEIGHT - 4" - (P3)

60" x 120" - CB FLAT TOP 6"W w/(2) 24" HOLES (Grease Trap) F/F - 8" - (P2)

60" x 120" - BOX BASE 6inW, 6inF F/n - 54" - (P1)

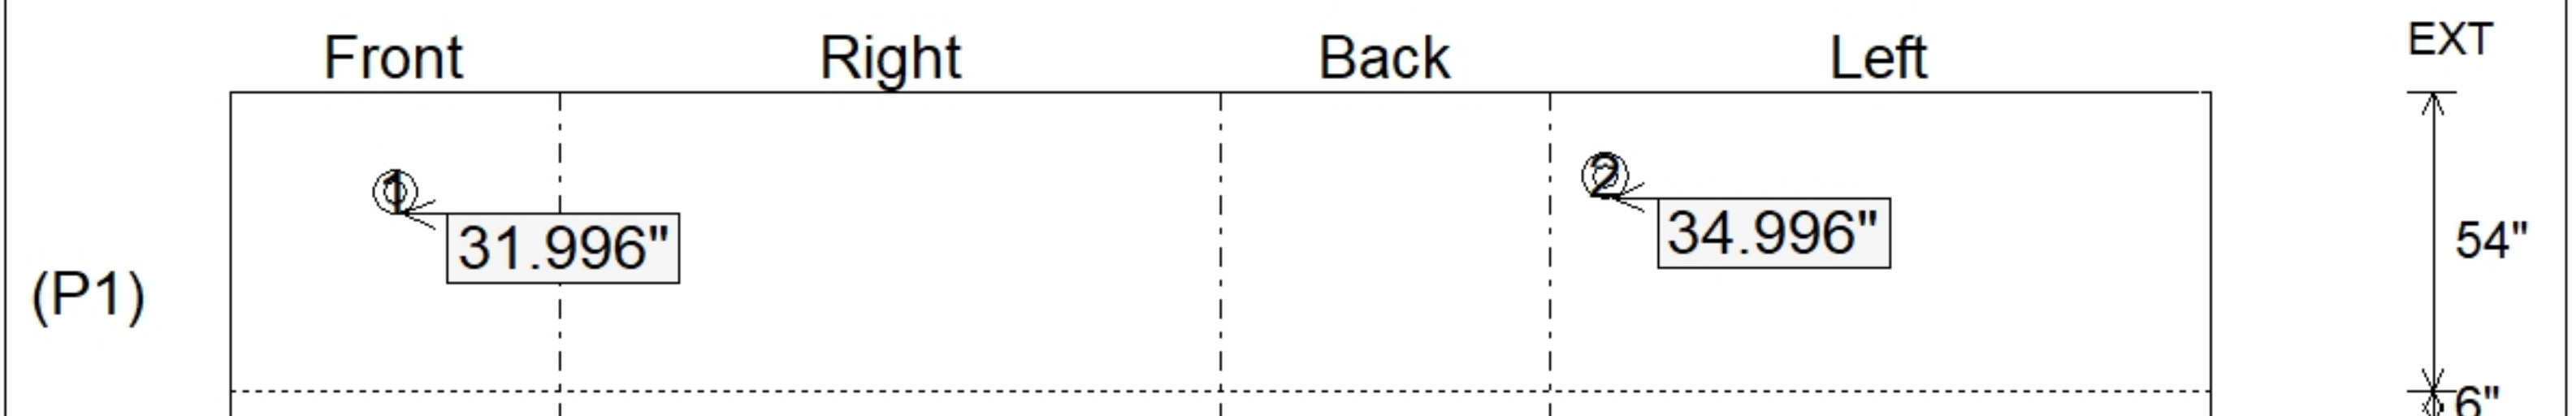

SUBMITTAL
APPROVED BY:
