






Job Name: 25-2073 - Alcoa Outfall
Job Location: Newburgh, IN
Contractor: Bowen Engineering Corporation

PC: A. Chambers
TECH: J. Horsley
Plant: 100





Structure ID: **BC 4 x 2 (PC 4)**
Spec: Box Culvert
Type: Box Culvert (08W/08F/08T) No Haunch
Size: 48" x 24"

Rim: 5.75'
Invert: 5.75'
Rim to Invert: 0'
Sump: 0"
Floor (Top): 0"
Floor Height: 0"
Floor (Bot): 0"
Overall Height: 5.75'
Slack: 0"

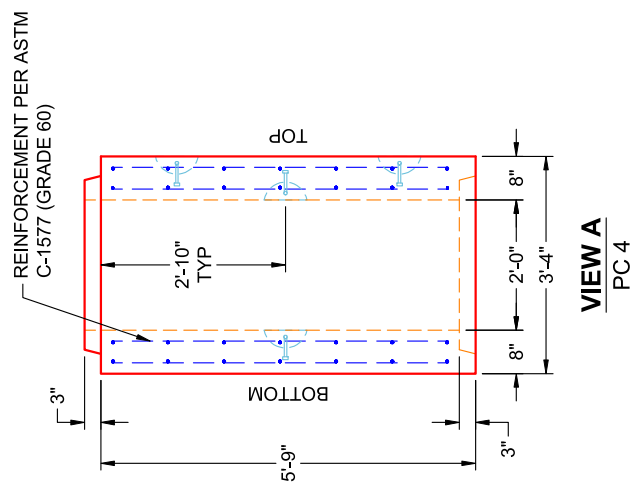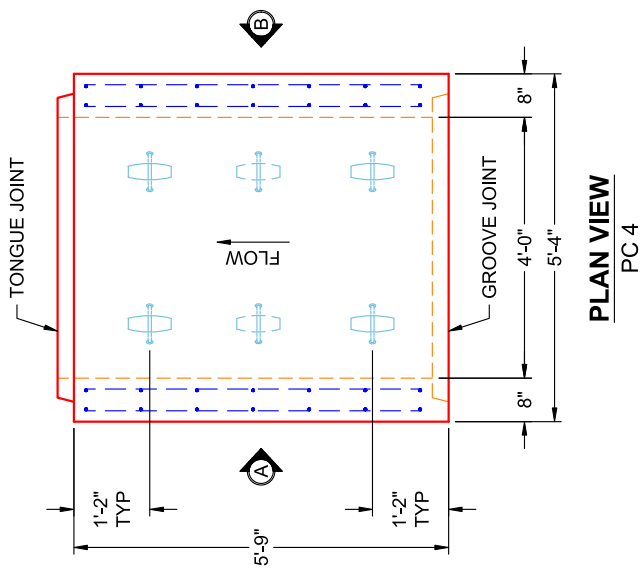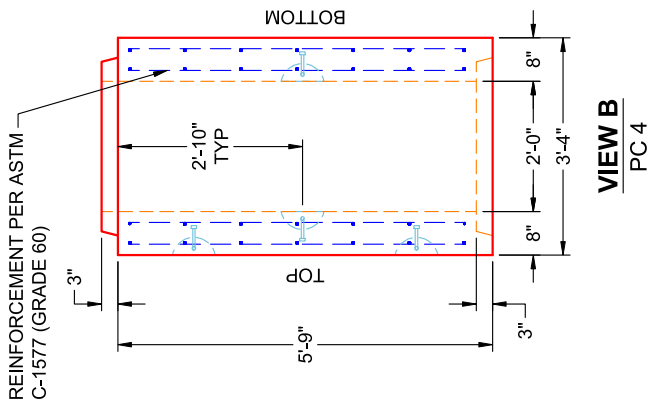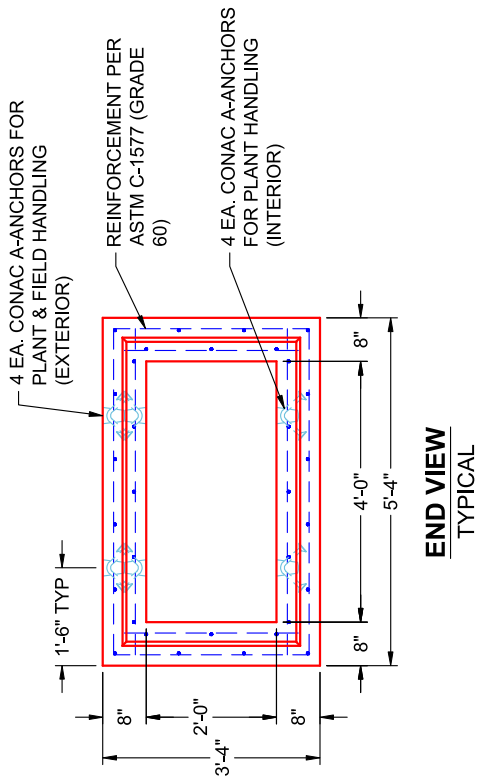

- GENERAL NOTES:**
- MANUFACTURED TO ASTM C-1577 & SECTION 714 OF INDOT STANDARD SPECIFICATIONS FOR REINFORCED CONCRETE BOX STRUCTURES
 - LOAD REQUIREMENTS: HL93
 - REINFORCEMENT PER ASTM C-1577 (GRADE 60)
 - COVER DEPTH: 4'-8"
 - CONCRETE: 5,000 PSI AT 28 DAYS
 - JOINT SEALANT: 1" BUTYL MASTIC (CS-102) EXTERIOR JOINT WRAP: 12" WIDE (CS-212)
 - WEIGHT: 4' X 2' RCBC = 1,418 LBS / LF (5'-9" LONG SECTION = 8,152 LBS)



- NOTES:

SUBMITTAL DRAWING: 4 X 2 ROBC LAYING PLAN
CUSTOMER: BOWEN ENGINEERING CORPORATION
PROJECT: ALCOA OUTFALL
STRUCTURE I.D.: BC 4 X 2
QUOTE/ORDER NO: 25-2073
CHECK: B. SMITH
DRAWN BY: J. HORSLEY
DATE: 01/09/26
SCALE: NTS
PG. 1 of 1

THIS DRAWING IS THE PROPERTY OF INFRASTRUCTURE PRECAST, INC. ANY USE OR DUPLICATION OF THIS DRAWING WITHOUT PRIOR AUTHORIZATION IS STRICTLY PROHIBITED.
