

Job Name: 25-2284C Parks at Cane Ridge Ph.2B
Job Location: Antioch, TN
Contractor: Josh King Excavating

Plant: Beaver Dam

7/21/2026 8:50:11 AM

Tech: S. Felletter

PC: A. Chambers



Structure ID: QL17

P3 GR28x28x6x3

GRADE RING 6"W F/F

P5) 28" x 28" - GRADE RING 6"W F/F - 3"
P4) 28" x 28" - GRADE RING 6"W F/F - 3"
P3) 28" x 28" - GRADE RING 6"W F/F - 3"
P2) 28" x 28" - GRADE RING 6"W F/F - 3"
P1) 28" x 28" - GRADE RING 6"W F/F - 3"

205 lb
205 lb
205 lb
205 lb
205 lb
205 lb

Structure Total: 1027 lb


Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE = 4,000 PSI @ 28 DAYS.
3. REINFORCING: #4 BAR AS SHOWN (GRADE 60 KSI).
4. LIFTS: 2 EA. CONAC .8 TON WIRE ROPE ANCHORS REQUIRED.

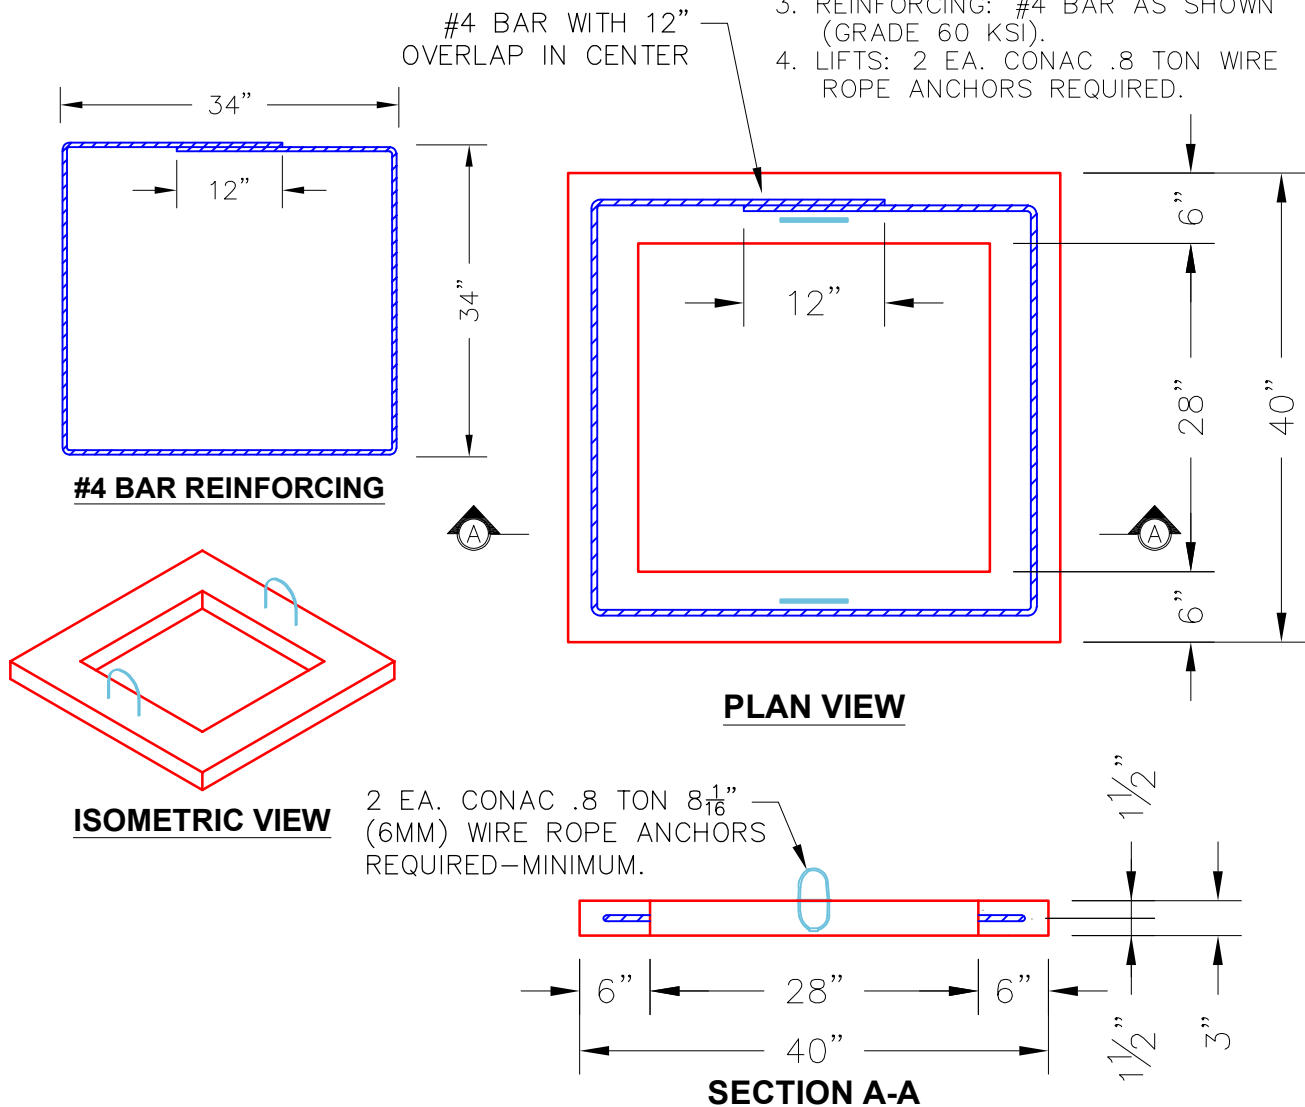

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 3"

Weight (Net): 205 lb
Volume (Net): 0.05cu.yd
