

Job Name: 25-2284C Parks at Cane Ridge Ph.2B
Job Location: Antioch, TN
Contractor: Josh King Excavating

Plant: Beaver Dam

Tech: S. Felletter

7/21/2026 8:50:13 AM

PC: A. Chambers



Structure ID: QL18

P5 GR28X28X6X4

GRADE RING 6"W F/F

P18) 28" x 28" - GRADE RING 6"W F/F - 4"
P17) 28" x 28" - GRADE RING 6"W F/F - 4"
P16) 28" x 28" - GRADE RING 6"W F/F - 4"
P15) 28" x 28" - GRADE RING 6"W F/F - 4"
P14) 28" x 28" - GRADE RING 6"W F/F - 4"
P13) 28" x 28" - GRADE RING 6"W F/F - 4"
P12) 28" x 28" - GRADE RING 6"W F/F - 4"
P11) 28" x 28" - GRADE RING 6"W F/F - 4"
P10) 28" x 28" - GRADE RING 6"W F/F - 4"
P9) 28" x 28" - GRADE RING 6"W F/F - 4"
P8) 28" x 28" - GRADE RING 6"W F/F - 4"
P7) 28" x 28" - GRADE RING 6"W F/F - 4"
P6) 28" x 28" - GRADE RING 6"W F/F - 4"
P5) 28" x 28" - GRADE RING 6"W F/F - 4"
P4) 28" x 28" - GRADE RING 6"W F/F - 4"
P3) 28" x 28" - GRADE RING 6"W F/F - 4"
P2) 28" x 28" - GRADE RING 6"W F/F - 4"
P1) 28" x 28" - GRADE RING 6"W F/F - 4"

274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb
274 lb

Structure Notes:


1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 4930 lb

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE = 4,000 PSI @ 28 DAYS.
3. REINFORCING: #4 BAR AS SHOWN (GRADE 60 KSI).
4. LIFTS: 2 EA. CONAC .8 TON WIRE ROPE ANCHORS REQUIRED.

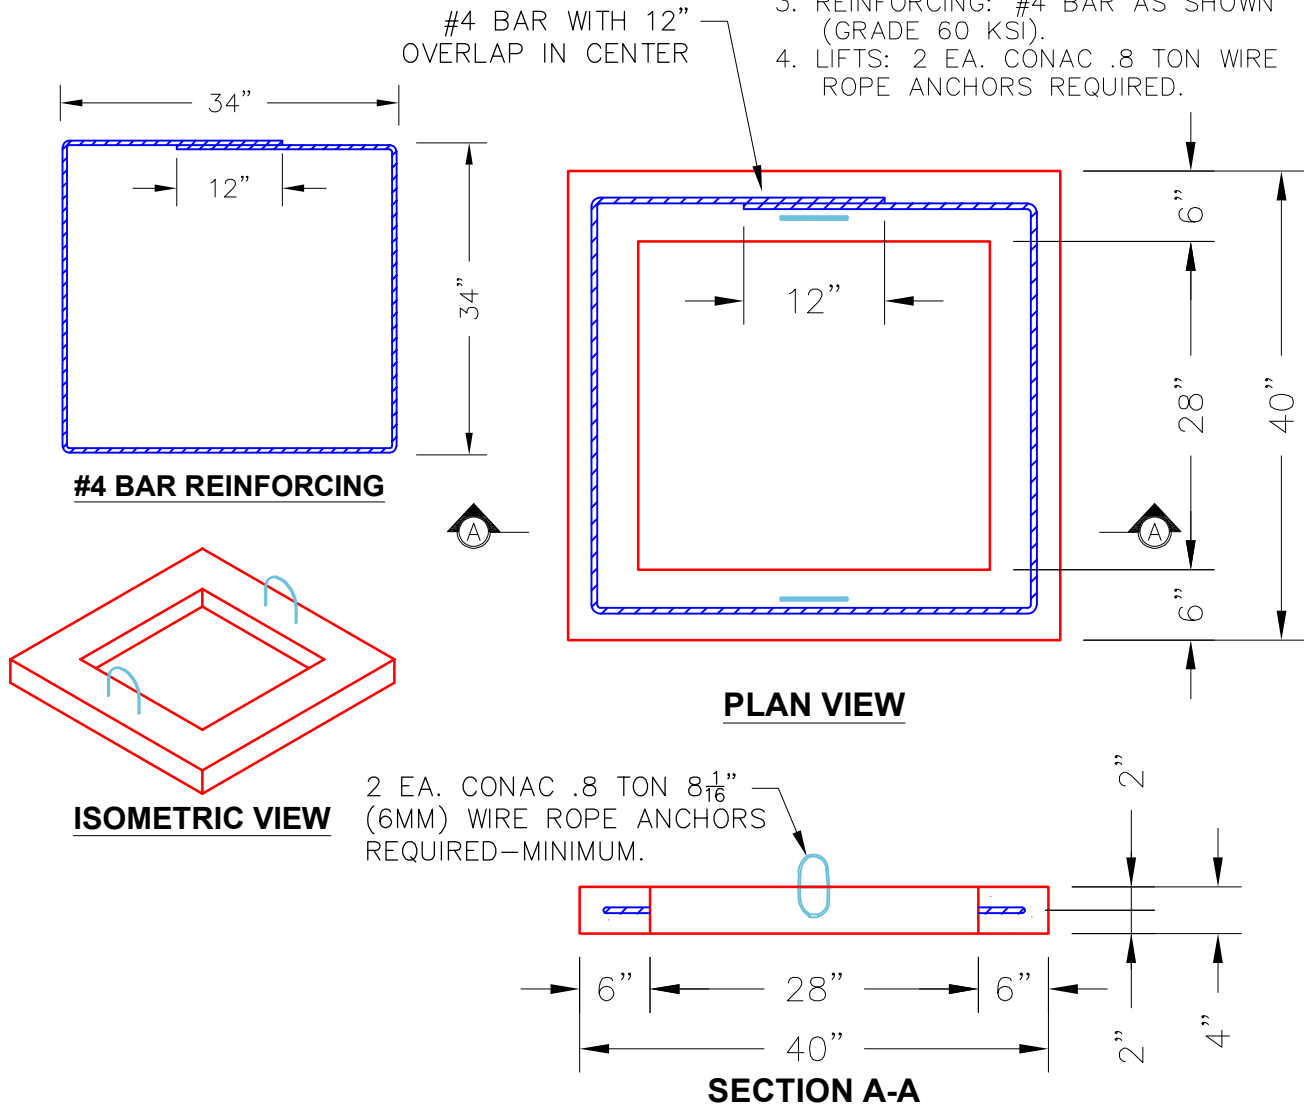

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 6"

Height (Ext): 4"

Weight (Net): 274 lb
Volume (Net): 0.07cu.yd
